

COMP7039 – Agile Processes

Final Project
evSD_Group1

Contents

Project Introduction.....	6
🧐 Problem statement	6
Project goal	6
🔍 Scope	7
🚩 Milestones and deadlines	7
Health report tool stakeholders	8
Our stakeholders.....	8
Open actions	8
Health report tool Risk assessment	8
📄 Background	8
🧑‍🚀 Risks management	9
Risk rating.....	9
✅ Action items	9
3. Sprint planning /Backlog	30
✅ Sprint planning checklist	33
👤 Sprint team members	34
📝 Sprint planning meeting items.....	34
Agenda	34
Create Sprint 1	34
Details	35
Capacity planning.....	35
Potential risks.....	35
4. Git workflow.....	36
5. Sprint review	37
Sprint 1 daily scrum meetings.....	37
📅 Week1	37
📅 Week2	38
📅 Week3	38
📅 Week4	39
📅 Week5	39
Sprint1 review report.....	40

Sprint Summary	40
Sprint Detail	40
Completed.....	40
Added.....	41
Removed	41
Impediments & Risks.....	41
6. Retrospective	45
📋 Overview	45
💡 Retrospective	46
Report Sprint 2	47
Sprint 2 Product backlog	47
User stories and subtask	49
Sprint planning /Backlog	63
Sprint 2 planning report.....	64
✅ Sprint planning checklist	65
👤 Sprint team members	65
📝 Sprint planning meeting items.....	66
Agenda	66
Previous sprint summary	66
Details	66
Capacity planning.....	66
Potential risks.....	67
Git worklow	67
Sprint review	87
📅 Week1 <03/11/2025>	87
📅 Week 2 <10/11/2025>	87
📅 Wednesday <12/11/25>	88
Sprint 2	91
Sprint Summary	91
Sprint2 Detail	91
Completed.....	91
Added.....	92
Removed	92

Impediments & Risks	93
📋 Overview	94
💡 Retrospective	94
✅ Action items	94
Sprint 3	96
Product backlog	96
Sprint 3 planning	106
Sprint 3 Planning report.....	108
✅ Sprint planning checklist	108
👤 Sprint team members	109
📌 Sprint planning meeting items.....	109
Agenda	109
Previous sprint summary	109
Details	109
Capacity planning.....	110
Potential risks.....	110
📁 Sprint planning resources	110
Team resources and definitions:	110
Sprint 3 review	111
Sprint 3 Daily/weekly report.....	111
📅 Monday <17/11/2025>	111
📅 Sunday <23/11/2025>.....	111
📅 Wednesday <03/12/2025>	112
Sprint 3	112
Sprint Summary	112
Sprint3 Detail	113
Completed.....	113
Added	113
Impediments & Risks	114
Sprint 3 retrospective review.....	119
📋 Overview	119
💡 Retrospective	119

✓ Action items	120
DevOps	121
Conclusions and future work	132
Problem Statement Summary	132
Project Management Approach.....	132
Technical Approach.....	132
Overview of Objectives	132
DataBase	133
Web Interface	133
Data visualization	135
Data Prediction	136
Documentation	139
Findings of Approach	139
Tool chain.....	140
Future Enhancements.....	140

Project Introduction

Driver	evSD_Group1
Approver	Jing-Hua Ye
Contributors	Edita Buneviciene, Dariusz Olczak, Patrick Strand, Edward Tracey
Informed	Jing-Hua Ye
Objective	To analyze the Global Health, Mortality, and Disease Trends dataset (2000–present) using Agile and Scrum practices, by building a system that imports and cleans data, visualizes health patterns, and extracts intelligent insights through anomaly detection and LLM integration
Due date	02 Nov 2025
Key outcomes	Data Import. Importing and parsing data. Pre-processing of information to identify empty/null/incorrect values. Data Presentation and Visualisation. Display, raw and/or processed data in tables and/or charts. Knowledge extraction. Applying machine learning techniques or communicating with LLM to produce intelligent results.
Status	NOT STARTED / IN PROGRESS / COMPLETE

Problem statement

We think transforming raw global health data into visual dashboards and intelligent insights will make patterns and anomalies easier to understand, and we'll know we've succeeded if users can interact with the data and get clear answers to their questions.

Project goal

For students and educators who want to have insight into global health, access to basic services, life expectancy, disease and treatment, mortality patterns across last 25 years, the <Health Report Tool> is a data analysis and visualization tool that imports, cleans, and visualizes health data while also providing intelligent insights through anomaly detection and natural language queries. Unlike excel spreadsheets or other reports, our <Health Report Tool> makes the data easy to access, extract and visualize.

Scope

Must have:	Import and preprocess dataset (handle missing/incorrect values). Store data in a structured database. Interactive tables with filtering/sorting.
Nice to have:	Additional visualizations in form of charts. Result export in PDF or other format
Not in scope:	

Milestones and deadlines

Milestone	Owner	Deadline	Status
Sprint 1	Dariusz	02 Nov 2025	Completed
Sprint 2	Edita	16/11/2025	Completed
Sprint 3	Edward	06/12/2025	Completed

Health report tool stakeholders

Comms plan goals: the project aims to deliver to develop interactive data visualization showing disease and mortality trends between 2000-2024 using Kaggle dataset.

Our stakeholders

Audience/Stakeholder	Role
Jing	Approve the ongoing work.
IT team	System management
Students	Retrieve and compared areas of interest in their research
Primary care clinics	Plan work ahead.
Specialist	Use trend analysis for future work planning.

Open actions

- After consulting the stakeholder, got some changes to do relating cleaning dataset. Visual implementation was satisfied.

Health report tool Risk assessment

Background

While working on this project, we encountered few risks that would effect planning and delivery. First understanding properly the scope of the project, what tools to use, are we able to deliver the tasks on time. Upfront planning could bring unexpected issues as uncertainty at a time to to complete task.

Additional risks were identified as requirement change, related to data. Our first dataset set wasn't meeting criteria, we had to research for more suitable dataset. Time management was a big issue for every team members trying to deal with academical workload. But by having a clear workload breakdown structure helped to track the progress and complete the tasks. Team communication was one of the risk factors too as people were available different day and different times. But keeping WhatsApp communication between team members kept everyone on track.

Risks management

Identify and prioritize risks based on their probability and severity. Then define what further actions you need to take to control the risks, and who needs to carry out these actions.

Risk rating

LOW	MEDIUM	HIGH	EXTREME
● Acceptable ● Ok to proceed	● As low as reasonably practicable ● Take mitigation efforts	● Generally unacceptable ● Seek support	● Intolerable ● Place event on hold

LIKELIHOOD	SEVERITY			
	ACCEPTABLE <i>Little to no effect on event</i>	TOLERABLE <i>Effects are felt, but not critical to outcome</i>	UNDESIRABLE <i>Serious impact to the course of action and outcome</i>	INTOLERABLE <i>Could result in disaster</i>
IMPROBABLE <i>Risk is unlikely to occur</i>	Slow performance	Integration between main code and HTML failure.	Predictions are not correct	Data loss or deletion
POSSIBLE <i>Risk will likely occur</i>	Team member sick	Team member not collaborating	Incorrect predictions Incorrect Git use	Data import fails
PROBABLE <i>Risk will occur</i>	Underestimation of task difficulty, duration	Learning new tools	Miscommunication between team members	Data quality issues

Action items

- Validate data inputs.

- Maintain backup of work
- Track time spent on workload.

Product backlog

Type	Key	Summary	Assignee	Priority	Status	Updated
	E1-119	Plan refresh frequency	Patrick Strand	Medium	TO DO	Oct 28, 2025, 03:04
	E1-94	Create Visual Summaries	Patrick Strand	Medium	TO DO	Oct 30, 2025, 21:37
	E1-93	Group Totals and Rates	Patrick Strand	Medium	TO DO	Oct 30, 2025, 21:37
	E1-92	Add Demographic Fields	Patrick Strand	Medium	TO DO	Oct 30, 2025, 21:37
	E1-88	Review and Test the Results	Patrick Strand	Medium	TO DO	Oct 30, 2025, 21:37
	E1-87	Display Filtered Results	Patrick Strand	Medium	TO DO	Oct 30, 2025, 21:37
	E1-86	add "year"	Patrick Strand	Medium	TO DO	Oct 30, 2025, 21:37
	E1-82	Redirection to Forgot/reset password page	Dariusz Olczak	Medium	DONE	Oct 28, 2025, 12:10
	E1-81	Prompt displaying best safety practices while entering password	Dariusz Olczak	Medium	DONE	Oct 28, 2025, 12:10
	E1-80	User input validation	Dariusz Olczak	Medium	DONE	Oct 28, 2025, 12:10
	E1-79	Incorrect password entered	Dariusz Olczak	Medium	DONE	Oct 28, 2025, 12:11
	E1-75	Add sign in and new user options	Patrick Strand	Medium	DONE	Oct 28, 2025, 12:46
	E1-73	Redirect users to registration page after sign in attempt	Patrick Strand	Medium	DONE	Oct 28, 2025, 12:46
	E1-72	Implement sign in button placement	Patrick Strand	Medium	DONE	Oct 28, 2025, 12:46
	E1-71	Double check and record the process	Patrick Strand	Medium	TO DO	Oct 30, 2025, 21:40
	E1-70	Align and adjust the data	Patrick Strand	Medium	TO DO	Oct 30, 2025, 21:40
	E1-69	Review Incoming Data	Patrick Strand	Medium	TO DO	Oct 30, 2025, 21:40
	E1-66	Validate uploaded CSV file format and content	Patrick Strand	Medium	DONE	Oct 28, 2025, 12:46
	E1-65	Implement backend endpoint for manual CSV upload	Patrick Strand	Medium	DONE	Oct 28, 2025, 12:46
	E1-62	Write the script to handle missing values.	Edita Buneviciene	Medium	DONE	Oct 30, 2025, 21:54
	E1-61	Analyze dataset for missing values	Edita Buneviciene	Medium	DONE	Oct 30, 2025, 21:54
	E1-59	Add functionality to update password and email	Ed Tracey	Medium	DONE	Oct 30, 2025, 21:52
	E1-58	Display confirmation message after profile update	Ed Tracey	Medium	DONE	Oct 30, 2025, 21:52
	E1-57	Implement form to display and edit user details	Ed Tracey	Medium	DONE	Oct 30, 2025, 21:52

	E1-55	Integrate email service to send password reset link		Ed Tracey	Medium	DONE	Oct 30, 2025, 21:51
	E1-53	Implement 'Forgot Password' button functionality		Ed Tracey	Medium	DONE	Oct 27, 2025, 21:30
	E1-52	Design 'Forgot Password' user interface		Ed Tracey	Medium	DONE	Oct 27, 2025, 21:30
	E1-51	Handle successful login redirection		Dariusz Olczak	Medium	DONE	Oct 30, 2025, 21:42
	E1-50	Handle non-existent user redirection		Dariusz Olczak	Medium	DONE	Oct 30, 2025, 21:42
	E1-49	Design login user interface		Dariusz Olczak	Medium	DONE	Oct 30, 2025, 21:42
	E1-48	Create Success and Error Messaging		Ed Tracey	Medium	DONE	Oct 27, 2025, 21:29
	E1-47	Handle Duplicate Email Registration		Ed Tracey	Medium	DONE	Oct 30, 2025, 21:54
	E1-46	Implement Sign Up Form Validation		Ed Tracey	Medium	DONE	Oct 27, 2025, 21:28
	E1-45	Design Sign Up Page		Ed Tracey	Medium	DONE	Oct 27, 2025, 21:28
	E1-42	scheduled data refreshes to ensure reports are accurate(scrum)		Patrick Strand	Medium	TO DO	Oct 30, 2025, 21:35
	E1-41	collaborator - share reports so that teams can discuss globe health		Ed Tracey	Medium	TO DO	Oct 30, 2025, 21:35
	E1-39	user: report builder can generate summaries		Dariusz Olczak	Medium	TO DO	Oct 30, 2025, 21:36
	E1-37	integrate tools with data eg link to original data set		Edita Buneviciene	Medium	TO DO	Oct 30, 2025, 21:36
	E1-36	exporter- able to download charts to confluence		Ed Tracey	Medium	TO DO	Oct 30, 2025, 21:36
	E1-35	visualizations to responsive for phones		Patrick Strand	Medium	TO DO	Oct 30, 2025, 21:36
	E1-32	Demographic breakdown by age and gender		Patrick Strand	Medium	TO DO	Oct 30, 2025, 21:36
	E1-31	year - on year percentage change in rates		Patrick Strand	Medium	TO DO	Oct 30, 2025, 21:36
	E1-30	user - comparative charts		Patrick Strand	Medium	TO DO	Oct 30, 2025, 21:36
	E1-29	an analyst - filter mortality trends by year		Edita Buneviciene	Medium	TO DO	Oct 30, 2025, 21:36
	E1-28	Manual upload data option		Patrick Strand	Medium	DONE	Oct 28, 2025, 12:46
	E1-27	Standardize units		Patrick Strand	Medium	TO DO	Oct 30, 2025, 21:36
	E1-26	Clean dataset		Edita Buneviciene	Medium	DONE	Oct 28, 2025, 22:45
	E1-19	set bitBucket / github		Patrick Strand	Medium	TO DO	Oct 30, 2025, 21:36
	E1-15	Registration		Ed Tracey	Medium	DONE	Oct 27, 2025, 21:30
	E1-13	Import dataset		Edita Buneviciene	Medium	DONE	Oct 30, 2025, 21:53
	E1-12	Analyse dataset		Edita Buneviciene	Medium	DONE	Oct 30, 2025, 21:52
	E1-10	Edit profile		Ed Tracey	Medium	DONE	Oct 28, 2025, 21:37
	E1-9	Forgot/Reset password		Ed Tracey	Medium	DONE	Oct 27, 2025, 21:31
	E1-8	Login to account		Dariusz Olczak	Medium	DONE	Oct 28, 2025, 12:12
	E1-7	Initial signup page		Patrick Strand	Medium	DONE	Oct 28, 2025, 12:46

Sprint 1 epics and user stories:

Signup page-Initial signup page, Registration, Incorrect password entered.
 Importing dataset-Importing data,Clean dataset, Manual upload data option.
 Account management-Login to account, Forget/Reset password,Edit profile.

Screenshots of each user story including description, acceptance criteria and story points, followed by subtask and descriptions:

The screenshot displays a Jira user story titled "Importing Data". The story is in a "Done" state, indicated by a green checkmark and the word "Done". The story ID is E1-11 / E1-1.

Description: As a user, I want to import dataset so that I can do some data analytics.

Acceptance criteria:

1. It should contain 20000 -50000 records.
2. It should have 15-20 columns.

Subtasks: A progress bar shows 100% Done. The subtasks are:

Work	Priority	Assignee	Status
E1-12 Analyse dataset	Me...	Edita ...	DONE
E1-13 Import dataset	Me...	Edita ...	DONE

Linked work items: Add linked work item

Activity: All Comments History Work Item

Details Panel:

- Done:** Done, Done, Improve Task
- Details:**
 - Assignee:** Edita Buneviciene
 - Labels:** Add labels
 - Parent:** E1-11 Import dataset
 - Due date:** Add due date
 - Team:** Add team
 - Start date:** Add date
 - Sprint:** Add sprint +1
 - Story point estimate:** 4
 - Fix versions:** None
 - Development:** Development
 - Reporter:** Dariusz Olczak

Dependencies: Need to have internet access to be able to proceed.

Risk: Dataset may not meet the criterias.

E1-1 / E1-13

Import dataset

+ @

Description
Using [Kaggle.com](#) import dataset.

Linked work items
Add linked work item

Activity
All Comments History Work log

Add a comment...

Status update... Thanks... Agree...

Pro tip: press **M** to comment

Done Done Improve Subtask

Details

Assignee Edita Buneviciene

Labels Add labels

Parent E1-1 Importing Data

Due date Add due date

Start date Add date

Fix versions None

Sprint Add sprint +1

Story point estimate 1

DoD: Dataset is imported and criterias are met.
Time estimated: 1.5 hour

E1-1 / E1-12

Analyse dataset

+ @

Description
Analyze data using `DataFrame corr()` function.

Linked work items
Add linked work item

Activity
All Comments History Work log

Add a comment...

Status update... Thanks... Agree...

Done Done Improve Subtask

Details

Assignee Edita Buneviciene

Labels Add labels

Parent E1-1 Importing Data

Due date Add due date

Start date Add date

Fix versions None

Sprint Add sprint +1

Story point estimate 3

DoD: Team member reviewed and standard are met.
Tim estimated: 4 hours

🔗 E1-6 / 📌 E1-7

Initial signup page

+ 📎

▼ **Description**

As the user, I want learn about the product and sign in my account so that I can securely browse and get access to the app.

Acceptance criteria:

1. The page should contain information about the product (project).
2. The sign in button should be displayed in the right top .
3. It gives sign in or new user options.
4. When signing in, it forwards you to login/ registration page.

▼ **Subtasks** 100% Done

Work	Priority	Assignee	Status
🔗 E1-72 Implement sign in button placement	Me...	PS Patric...	DONE
🔗 E1-73 Redirect users to registration page after sign in attempt	Me...	PS Patric...	DONE
🔗 E1-75 Add sign in and new user options	Me...	PS Patric...	DONE

Linked work items

Add linked work item

Activity

All Comments History **Work log**

Done ▾ ✓ Done ⚡ ⚙ Improve Task

▼ **Details** ⚙

Assignee PS Patrick Strand
[Assign to me](#)

Labels Add labels

Parent 🔗 E1-6 Signup page

Due date Add due date

Team Add team

Start date Oct 01, 2025

Sprint Add sprint +1

Story point estimate 4

Fix versions None

Development ▾

Reporter 19 Edita Buneviciene

> **Automation** ⚡ Rule executions

> **Planning Poker** 🎲 Open Planning Poker

Created October 6, 2025 at 2:00 PM
Updated last month ⚙ Configure

Dependencies: HTML have to be available and working to be able to sign in.

Risk: HTML is not loading.

📌 E1-7 / 🔗 E1-72

Implement sign in button placement

+ 📎

Description

Develop and position the sign in button at the top right corner of the signup page, ensuring it is easily visible and accessible to users.

Linked work items

Add linked work item

Activity

All **Comments** History Work log

19 Add a comment...

Status update... Thanks... Agree...

Done ▾ ✓ Done ⚡ ⚙ Improve Subtask

▼ **Details** ⚙

Assignee PS Patrick Strand
[Assign to me](#)

Labels Add labels

Parent 📌 E1-7 Initial signup page

Due date Add due date

Start date Add date

Fix versions None

Sprint Add sprint +1

Story point estimate 3

DoD: "Sign In" button is displayed

Time estimated: 3 hours

E1-7 / E1-73

1

Redirect users to registration page after sign in attempt



Description

When a user attempts to sign in and does not have an account, they are forwarded to the registration page to complete the signup process.

Linked work items

Add linked work item

Activity

All Comments History Work log



Add a comment...

Status update...

Thanks...

Agree...

Pro tip: press **M** to comment

Done

✓ Done



Improve Subtask

Details

Assignee Patrick Strand

[Assign to me](#)

Labels Add labels

Parent ☒ E1-7 Initial signup page

Due date Add due date

Start date Add date

Fix versions None

Sprint Add sprint +1

Story point estimate 3

DoD: Registration page is loaded.

Time estimated: 3 hours.

E1-7 / E1-75

1

Add sign in and new user options



Description

Provide users with options to either sign in to an existing account or proceed as a new user.

Linked work items

Add linked work item

Activity

All Comments History Work log



Add a comment...

Status update...

Thanks...

Agree...

Pro tip: press **M** to comment

Done

✓ Done



Improve Subtask

Details

Assignee Patrick Strand

[Assign to me](#)

Labels Add labels

Parent ☒ E1-7 Initial signup page

Due date Add due date

Start date Oct 01, 2025

Fix versions None

Sprint Add sprint +1

Story point estimate 4

Development

DoD: team members reviewed and options for user are provided.

Time estimated: 5 hours

E1-5 / E1-8

Login to account

+ @

✓ **Description**
As the user, I want securely login in my account.

Acceptance criteria:

1. If account exists, it forwards you to next page in 3 sec max.
2. If user do not exist, it forwards you to sig up/ registration page.

✓ **Subtasks** 100% Done

Work	Priority	Assignee	Status
E1-4B Design login user interface	Me...	Dariusz...	DONE
E1-5B Handle non-existent user redirection	Me...	Dariusz...	DONE
E1-6B Handle successful login redirection	Me...	Dariusz...	DONE

Linked work items
Add linked work item

Confluence content

Details panel:

- Assignee: Dariusz Olczak
- Labels: Add labels
- Parent: E1-5 Account Management
- Due date: Add due date
- Team: Add team
- Start date: Add date
- Sprint: Add sprint +1
- Story point estimate: 4
- Fix versions: None
- Development
- Reporter: Edita Buneviciene

Dependencies: the user has login credentials.

Risk: for an exist user login page is not loading.

E1-8 / E1-4B

Design login user interface

+ @

✓ **Description**
Create the frontend login form, including fields for username/email and password, and ensure it meets usability and accessibility standards.

Linked work items
Add linked work item

Activity
All Comments History Work log

Add a comment...

Details panel:

- Assignee: Dariusz Olczak
- Labels: Add labels
- Parent: E1-8 Login to account
- Due date: Add due date
- Start date: Add date
- Fix versions: None
- Sprint: Add sprint +1

DoD: interface contains required fields.

Time estimated: 1.5 hour

E1-8 / E1-50

Handle non-existent user redirection

+ @

Description
Develop logic to detect when a user does not exist and redirect them to the signup/registration page.

Linked work items
Add linked work item

Activity
All Comments History Work log

18 Add a comment...

Status update... Thanks... Agree...

Pro tip: press **M** to comment

Done Done ⚡ Improve Subtask

Details

Assignee  Dariusz Olczak
[Assign to me](#)

Labels Add labels

Parent ☒ E1-8 Login to account

Due date Add due date

Start date Add date

Fix versions None

Sprint Add sprint +1

Story point estimate 2

DoD: the user is redirected to registration page.
Time estimated: 3 hours.

E1-8 / E1-51

Handle successful login redirection

+ @

✓ **Description**
Implement logic to redirect authenticated users to the next page within 3 seconds after successful login.

Linked work items
Add linked work item

Activity
All Comments History Work log

19 Add a comment...

Status update... Thanks... Agree...

Pro tip: press **M** to comment

Done Done ⚡ Improve Subtask

Details

Assignee  Dariusz Olczak
[Assign to me](#)

Labels Add labels

Parent ☒ E1-8 Login to account

Due date Add due date

Start date Add date

Fix versions None

Sprint Add sprint +1

Story point estimate 3

DoD: team members reviewed and criteria is met.
Time estimated: 2 hours.

E1-5 / E1-9

Forgot/Reset password

+ @

Description

As the user, I want to have an option to resend password or reset password if forgotten to be able to login in the app.

Acceptance criteria:

1. When "Forgot password" button is clicked, it displays "Reset a password"
2. The user receives a link to reset a password within 5 sec.

Subtasks

100% Done

Work	Priority	Assignee	Status
E1-52 Design 'Forgot Password' user interface	Me...	Ed Tra...	DONE
E1-53 Implement 'Forgot Password' button functionality	Me...	Ed Tra...	DONE
E1-55 Integrate email service to send password reset link	Me...	Ed Tra...	DONE

Linked work items

Add linked work item

Details

Assignee: Ed Tracey
[Assign to me](#)

Labels: Add labels

Parent: E1-5 Account Management

Due date: Add due date

Team: Add team

Start date: Add date

Sprint: Add sprint +1

Story point estimate: 3

Fix versions: None

Development

Reporter: Edita Buneviciene

Dependencies: an existing email required.

Risk: resent link not working.

E1-9 / E1-52

Design 'Forgot Password' user interface

+ @

Description

Create the UI for the 'Forgot password' feature, including the button and the 'Reset a password' screen, ensuring it aligns with the app's design guidelines.

Linked work items

Add linked work item

Activity

All Comments History Work log

Add a comment...

Status update... Thanks... Agree...

Details

Assignee: Ed Tracey
[Assign to me](#)

Labels: Add labels

Parent: E1-9 Forgot/Reset password

Due date: Add due date

Start date: Add date

Fix versions: None

Sprint: Add sprint +1

Story point estimate: 2

DoD: The 2 required buttons are created.

Estimated time: 3 hours

E1-9 / E1-53

1 1

Implement 'Forgot Password' button functionality



Description

Develop the logic to handle the 'Forgot password' button click, triggering the display of the 'Reset a password' screen.

Linked work items

Add linked work item

Activity

All Comments History Work log

E1 Add a comment...

Status update... Thanks... Agree...

Pro tip: press **M** to comment

Done Done Improve Subtask

Details

Assignee **E1** Ed Tracey
Assign to me

Labels Add labels

Parent ☒ E1-9 Forgot/Reset password

Due date Add due date

Start date Add date

Fix versions None

Sprint Add sprint +1

Story point estimate 3

Development

Reporter **E1** Edita Buneviciene

DoD: "Reset password" button is displayed.
Estimated time: 4hours.

E1-9 / E1-55

2 1

Integrate email service to send password reset link



Description

Set up and configure the email service to send password reset links to users within 5 seconds of the request.

Linked work items

Add linked work item

Activity

All Comments History Work log

E1 Add a comment...

Suggest a reply... Status update... Thanks...

Pro tip: press **M** to comment

Done Done Improve Subtask

Details

Assignee **E1** Ed Tracey
Assign to me

Labels Add labels

Parent ☒ E1-9 Forgot/Reset password

Due date Add due date

Start date Add date

Fix versions None

Sprint Add sprint +1

Story point estimate 3

DoD: Time limit of 5 sec is accomplished.
Estimated time: 2hours

✦ E1-5 / ☒ E1-10

Edit profile

+

✓ **Description**

As the user I want to be able to edit my profile when my personal details change.

Acceptance criteria:

1. Edit function should return all user details in the form.
2. It gives the options to change the password, email.
3. After the details are edit, confirmation message should be displayed.

✓ **Subtasks** ... +

100% Done

Work	Priority	Assignee	Status
E1-57 Implement form to display and edit user details	Me...	Ed Tra...	DONE
E1-58 Display confirmation message after profile update	Me...	Ed Tra...	DONE
E1-59 Add functionality to update password and email	Me...	Ed Tra...	DONE

Linked work items

Add linked work item

Done Done Improve Task

Details

Assignee Ed Tracey
[Assign to me](#)

Labels Add labels

Parent E1-5 Account Management

Due date Add due date

Team Add team

Start date Add date

Sprint Add sprint +1

Story point estimate 4

Fix versions None

Development

Reporter Edita Buneviciene

Dependencies: user profile needs to be existing.
Risk: no profile found.

Implement form to display and edit user details

+

Description

Create a form that retrieves and displays current user details, allowing the user to edit their information as needed.

Linked work items

Add linked work item

Activity

All **Comments** History Work log

Add a comment...

Status update... Thanks... Agree...

Pro tip: press to comment

Done Done Improve Subtask

Details

Assignee Ed Tracey
[Assign to me](#)

Labels Add labels

Parent ☒ E1-10 Edit profile

Due date Add due date

Start date Add date

Fix versions None

Sprint Add sprint +1

Story point estimate 3

DoD: team member reviewed and criteria is met.
Estimated time: 2 hours.

E1-10 / E1-58

1

Display confirmation message after profile update



Description

Show a confirmation message to the user after their profile details have been successfully updated, indicating the changes have been saved.

Linked work items

Add linked work item

Activity

All Comments History Work log

19 Add a comment...

Status update... Thanks... Agree...

Pro tip: press **M** to comment

Done Done ⚡ Improve Subtask

Details

Assignee **ET** Ed Tracey
[Assign to me](#)

Labels Add labels

Parent ☒ E1-10 Edit profile

Due date Add due date

Start date Add date

Fix versions None

Sprint Add sprint +1

Story point estimate 1

DoD: the requirement is implemented.
 Estimated time: 1hour.

E1-10 / E1-59

1

Add functionality to update password and email



Description

Provide options within the edit profile form for users to change their password and email address, ensuring proper validation and security measures are in place.

Linked work items

Add linked work item

Activity

All Comments History Work log

19 Add a comment...

Status update... Thanks... Agree...

Pro tip: press **M** to comment

Done Done ⚡ Improve Subtask

Details

Assignee **ET** Ed Tracey
[Assign to me](#)

Labels Add labels

Parent ☒ E1-10 Edit profile

Due date Add due date

Start date Add date

Fix versions None

Sprint Add sprint +1

Story point estimate 2

DoD: the requirement is met.
 Time estimated: 1.5 hour.

E1-6 / E1-15

Registration

+ @

Description

As a new user/manager I want be able to sign up.

Acceptance criteria:

1. Sign up page should contain full name, email address, password, confirm password fields, and create an account button.
2. If the email address already exist, should display message and ask to login with existing email.

Subtasks

100% Done

Work	Priority	Assignee	Status
E1-45 Design Sign Up Page	Me...	Ed Tracey	DONE
E1-46 Implement Sign Up Form Validation	Me...	Ed Tracey	DONE
E1-47 Handle Duplicate Email Registration	Me...	Ed Tracey	DONE
E1-48 Create Success and Error Messaging	Me...	Ed Tracey	DONE

Linked work items

Details:

- Assignee: Ed Tracey (Assign to me)
- Labels: Add labels
- Parent: E1-6 Signup page
- Due date: Add due date
- Team: Add team
- Start date: Add date
- Sprint: Add sprint (+1)
- Story point estimate: 3
- Fix versions: None
- Development: [dropdown]
- Reporter: Patrick Strand

Dependencies: should have a valid email for sign up option.

Risk: the user may have only one email address.

E1-15 / E1-45

Design Sign Up Page

+ @

Description

Create the user interface for the sign up page, including fields for full name, email address, password, confirm password, and a create account button.

Linked work items

Add linked work item

Activity

All Comments History Work log

Add a comment...

Status update... Thanks... Agree...

Pro tip: press **M** to comment

Details:

- Assignee: Ed Tracey (Assign to me)
- Labels: Add labels
- Parent: E1-15 Registration
- Due date: Add due date
- Start date: Add date
- Fix versions: None
- Sprint: Add sprint (+1)
- Story point estimate: 5

DoD: team member reviewed, interface contains all required fields.

Time estimated: 4 hours.

✓ E1-15 / 🔗 E1-46

👤 1 🔄 ⋮ ⌵

Implement Sign Up Form Validation



Description

Develop client-side and server-side validation for the sign up form, ensuring all fields are required, passwords match, and email format is correct.

Linked work items

Add linked work item

Activity

All **Comments** History Work log

👤 Add a comment...

Status update... Thanks... Agree...

Pro tip: press **M** to comment

Done ✓ Done ⚡ ⚙ Improve Subtask

Details

Assignee 👤 Ed Tracey
[Assign to me](#)

Labels Add labels

Parent ✓ E1-15 Registration

Due date Add due date

Start date Add date

Fix versions None

Sprint Add sprint +1

Story point estimate 5

DoD: team member reviewed , the criteria is met.
Estimated time: 5 hours.

✓ E1-15 / 🔗 E1-47

👤 1 🔄 ⋮ ⌵

Handle Duplicate Email Registration



Description

Implement logic to check if the email address already exists in the system and display an appropriate message prompting the user to log in instead.

Linked work items

Add linked work item

Activity

All **Comments** History Work log

👤 Add a comment...

Status update... Thanks... Agree...

Pro tip: press **M** to comment

Done ✓ Done ⚡ ⚙ Improve Subtask

Details

Assignee 👤 Ed Tracey
[Assign to me](#)

Labels Add labels

Parent ✓ E1-15 Registration

Due date Add due date

Start date Add date

Fix versions None

Sprint Add sprint +1

Story point estimate 4

DoD: team member reviewed, the requirements are met.
Time estimated: 3 hours.

E1-15 / E1-48

Create Success and Error Messaging

+ @

Description
Develop user feedback mechanisms for successful account creation and for error scenarios such as duplicate email or invalid input.

Linked work items
Add linked work item

Activity
All Comments History Work log

15 Add a comment...

Status update... Thanks... Agree...

Pro tip: press **M** to comment

Done Done ⚡ Improve Subtask

Details

Assignee Ed Tracey
[Assign to me](#)

Labels Add labels

Parent E1-15 Registration

Due date Add due date

Start date Add date

Fix versions None

Sprint Add sprint +1

Story point estimate 4

DoD: the criterias met.
Time estimated: 3 hours.

E1-11 / E1-26

Clean dataset

+ @

Description
As the developer I want to write a script to handle missing data.

Subtasks ... ⚙ +

100% Done

Work	Priority	Assignee	Status
E1-61 Analyze dataset for missing values	Me...	Edita ...	DONE
E1-62 Write the script to handle missing values.	Me...	Edita ...	DONE

Linked work items
Add linked work item

Web links +

Link to document outlining the data set. Connect your OneDrive account

Project Data Connect your OneDrive account

Done Done ⚡ Improve Task

Details ⚙

Assignee Edita Buneviciene

Labels Add labels

Parent E1-11 Import dataset

Due date Add due date

Team Add team

Start date Add date

Sprint Add sprint +1

Story point estimate 4

Fix versions None

Development

Reporter Patrick Strand

Acceptance criteria: The script should remove empty columns/rows
Dependencies: dataset should have some empty cells.
Risk: empty cells still remain in dataset.

E1-26 / E1-61

Analyze dataset for missing values

+ @

✓ **Description**
Scan the imported dataset to detect and quantify missing values in each column or field, and generate a summary report of missing data patterns.

Linked work items
Add linked work item

Activity
All Comments History Work log

EB Add a comment...
Status update... Thanks... Agree...

Done Done Improve Subtask

Details

Assignee Edita Buneviciene

Labels Add labels

Parent E1-26 Clean dataset

Due date Add due date

Start date Add date

Fix versions None

Sprint Add sprint +1

Story point estimate 2

DoD: empty rows are counted.

Estimated time: 2 hours.

E1-26 / E1-62

Write the script to handle missing values.

+ @

Description
Write script using Python to handle missing data or remove unimportant information.

Linked work items
Add linked work item

Activity
All Comments History Work log

EB Add a comment...
Status update... Thanks... Agree...

Pro tip: press **M** to comment

Done Done Improve Subtask

Details

Assignee Edita Buneviciene

Labels Add labels

Parent E1-26 Clean dataset

Due date Add due date

Start date Add date

Fix versions None

Sprint Add sprint +1

Story point estimate 4

DoD: team member reviewed, the script is working.

Estimated time: 4 hours.

🔗 E1-11 / 📄 E1-28

Manual upload data option

+ 📎

▼ **Description**

As an admin I want to have an option to upload dataset manually.

Acceptance criteria:

1. As an admin can upload dataset manually (CSV).
2. Validate when uploaded.

▼ **Subtasks** ... ⚙ +

100% Done

Work	Pri...	As...	Status
🔗 E1-65 Implement backend endpoint for manual CSV upload	M	PS	F DONE
🔗 E1-66 Validate uploaded CSV file format and content	M	PS	F DONE

Linked work items

Add linked work item

Activity

All Comments Work items Work log

Done ▾ ✓ Done ⚡ ⚙ Improve Story

▼ **Details** ⚙

Assignee PS Patrick Strand
[Assign to me](#)

Labels Add labels

Parent 🔗 E1-11 Import dataset

Due date Add due date

Team Add team

Start date Add date

Sprint Add sprint +1

Story point estimate 4

Fix versions None

Development ▾

Reporter PS Patrick Strand

Dependencies: have to have login credentials.

Risk: dataset is not uploading.

📄 E1-28 / 🔗 E1-65

Implement backend endpoint for manual CSV upload

+ 📎

Description

As a developer, I want to create a backend API endpoint that accepts CSV file uploads, so that the uploaded data can be processed and stored.

Linked work items

Add linked work item

Activity

All Comments History Work log

👤 Add a comment...

Status update... Thanks... Agree...

Pro tip: press **M** to comment

Done ▾ ✓ Done ⚡ ⚙ Improve Subtask

▼ **Details** ⚙

Assignee PS Patrick Strand
[Assign to me](#)

Labels Add labels

Parent 📄 E1-28 Manual upload data opt

Due date Add due date

Start date Add date

Fix versions None

Sprint Add sprint +1

Story point estimate 4

Development ▾

DoD: API is created.

Estimated time: 4 hours.

E1-28 / E1-66

1

Validate uploaded CSV file format and content



Description

As a system, I want to validate the structure and content of the uploaded CSV file, so that only correctly formatted datasets are accepted for import.

Linked work items

Add linked work item

Activity

All Comments History Work log

Add a comment...

Pro tip: press **M** to comment

Done Done Improve Subtask

Details

Assignee Patrick Strand
[Assign to me](#)

Labels Add labels

Parent E1-28 Manual upload data opt

Due date Add due date

Start date Add date

Fix versions None

Sprint Add sprint +1

Story point estimate 4

DoD: team members reviewed and criteria met.
Estimated time: 3 hours

E1-6 / E1-79

1

Incorrect password entered



Description

As a user I'd like to get prompt whenever incorrect password entered.

Acceptance criteria:

1. Prompt incorrect password entry
2. Suggest best safety practice when entering password.
3. Display Forgot password or reset

Subtasks

... 100% Done

Work	Priority	Assignee	Status
E1-80 User input validation	Me...	Darius...	DONE
E1-81 Prompt displaying best safety practices while entering password	Me...	Darius...	DONE
E1-82 Redirection to Forgot/reset password page	Me...	Darius...	DONE

Linked work items

Add linked work item

Done Done Improve Task

Details

Assignee Dariusz Olczak
[Assign to me](#)

Labels Add labels

Parent E1-6 Signup page

Due date Add due date

Team evSD_Group1

Start date Add date

Sprint Add sprint +1

Story point estimate 5

Fix versions None

Development

Reporter Dariusz Olczak

Dependencies: user has to be registered prior.
Risk: no clear path for password recovery.

E1-79 / E1-80

User input validation

+ @

Description

Check if user is valid or not by checking your database.

Linked work items

Add linked work item

Activity

All Comments History Work log

19 Add a comment...

Status update... Thanks... Agree...

Pro tip: press **M** to comment

Done Done Improve Subtask

Details

Assignee Dariusz Olczak
[Assign to me](#)

Labels Add labels

Parent ☒ E1-79 Incorrect password ent

Due date Add due date

Team evSD_Group1

Start date Add date

Fix versions None

Sprint Add sprint +1

Story point estimate 4

DoD: the requirements is met for checking user credentials.
Estimated time: 2.5hours.

E1-79 / E1-81

Prompt displaying best safety practices while entering password

+ @

Description

Advice on password combination: password should contain 8 characters, at least 1 capital letter, 1 number.

Linked work items

Add linked work item

Activity

All Comments History Work log

19 Add a comment...

Status update... Thanks... Agree...

Pro tip: press **M** to comment

Done Done Improve Subtask

Details

Assignee Dariusz Olczak
[Assign to me](#)

Labels Add labels

Parent ☒ E1-79 Incorrect password ent

Due date Add due date

Team evSD_Group1

Start date Add date

Fix versions None

Sprint Add sprint +1

Story point estimate 3

DoD: team member reviewed and implemented.
Estimated time: 3hours.

The screenshot shows a Jira ticket titled "Redirection to Forgot/reset password page". The ticket ID is E1-79 / E1-82. The description is "Display forgot/reset password page if I need it." The ticket is assigned to Dariusz Olczak. The parent ticket is "E1-79 Incorrect password ent". The team is "evSD_Group1". The sprint is "Add sprint +1". The story point estimate is "2". The activity tab is selected, showing a comment input field with a "Pro tip: press [M] to comment" message.

DoD: the page is displayed.
Estimated time:1 hour.

Planning Poker Process:

For the Poker process we had a zoom call. PO was Dariusz, scrum master was Edita. So we played a game and voted anonymously,giving a chance for everyone to experience how to conduct the game. We did the game for few tasks but is quite time consuming. So lastly loudly assigned the story points to the remaining tasks by average of the points of all members.

Planning Poker



The screenshot shows the "VOTED: 0" section of the Planning Poker process. A blue bar with the text "ET" is visible. Below it, the text "Pick your estimate" is displayed. A row of buttons with the numbers 0, 1, 2, 3, 5, 8, 13, 21, 34, and 55 is shown for voting.

When scores were tied, the scrum master had the final decision.

3. Sprint planning /Backlog

The list of epics and screenshots including subtask and assignee(for sprint 1 backlog).

E1-1 Import dataset-Importing data E1-8 Account Management-Login to account

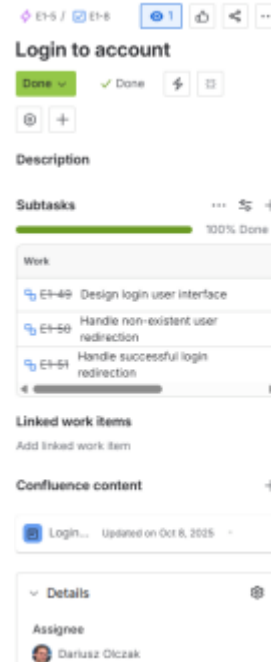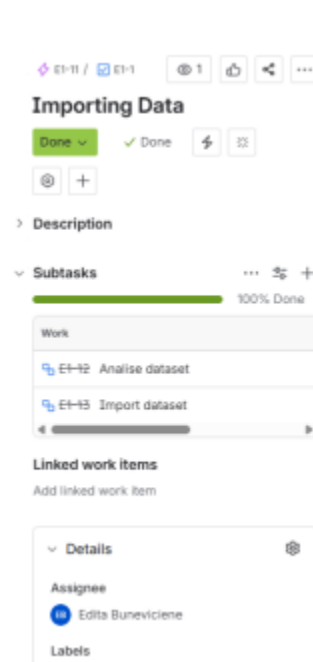

E1-9 Account Management-

Forgot/Reset password

E1-10 Account Management-

Edit profile

✦ E1-5 / ☒ E1-9   

Forgot/Reset password

Done  ✓ Done  

> Description

▼ Subtasks   

100% Done

Work	
	E1-52 Design 'Forgot Password' user interface
	E1-53 Implement 'Forgot Password' button functionality
	E1-55 Integrate email service to send password reset link

Linked work items

Add linked work item

Confluence content 

 Forgot... Updated on Oct 8, 2025

▼ Details 

Assignee

 Ed Tracey

E1-15 Signup page- Registration

✦ E1-5 / ☒ E1-10   

Edit profile

Done  ✓ Done  

> Description

▼ Subtasks   

100% Done

Work	
	E1-57 Implement form to display and edit user details
	E1-58 Display confirmation message after profile update
	E1-59 Add functionality to update password and email

Linked work items

Add linked work item

▼ Details 

Assignee

 Ed Tracey

E1-26 Import dataset-Clean dataset

✦ E1-6 / ☒ E1-15   

Registration

Done  ✓ Done  

> Description

▼ Subtasks   

100% Done

Work	
	E1-45 Design Sign Up Page
	E1-46 Implement Sign Up Form Validation
	E1-47 Handle Duplicate Email Registration
	E1-48 Create Success and Error Messaging

Linked work items

Add linked work item

Confluence content 

 Sing I... Updated on Oct 8, 2025

▼ Details 

Assignee

 Ed Tracey

✦ E1-11 / ☒ E1-26   

Clean dataset

Done  ✓ Done  

Description

▼ Subtasks   

100% Done

Work	
	E1-61 Analyze dataset for missing values
	E1-62 Write the script to handle missing values.

Linked work items

Add linked work item

Web links 

 Link to document... Connect your


 Project... Connect your OneDrive

▼ Details 


Assignee

 Edita Buneviciene


E1-28 Import dataset- Manual upload data option

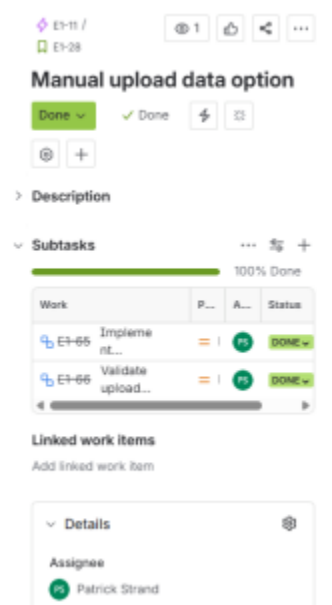

E1-79 Signup page- Incorrect password entered

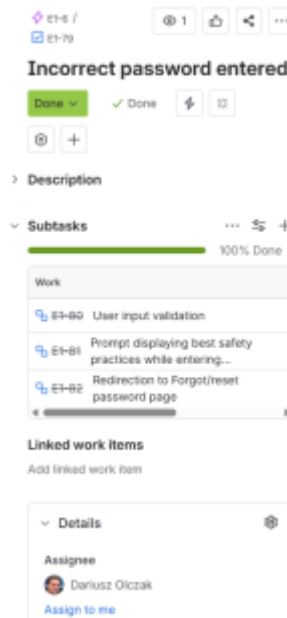

E1-7 Signup page-Initial signup page

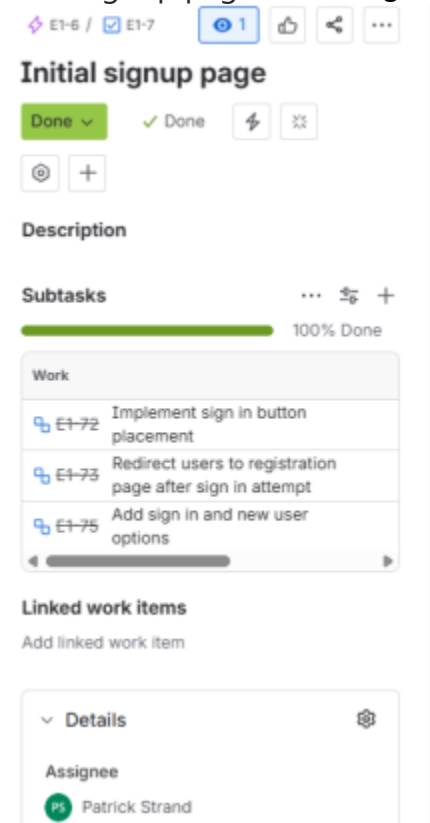

In this sprint we choose velocity and story point approach. Total 35 story points per sprint
1. In total 91 story points in backlog before completing sprint1.

Active scrum board

Task ID	Task Name	Status	Assignee
CS-PS	Incorrect password entered	TO DO	Assignee 1
CS-SS	Manual upload data option	TO DO	Assignee 2
CS-SS	Clean dataset	TO DO	Assignee 3
CS-SS	Registration	TO DO	Assignee 4
CS-SS	Edit profile	TO DO	Assignee 5
CS-SS	Forgot/Reset password	TO DO	Assignee 6
CS-SS	Login to account	TO DO	Assignee 7
CS-SS	Initial signup page	TO DO	Assignee 8

Sprint1 planning report

- [Sprint planning checklist](#)
- [Sprint team members](#)
- [Sprint planning meeting items](#)
 - [Agenda](#)
 - [Create Sprint 1](#)
 - [Details](#)
 - [Velocity tracking](#)
 - [Adjusted velocity tracking](#)
 - [Capacity planning](#)
 - [Potential risks](#)
- [Sprint planning resources](#)
 - [Sprint boards and retrospectives](#)
 - [Team resources and definitions](#)

Sprint planning checklist

Preparation	Meeting	Follow up
- Create Jira, add members - Create Confluence, add members	communication via WhatsApp and Canvas for email exchange	- created Jira, Confluence, Github - weekly updates in Jira and Confluence. - updated scrum board.

• Create Github, add members • Choose dataset • Import dataset • Create the product backlog • Review product backlog and prioritize • Make sure user stories well defined • Make sure user stories reflects the project • Assign story points • Assign developer	• Zoom call weekly • zoom call to play Poker Planning.	• updated stories, description added, subtask described, story points added.
--	---	--

Sprint team members

Name	Role
Edita Buneviciene	Scrum master
Dariusz Olczak	PO
Edward Tracey	Developer
Patrick Strand	Developer

Sprint planning meeting items

Use this template to structure your meeting, set expectations and goals, and define the backlog for the upcoming sprint. For detailed instructions and best practices, see our [sprintplanning guide](#) and review how to estimate story points.

Agenda

1. Choose scrum master and PO
2. Create backlog
3. Assign story points and tasks.
4. Create first sprint

Create Sprint 1

Sprint theme	Create Sprint 1 product backlog
Summary	In this sprint our team will work on creating product backlog, implement stories, learn how to use new tools Jira, Confluence, Github.

Details

Start date	16 Oct 2025
End date	02 Nov 2025
Sprint theme	Sprint 1

Capacity planning

You can customize this template to change or add capacity measurements. You can also review older sprints by adding columns.

	Current sprint	Previous sprint
Total days	14 days	n/a
Team capacity	100%	n/a
Projected capacity	35 points	n/a
Individual capacity	Edita Buneviciene 8 points Ed Tracey 10 points Patrick Strand 8 points Dariusz Olczak 9 points	n/a

Potential risks

Risk	Mitigation
The team members have higher buffer then expected.	The team would move low priority work to the backlog.
The team members not delivering tasks on time	Change the scope of project.


4. Git workflow

Link to github <https://github.com/EditaBuneviciene/AgileProject>

Timeline of most recent commits.



Git workflow sequence.

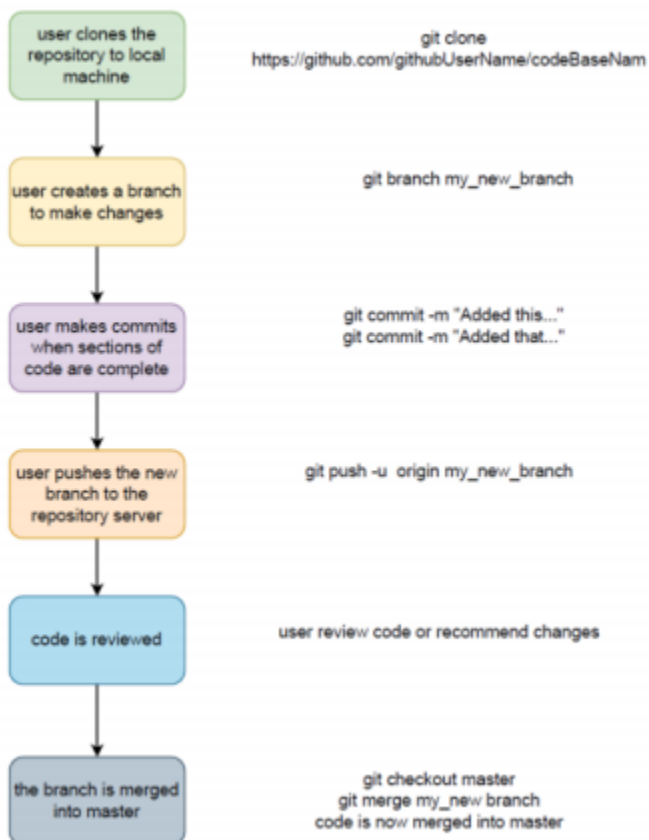

5. Sprint review

Sprint 1 daily scrum meetings

All team members should provide their priorities, progress, and problems each day in this report.

Team name	evSD-1
Direct supervisor	Scrum master Edita
Table of contents	• \uD83D\uDD3 Week1 • \uD83D\uDD3 Week2 • \uD83D\uDD3 Week3 • \uD83D\uDD3 Week4 • \uD83D\uDD3 Week5

Week1

	Name	Priorities 🗨️	Progress 😊	Problems 😞
1	Edita Buneviciene	set github	Waiting on remaining team members emails addresses.	A new members added but no contact for a week.
2	Dariusz Olczak	pick the dataset	Discussed and agreed on dataset	Pick the correct size dataset, previously picked didn't meet the criteria's.
3	Ed Tracey	set WhatsApp group	chat group created	A new member added, no contact.

 Week2

	Name	Priorities 🗓️	Progress 😊	Problems 😞
1	Dariusz Olczak	Set Jira, Confluence	Jira project and Confluence space were created and linked.	Members couldn't sign in due to typing errors.
2	Patrick Strand	Outline objectives, milestones, scope, and success criteria.	Pages created	Understand the project scope.
3	Edita Buneviciene	Work on code for dataset	Analyze dataset, work on code.	It removes a lot of data, analyze again.
4	Ed Tracey	Explore Scrum concepts.	Practice navigating boards, backlogs, and Confluence documentation	

 Week3

	Name	Priorities 🗓️	Progress 😊	Problems 😞
1	evSD_Group1 (Edita Buneviciene Dariusz Olczak Ed Tracey Patrick Strand)	Create epics(tasks), describe, acceptance criteria.	Product backlog created	What want to display for the user.
2	evSD_Group1 (Edita Buneviciene Dariusz Olczak Ed Tracey Patrick Strand)	Create subtask, describe them	Product backlog created	Can we implement them ?

 Week4

	Name	Priorities 🗣️	Progress 😊	Problems 😞
1	evSD_Group1 (Edita Buneviciene Dariusz Olczak Ed Tracey Patrick Strand)	Poker planning game	Story points assigned	Poker planning taking too long, assigned the rest tasks by general agreement on points value.
2	evSD_Group1 (Edita Buneviciene Dariusz Olczak Ed Tracey Patrick Strand)	Prioritize backlog	Most important tasks moved to top of backlog.	The number of tasks could be large.

 Week5

	Name	Priorities 🗣️	Progress 😊	Problems 😞
1	evSD_Group1 (Edita Buneviciene Dariusz Olczak Ed Tracey Patrick Strand)	Sprint 1 planning	Developers assigned	
2	evSD_Group1 (Edita Buneviciene Dariusz Olczak Ed Tracey Patrick Strand)	Implement the subtasks	Implementing the subtasks.	The number of tasks could be large.

Sprint1 review report

Sprint Summary

Sprint Dates: 13 Oct 2025to 24 Oct 2025

Sprint Goal: Report

To establish the project's foundation, data processing ways and user management system by enabling data upload, cleansing, and basic features required for clear and intuitive visualization and analysis.

Sprint Detail

Completed

Key	Summary	Story Points	Planned	Comment	Feedback
E1-7	Initial signup page	4	YES		
E1-15	Registration	3	YES		
E1-79	Incorrect password entered	5	YES		
E1-8	Login to account	4	YES		
E1-9	Forgot/Reset password	3	YES		
E1-10	Edit profile	4	YES		
E1-1	Importing Data	4	YES		

E1-28	Manual upload data option	4	YES		
E1-26	Clean dataset	4	YES		

Added

Key	Summary	Story Points	Planned	Comment	Feedback
E1-79	Incorrect password entered	5	YES		

Removed

No issues removed

Impediments & Risks

Impediments

Title / Description	Impact	Status	Action taken
The original dataset was found to be too small and unsuitable for the project requirements.	small	resolved	The team spent additional time researching and selecting a new dataset (<i>Global Health, Mortality, and Disease Trends Since 2000</i>).
Initial setup and linking between Jira and Confluence	medium	resolved	Extra time dedicated as team members learned how to set up, connect, navigate and configure the tools properly. Problems were resolved after establishing shared access and permissions.
Communication Delays	small	resolved	Coordination was occasionally slowed down by work and personal schedules, which impacted meeting times and the pace of collaboration

Risks

Title / Description	Impact	Likelihood	Action taken
Risk of delayed approval was present as initial dataset was too small, requiring a search for a larger one.	Medium		Thoroughly research performed by entire team to maximise search result and compatibility with Stakeholders requirements.
Possibility of limited or lost access to Jira/Confluence free access.	High		The risk of free Confluence/Jira access expiring caused concern about losing reports, backlogs, and sprint data, which would have resulted in additional recovery and transfer work.
Lack of communication/Miscommunication as team members balancing academic and work responsibilities occasionally led to delays.	Small		Shared group chat, phone calls and daily updates were implemented to keep all members up to date with progressions and delays.

Burndown chart

Spaces / avsd-1 / Reports
Sprint burndown chart

[How to read this report](#)

Sprint: E1 Sprint 1 Estimation field: Story points

Linked content

Retrospective: E1 Sprint 1
 Updated 20 minutes ago - Confluence - Agile Processes Project


[Copy link](#) X

Untitled whiteboard 2025-10-02
 Confluence - Agile Processes Project

[Copy link](#) X

Date - October 13th, 2025 - October 24th, 2025

Sprint goal - Report

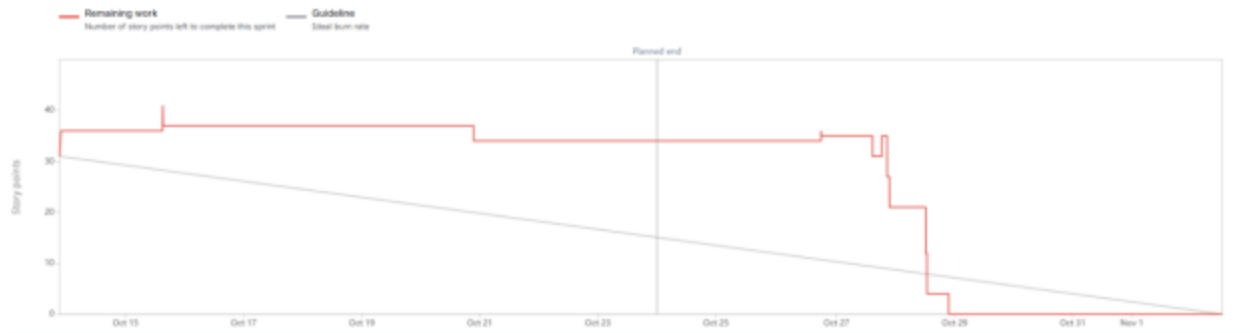

Report: E1 Sprint 1

Work item added after sprint start

Scope changes log

[View in All work navigator](#)

Date ↑	Key	Summary	Work type	Epic	Details of scope change	Change in estimation
2025-10-16	E1-79	Incorrect password entered	Task		Work item added to sprint	-
2025-10-16	E1-79	Incorrect password entered	Task		Estimate of 5 has been added	- → 5
2025-10-16	E1-39	set bitbucket / github	Task		Work item removed from sprint	-4
2025-10-20	E1-27	Standardize units	Task		Work item removed from sprint	-3
2025-10-26	E1-1	Importing Data	Task		Estimate changed from 2 to 4	2 → 4
2025-10-26	E1-26	Clean dataset	Task		Estimate changed from 5 to 4	5 → 4
2025-10-28	E1-27	Standardize units	Task		Estimate changed from 3 to 4	3 → 4

Your sprint commitment has decreased by 1 story point
 Due to scope changes: You have 30 story points to complete this sprint

[View in All work navigator](#)

Completed work items


Key	Summary	Work type	Epic	Status	Assignee	Story points
E1-2	Initial signup page	Task		DONE		4
E1-15	Registration	Task		DONE		5
E1-8	Login to account	Task		DONE		4
E1-9	Forgot/Reset password	Task		DONE		5
E1-10	Edit profile	Task		DONE		4
E1-1	Importing Data	Task		DONE		4
E1-29	Clean dataset	Task		DONE		4
E1-29	Manual upload data option	Story		DONE		4
E1-79	Incorrect password entered	Task		DONE		5

Work items completed outside of sprint

Key	Summary	Work type	Epic	Status	Assignee	Story points
-----	---------	-----------	------	--------	----------	--------------

Burnup report



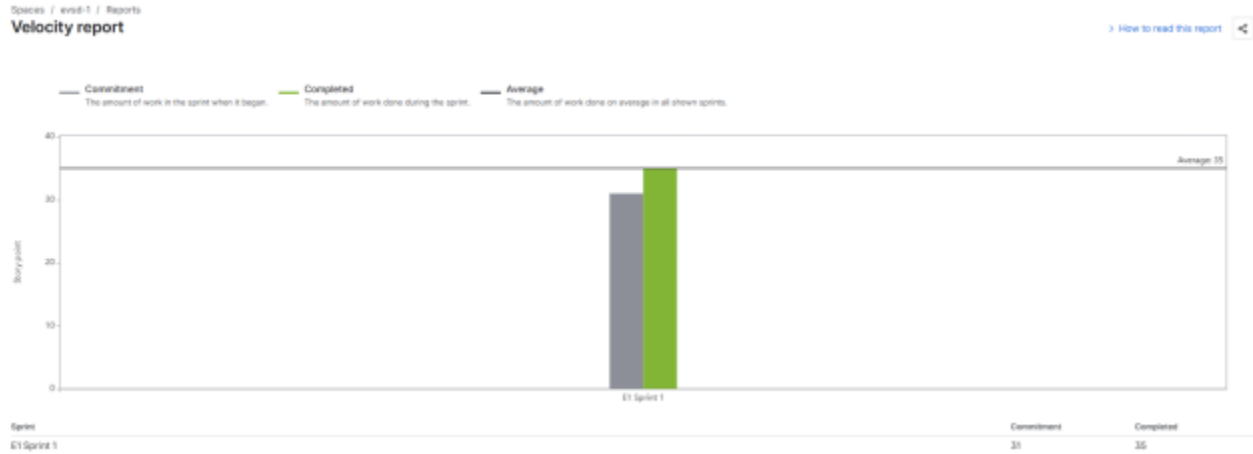

6. Retrospective

Reflect on past work and identify opportunities for improvement by following the instructions for the Retrospective Play.

Overview

Date	31 Oct 2025
Team	ev SD-1
Participants	evSD Group1 (Edita Buneviciene Dariusz Olczak Ed Tracey Patrick Strand)

During this sprint, our team continued using the AgileScrum approach to keep work organized and transparent.

We managed all sprint tasks through Jira and used Confluence to track up dates and document progress.

This sprint focused mainly on improving how data is imported, standardized, and presented through visual dashboards.

Everyone worked together to balance workload, share feedback early, and keep communication open throughout the process through What's app and Zoom.

As for next sprints, do not proceed with sprint complete button until most of report are exported to the file. While doing report I discovered that backlog, scrum board, epic burndown

chart and others are not achievable since the sprint is complete. The lack of knowledge in tool was definitely effected in this case.

Retrospective

 Start doing	 Stop doing	 Keep doing
Spend a little more time aligning on priorities at the start of each sprint	Leaving some stories without a clear assignee halfway through a sprint.	Daily stand-ups and open communication.
Make better use of Confluence whiteboards for group discussions and retros.	Updating progress manually when it can be synced directly from Jira.	Clear documentation and updates in Confluence.
Set up automatic linking between Jira tickets and Confluence pages to save time. and the next sprint		Collaboration between data, visualization, and analysis teams.

Action items

- Assign all remaining un-allocated items for Sprint 2.
- Set up automated status reports in Confluence.
- Keep improving visualization features and export options.

Report Sprint 2

Sprint 2 Product backlog

Sprint 2 epics and user stories:

Repository: Github repository and details

Trend analysis: Filter mortality trends in certain years, Filter series by relevant countries.

Visualisation: Create HTML, Implementation of Login stories, Connect User login web pages.

Type	Key	Summary	Assignee	Priority	Status	Updated
	E1-129	Create test home page for data visualization.	 Ed Tracey	 Medium		Nov 13, 2025, 20:58
	E1-128	Create instructions in the read.me file for user to start local ...	 Ed Tracey	 Medium		Nov 13, 2025, 20:56
	E1-127	Add on-click functionality to buttons for navigation.	 Ed Tracey	 Medium		Nov 13, 2025, 20:55
	E1-126	Ensure each html page layout is complete.	 Ed Tracey	 Medium		Nov 13, 2025, 20:54
	E1-125	Connect User login web pages	 Ed Tracey	 Medium		Nov 13, 2025, 20:58
	E1-124	Visualisation		 Medium		Nov 12, 2025, 21:53
	E1-123	Trend analysis	 Edita Buneviciene	 Medium		Nov 10, 2025, 12:45
	E1-122	Repository	 Edita Buneviciene	 Medium		Nov 12, 2025, 21:53
	E1-121	Monitor accuracy and timing	 Patrick Strand	 Medium		Oct 29, 2025, 03:07
	E1-120	Implement the schedule	 Patrick Strand	 Medium		Oct 29, 2025, 03:05
	E1-119	Plan refresh frequency	 Patrick Strand	 Medium		Oct 29, 2025, 03:04
	E1-118	Collect and manage feedback	 Patrick Strand	 Medium		Oct 29, 2025, 03:02

	E1-117	Create shareable links or exports	Patrick Strand	Medium	REVIEW	Oct 29, 2025, 03:00
	E1-116	Set up sharing permissions	Patrick Strand	Medium	REVIEW	Oct 29, 2025, 02:59
	E1-115	Test the report builder		Medium	REVIEW	Oct 29, 2025, 02:55
	E1-114	Design the summary layout	Patrick Strand	Medium	REVIEW	Oct 29, 2025, 02:54
	E1-113	Define summary fields	Patrick Strand	Medium	REVIEW	Oct 29, 2025, 02:53
	E1-112	Review with stakeholders/client	Patrick Strand	Medium	REVIEW	Oct 29, 2025, 02:48
	E1-111	Build initial visual templates	Patrick Strand	Medium	REVIEW	Oct 29, 2025, 02:46
	E1-110	Plan visualization types	Patrick Strand	Medium	REVIEW	Oct 29, 2025, 02:47
	E1-109	Upload and tag in confluence	Patrick Strand	Medium	REVIEW	Oct 29, 2025, 02:27
	E1-108	Create a simple export format		Medium	REVIEW	Oct 29, 2025, 02:25
	E1-107	Identify key chat threads		Medium	REVIEW	Oct 29, 2025, 02:22
	E1-106	Verify and record updates	Dariusz Olczak	Medium	REVIEW	Oct 29, 2025, 02:14
Synced 11 minutes ago • 90 items						
	E1-105	Add source linking	Edita Buneviciene	Medium	REVIEW	Oct 29, 2025, 02:06
	E1-104	Identify data sources to connect	Edita Buneviciene	Medium	REVIEW	Oct 29, 2025, 02:04
	E1-103	Confirm usability across devices	Patrick Strand	Medium	REVIEW	Oct 29, 2025, 01:41
	E1-102	Adjust layouts for mobile use	Patrick Strand	Medium	REVIEW	Oct 29, 2025, 01:40
	E1-101	Review existing layout	Patrick Strand	Medium	REVIEW	Oct 29, 2025, 01:38
	E1-100	Data Filtering and Display	Dariusz Olczak	Medium	DONE	Nov 15, 2025, 11:38
	E1-99	Country Filtering by Series	Dariusz Olczak	Medium	DONE	Nov 15, 2025, 11:37
	E1-98	Extract and Display Unique Series	Dariusz Olczak	Medium	DONE	Nov 15, 2025, 12:10
	E1-97	Check presentation	Ed Tracey	Medium	REVIEW	Nov 12, 2025, 21:04
	E1-96	Data to the chart	Ed Tracey	Medium	REVIEW	Nov 12, 2025, 21:09
	E1-95	the chart layout	Ed Tracey	Medium	REVIEW	Nov 12, 2025, 21:08
	E1-94	Create Visual Summaries	Patrick Strand	Medium	REVIEW	Nov 14, 2025, 16:08
	E1-93	Group Totals and Rates	Patrick Strand	Medium	REVIEW	Nov 14, 2025, 16:07
	E1-92	Add Demographic Fields	Patrick Strand	Medium	REVIEW	Nov 14, 2025, 16:05
	E1-91	Add Clear Setup Information	Ed Tracey	Medium	REVIEW	Nov 6, 2025, 21:35
	E1-90	Organize Branches and Rules	Ed Tracey	Medium	REVIEW	Nov 6, 2025, 21:34
	E1-89	Create the Repository	Edita Buneviciene	Medium	REVIEW	Nov 6, 2025, 21:34
	E1-88	Test and display in main.py	Edita Buneviciene	Medium	DONE	Nov 15, 2025, 15:50
	E1-87	Mortality and nurses comparison	Edita Buneviciene	Medium	DONE	Nov 15, 2025, 15:50
	E1-86	Mortality rates between Ireland and Pakistan	Edita Buneviciene	Medium	DONE	Nov 15, 2025, 15:50
	E1-82	Redirection to Forgot/reset password page	Dariusz Olczak	Medium	DONE	Oct 28, 2025, 12:10
	E1-81	Prompt displaying best safety practices while entering pass...	Dariusz Olczak	Medium	DONE	Oct 28, 2025, 12:10
	E1-80	User input validation	Dariusz Olczak	Medium	DONE	Oct 28, 2025, 12:10
	E1-79	Incorrect password entered	Dariusz Olczak	Medium	DONE	Oct 28, 2025, 12:11

User stories and subtask

Filter mortality trends in certain years.

TEST ⌵ ⚡ ⌚ +

▼ Description

As a user, I want to filter mortality statistics by year so I can compare two countries death rates.

Acceptance criteria:

1. Script is written in Python, using Seaborn or Matplot for diagrams visualization.

2. A plot with the results displayed

Dependencies:

1. Do research on Seaborn and Matplot as this is a new technology to be used.

2. Clean data csv file must for this task.

Risk for a story:

Team has little experience in technology to be used.

▼ Subtasks

100% Done

Work	P...	A...	Status
E1-06 Mortality rates...	==	E1	DONE ▾
E1-07 Mortality and...	==	E1	DONE ▾
E1-08 Test and display ...	==	E1	DONE ▾

▼ Details

Assignee

Edita Buneviciene

Labels

Add labels

Parent

E1-123 Trend analysis

Due date

Nov 15, 2025

Team

Add team

Start date

Nov 09, 2025

Sprint

E1 Sprint 2

Story point estimate

4

Fix versions

None

Development

Reporter

Subtask:

E1-29 / E1-86

Mortality rates between Ireland and Pakistan

Done ✓ Done ⚡ ⌚ +

Description

As developer I write Python write code to compare Mortality rate in male and female between Ireland and Pakistan while displaying bar chart diagram.

DoD criterion:

Team member revied and standard of code and graphs displayed are met.

Linked work items

Add linked work item

Details

Assignee

EB Edita Buneviciene

Labels

Add labels

Parent

E1-29 Filter mortality trends in certain

Due date

Nov 15, 2025

Estimated time: 3 hours

E1-29 / E1-87

Mortality and nurses comparison

Done ✓ Done ⚡ ⌚ +

Description

Using python write a script to compare "Mortality from CVD, cancer, diabetes or CRD between exact ages 30 and 70, male (%)" and "Nurses and midwives (per 1,000 people)" in Ireland and China between 2000-2021 and display a plot.

DoD criterion:

Team member revied and standard of code and graphs displayed are met.

Linked work items

Add linked work item

Estimated time: 1.5 hour

Details

Assignee

EB Edita Buneviciene

Labels

Add labels

Parent

E1-29 Filter mortality trends in certain

Due date

Nov 15, 2025

Start date

Nov 02, 2025

Fix versions

None

Sprint

E1 Sprint 2

Story point estimate

2

Development

Details

Assignee

EB Edita Buneviciene

Labels

Add labels

Parent

E1-29 Filter mortality trends in certain

Due date

Nov 15, 2025

Start date

Nov 02, 2025

Fix versions

None

Sprint

E1 Sprint 2

Story point estimate

1

E1-29 / E1-88

1

Test and display in main.py

Done

✓ Done

+

Description

Test if the diagrams are displayed of "Mortality_from_cancer" "Mortality rate" and visualize by Python TKinter.

DoD criterion:

1. Team member revied and standard of code and graphs displayed are met.

2. Visualition in TKinter is complete.

Linked work items

Add linked work item

Estimated time: 2 hours

User story:

Details

Assignee

Edita Buneviciene

Labels

Add labels

Parent

E1-29

 Filter mortality trends in certain

Due date

Nov 15, 2025

Start date

Nov 02, 2025

Fix versions

None

Sprint

E1 Sprint 2

Story point estimate

1

Development

E1-122 / ☒ E1-19

1

Github repository and details

In Progress

Description

As a developer, I want create Git repository, describe how to use it so everyone can access the same scripts and data files, track changes, and collaborate without losing progress.

Acceptance criteria:

1. Describe the workflow used
2. Show examples of git commands
3. README.md should be create with set up information.

Dependencies:

1. Team members must have a valid email.
2. Team members have to accept invite for collaboration.

Risk for the user story:

1. Team members not accept the invite for collaboration.

Subtasks

66% Done

Work

E1-89 Create the Repository

E1-90 Organize Branches and Rules

E1-91 Add Clear Setup Information

Linked work items

Details

Assignee

ET Ed Tracey

Assign to me

Labels

Add labels

Parent

E1-122 Repository

Due date

Nov 15, 2025

Team

Add team

Start date

Nov 02, 2025

Sprint

E1 Sprint 2

Story point estimate

4

Subtasks:

☒ E1-19 / ☒ E1-89

1

Create the Repository

Done

Done

Description

Set up the new repository and name it clearly for the project. Add team members with suitable permissions and agree on a basic structure for folders and files.

DoD criterion:

1. Repository is created.
2. Team members accepted to the emails for invite collaboration.

Details

Assignee

EB Edita Buneviciene

Labels

Add labels

Parent

☒ E1-19 Github repository and details

Due date

Nov 15, 2025

Start date

Nov 02, 2025

Fix versions

None

Sprint

E1 Sprint 2

Story point estimate

1

Estimated time: 2hours

☒ E1-19 / [E1-90](#)

1

Organize Branches and Rules

Done ▾

✓ Done

⚡

🔒

+

✓ Description

As a developer I need to decide how manage updates in repository as everyone would follow the same process for adding or reviewing changes. Keep main branch for stable work and feature branch for development. create Workflow.

DoD criterion:

1. Workflow is created
2. Team members revied it and acceptance criteria is met.

Details

Assignee

ET Ed Tracey

Assign to me

Labels

Add labels

Parent

☒ [E1-19 Github repository and details](#)

Due date

Nov 15, 2025

Start date

Nov 02, 2025

Fix versions

None

Sprint

[E1 Sprint 2](#)

Story point estimate

2

Estimated time: 2.5 hours

Confirmation of pull request from team member.

Pull request successfully merged and closed

You're all set — the [feature-connect_user_login_pages](#) branch can be safely deleted.

Delete branch

Add a comment

☒ E1-19 / [E1-91](#)

1

Add Clear Setup Information

REVIEW ▾

⚡

🔒

+

✓ Description

As a developer I need to write a short guide inside the git repository explaining how to open, run, and update the project. Include simple instructions so new members can join without needing extra help. Created README.md file for this information.

DoD criterion:

1. README.md file is set in Git repository with current details.

Details

Assignee

ET Ed Tracey

Assign to me

Labels

Add labels

Parent

☒ [E1-19 Github repository and details](#)

Due date

🕒 Nov 15, 2025

Start date

Nov 02, 2025

Fix versions

None

Sprint

[E1 Sprint 2](#)

Story point estimate

1

Estimated time: 2 hours

User story:

E1-124 / ☒ E1-125

1

Connect User login web pages

Done

✓ Done

Description

As a user I want to navigate the user login pages so I can login, signup, reset password and access the data visualization page.

Acceptance criteria:

1. Complete html pages and ensure clean navigation.

2. Ensure reverse navigation

3. Successful login should open the main data visualization page (home.html)

Dependencies:

Each html page needs finished layout.

Instructions for testers to setup local server.

Risk for a story:

Local server is not set up on time.

Details

Labels

Add labels

Parent

E1-124 Visualisation

Due date

Nov 13, 2025

Team

evSD_Group1

Start date

Nov 02, 2025

Subtasks

100% Done

Work

E1-126

Ensure each html page layout is complete.

E1-127

Add on-click functionality to buttons for navigation.

E1-128

Create instructions in the read.me file for user to start...

E1-129

Create test home page for data visualization.

Linked work items

Subtasks:

☒ E1-125 / ☒ E1-126

1

Ensure each html page layout is complete.

Done

✓ Done

Description

Test buttons, text input and page navigation.

Ensure all pages load correctly.

DoD criterion:

Team members revied and tests are passed.

PO revied and accepted.

Linked work items

Add linked work item

Details

Labels

Add labels

Parent

E1-125 Connect User login web pages

Due date

Nov 15, 2025

Team

evSD_Group1

Start date

Nov 02, 2025

Fix versions

None

Sprint

E1 Sprint 2

Story point estimate

1

Estimated time: 2 hours

✓ E1-125 / E1-127

1

Add on-click functionality to buttons for navigation.

Done ✓ Done

+

Description

Link the relevant pages to the navigation buttons.

DoD criterion:

All connections establishes and tests are passed.

Linked work items

Add linked work item

Details

Assignee
ET Ed Tracey
[Assign to me](#)

Labels
Add labels

Parent
✓ E1-125 Connect User login web pages

Due date
Nov 15, 2025

Estimated time:1.5 hour

Start date

Nov 02, 2025

Fix versions

None

Sprint

E1 Sprint 2

Story point estimate

1

Development

✓ E1-125 / E1-128

1

Create instructions in the read.me file for user to start local server.

Done ✓ Done

+

Description

Add instructions for running a local server so the developers can test the web interface.

DoD criterion:

Team members revied and [READ.me](#) file is created.

Linked work items

Add linked work item

Details

Assignee
ET Ed Tracey
[Assign to me](#)

Labels
Add labels

Parent
✓ E1-125 Connect User login web pages

Estimated time:1.5 hour

Due date

Nov 15, 2025

Team

evSD_Group1

Start date

Nov 02, 2025

Fix versions

None

Sprint

E1 Sprint 2

Story point estimate

1

Development

▼

Subtasks:

E1-31 / E1-98  1  ..

Extract and Display Unique Series

Done  Done   

✓ **Description**

Description:

Load dataset and extract all unique series names

Extract all unique county names relevant for selected series

Remove duplicates and display in user interface

DoD criterion:

- All unique series names extracted from dataset
- No duplicate series displayed

Estimated time: 4hours

Details 

Assignee
 Dariusz Olczak
[Assign to me](#)

Labels
backend filtering

Parent
☒ E1-31 Filter series by relevant countrie

Due date
Nov 16, 2025

Start date
Nov 02, 2025

Fix versions
None

Sprint
[E1 Sprint 2](#)

Story point estimate
2

E1-31 / E1-99  1  ...

Country Filtering by Series

Done  Done   

✓ **Description**

When user selects a series, show only countries that have data for that series

Filter country list dynamically based on series selection

Remove duplicate countries from filtered list

DoD criterion:

Team member review the results and all criteria are met.

Estimated time: 4 hours.

Details 

Assignee
 Dariusz Olczak
[Assign to me](#)

Labels
backend filtering

Parent
☒ E1-31 Filter series by relevant countrie

Due date
Nov 16, 2025

Start date
Nov 02, 2025

Fix versions
None

Sprint
[E1 Sprint 2](#)

Story point estimate
2

☒ E1-31 / E1-100
 👁 1 🔗 ⋮

Data Filtering and Display

Done ▾
✓ Done
⚡
🔒
+

Description
 Apply country filter to data visualization
 Show data only for user-selected countries
 Update all charts and displays based on country selection
 DoD criterion:
 Team member reviewed and all criteria of displaying graph data filtering are met.

Linked work items
 Add linked work item

Estimated time: 3.5 hours

User story:

E1-124 / E1-32
 👁 1 🔗 ⋮

Create HTML

Done ▾
✓ Done
⚡
🔒
+

Description
 As a developer I need to show the results visually after calculating the trends of series so the user could understand easily. The page will have a chart that displays the data clearly.

Acceptance criteria:

- Tables or charts are clearly labelled with headings.
- Data values are correct and easy to read.
- Basic colors are used to separate sections.
- It should work on Chrome, Firefox.

Dependencies:

- Should have [read.me](#) file to describe any software dependencies if needed, etc.
- The completed html file should be called home.html and placed in the web directory of the source project.
- Any additional files needed should be placed in the web directory or grouped into a new folder inside the web directory.

Risk for a user story:

- Page may load different on other devices
medium risk to mitigate to test other screens or devices.
- Team members may not know where it is stored and or how to view the file .low impact as its only collages but it can happen, save the html/css/js files in shared repo and have a clear and concise readme instructions.

Details
⚙

Assignee
 Dariusz Olczak
[Assign to me](#)

Labels
backend filtering

Parent
☒ E1-31 Filter series by relevant countrie

Due date
 Nov 16, 2025

Start date
 Nov 02, 2025

Fix versions
 None

Sprint
[E1 Sprint 2](#)

Story point estimate
1

Subtasks
⋮ 🔍 +

0% Done

Work	P...	A...	Status
E1-92 Add Demog...	=		REVIEW
E1-93 Group Totals...	=		REVIEW
E1-94 Create Visual...	=		REVIEW

Linked work items

Add linked work item

Details
⚙

Assignee
 Patrick Strand
[Assign to me](#)

Labels
 Add labels

Parent
 E1-124 Visualisation

Due date
 Nov 15, 2025

Team
 Add team

Start date
 Nov 03, 2025

Sprint
[E1 Sprint 2](#)

Story point estimate
4

Subtasks:

E1-32 / E1-92

1

Add Demographic Fields

REVIEW

Description

Add new fields for age and gender, year to help make the reports more meaningful.

DoD criterion:

- The dataset includes at least two new columns:

Charts, tables, and filters in the dashboard can use the new demographic fields.

- Missing or unknown values are handled safely (for example, shown as "Unknown" rather than left blank or removed the row

Details

Assignee

Patrick Strand

Assign to me

Labels

Add labels

Parent

E1-32 Create HTML

Due date

Nov 16, 2025

Start date

Nov 09, 2025

Fix versions

None

Sprint

E1 Sprint 2

Story point estimate

2

Development

Estimated time: 2.5 hours

E1-32 / E1-93

1

Group Totals and Rates

Done

Done

Description

As a developer I want to calculate totals and rates for each age group and gender, so that I can compare how birth, disease or mortality figures differ between different each of the demographic groups and identify where health risks are highest, lowest and any trends.

DoD criterion:

- Records are organised by both age group and gender
- Each group shows a calculated rate (for example, number per 100,000 people).
- Team member review and all tests passed.

Linked work items

Details

Assignee

Patrick Strand

Assign to me

Labels

Add labels

Parent

E1-32 Create HTML

Due date

Nov 15, 2025

Start date

Nov 07, 2025

Fix versions

None

Sprint

E1 Sprint 2

Story point estimate

1

Development

Estimated time: 2hours

E1-32 / E1-94

1

Create Visual Summaries

Done ✓ Done

✓ Description

As a developer

I want to create simple visual summaries using HTML so that users can easily view grouped totals and rates for different age groups and genders in a clean, readable format without needing technical tools and present this information visually.

These visual summaries will be used in reports and dashboards. The design should stay lightweight and easy to understand, avoiding clutter.

DoD criterion:

1. The HTML page opens correctly in modern browsers (Chrome, Edge, Firefox).
2. The HTML file is stored in the shared repository under the correct project folder.

Estimated time: 4 hours

User story:

E1-124 / E1-30

1

Display Charts for Data Selections

Done ✓ Done

✓ Description

As a user , I want to display charts that display the selected data from the database.

Acceptance criteria:

1. Graph must show relevant data points for the selected data, including axis names and chart title.
2. If the data selected is grouped by year, topic, etc, a label must be shown on the graph to reflect the selection.
3. The graph must be clear and uncluttered.
4. The page must be named home.html and will replace the current temporary home.html page in the web folder.

Dependencies:

1. Dataset must be cleaned/sorted.
2. The html for the page for the source should be completed.

Risk for a story:

1. External dependencies for sorting and visualization may need to be debugged.

Details

Assignee

PS Patrick Strand

[Assign to me](#)

Labels

Add labels

Parent

E1-32 Create HTML

Due date

Nov 15, 2025

Start date

Nov 03, 2025

Fix versions

None

Sprint

E1 Sprint 2

Story point estimate

2

Subtasks

0% Done

Work	P...	A...	Status
E1-95 The chart layout	PS	REVIEW	
E1-96 Data to the chart	PS	REVIEW	
E1-97 Check Visualiz...	PS	REVIEW	

Linked work items

Add linked work item

Details

Assignee

PS Patrick Strand

[Assign to me](#)

Labels

Add labels

Parent

E1-124 Visualisation

Due date

Nov 16, 2025

Team

Add team

Start date

Nov 02, 2025

Sprint

E1 Sprint 2

Story point estimate

5

Subtasks:

The chart layout

Done ▾ ✓ Done ⚡ ⌂ +

Description

As a developer I want to display the selected data on a graph. The name for each axis of the graph should match the column header of the data set selection.

DoD criterion:

This task is complete when a selected data set can be visualized on the web page.

Details

Assignee
Patrick Strand
[Assign to me](#)

Labels
Add labels

Parent
[E1-30 Display Charts for Data Selectio](#)

Due date
Nov 16, 2025

Start date
Nov 02, 2025

Fix versions
None

Sprint
[E1 Sprint 2](#)

Story point estimate
2

Estimated time: 3hours.

E1-30 / E1-96 ⌕ 1 🔗 ⋮

Data to the chart

REVIEW ▾ ⚡ ⌂ +

Description

As a developer I want to make selections of the data set and sort by size, date, etc.. The data should be cleaned/sorted before selected to avoid any null, empty enteries.

DoD criterion:

The data series that will be plotted on the graph should reflect the selected data. Any selections should be tested for incompatible data, (Does the graphed data look complete?)

Details

Assignee
Patrick Strand
[Assign to me](#)

Labels
Add labels

Parent
[E1-30 Display Charts for Data Selectio](#)

Due date
[Nov 16, 2025](#)

Start date
Nov 02, 2025

Fix versions
None

Sprint
[E1 Sprint 2](#)

Story point estimate
2

Estimated time: 3.5 hours

The screenshot shows a Jira ticket interface. At the top, there's a header with 'E1-30 / E1-97', a '1' icon, and a share icon. The title 'Check Visualization' is prominently displayed. Below the title, there's a 'Done' button and a 'Done' status indicator. The 'Description' section contains a user story: 'As a developer I want to ensure that the graph has the following elements:'. It lists three requirements: 'Title', 'Axis names are correct', and 'Display grouping or sorting label for the graph.'. An 'Example:' section follows, stating: 'If I want to display the **Number of Deaths** between **2000 to 2001** from the **Ebola Virus** in **Africa**, the graph should clearly show this information in a clear and uncluttered manner.'. Below this, a 'DoD:' (Definition of Done) section lists: 'Axis titles match the column headers or sorting of the selected data.' and 'Visually, the graph is readable and clear.'. On the right, a 'Details' sidebar shows fields like 'Assignee' (Patrick Strand), 'Labels', 'Parent' (E1-30 Display Charts for Data Selectio), 'Due date' (Nov 16, 2025), 'Start date' (Nov 02, 2025), 'Fix versions' (None), 'Sprint' (E1 Sprint 2), and 'Story point estimate' (1).

Estimated time: 4 hours.

Estimated time could change because some unexpected issues could arise while working on a certain subtask.

Planning Poker Process:

For the Poker process we had a zoom call like in previous sprint. PO was Edita, scrum master was Dariusz. So we played a game and voted anonymously. We did the game for few tasks but is quite time consuming. So lastly loudly assigned the story points to the remaining tasks by average of the points of all members.

The screenshot shows the 'Planning Poker' interface. At the top, it says 'VOTED: 0'. Below this, there's a blue bar with a circular button labeled 'ET'. Underneath the bar, it says 'Pick your estimate'. At the bottom, there's a row of buttons with the following values: 0, 1, 2, 3, 5, 8, 13, 21, 34, and 55.

When scores were tied, the scrum master had the final decision.

Sprint planning /Backlog

Backlog:

The screenshot shows a Jira backlog with two sections. The top section is titled 'E1 Sprint 2 2 Nov - 15 Nov (6 work items)' and contains six items. The bottom section is titled 'Backlog (7 work items)' and contains seven items. Each item has a checkbox, a key, a description, a status, a priority, a due date, and an assignee.

Section	Item Key	Description	Status	Priority	Due Date	Assignee
E1 Sprint 2	E1-29	Filter mortality trends in certain years.	TREND ANALYSIS	DONE	Nov 15	EB
	E1-19	Github repository and details	REPOSITORY	TEST	Nov 15	ET
	E1-32	Create HTML	VISUALISATION	DONE	Nov 15	PS
	E1-39	Display Charts for Data Selections	VISUALISATION	DONE	Nov 16	PS
	E1-31	Filter series by relevant countries.	TREND ANALYSIS	TEST	Nov 16	DO
	E1-125	Connect User login web pages	VISUALISATION	REVIEW	Nov 13	ET
Backlog	E1-35	visualizations to responsive for phones	TO DO	5		PS
	E1-37	integrate tools with data eg link to original data set	TO DO	4		ET
	E1-36	exporter- able to download chats to confluence	TO DO	3		ET
	E1-3	Data Presentation and Visualisation	TO DO	4		DO
	E1-39	user: report builder can generate summaries	TO DO	4		DO
	E1-41	collaborator - share reports so that teams can discuss globe health	TO DO	4		ET
	E1-42	scheduled data refreshes to ensure reports are accurate(scrum)	TO DO	5		PS

User story “Filter mortality trends in certain years” assigned to Edita Buneviciene.
Subtasks of “Filter mortality trends in certain years” are assigned to Edita Buneviciene too.

User story “Github repository and details” assigned to Ed Tracey.
Subtask “Create the Repository” is assigned to Edita Buneviciene.
Subtasks “Organize Branches and Rules” and “Add clear Setup Information” are assigned to Ed Tracey.

User story “Create HTML” is assigned to Patrick Strand. All subtasks belonging to this tasks are assigned to Patrick too.


User story “Display Charts for data Selections” is assigned to Patrick Strand. All belonging subtasks of the story are assigned to Patrick as well.

User story “Filter series by relevant countries” is assigned to Dariusz Olczak. All belonging subtasks are assigned to Dariusz Olczak.


User story “Connect User login web pages” is assigned to Ed Tracey. All belonging subtasks are assigned to Ed Tracey.

In this sprint we choose velocity and story point approach. Total 26 story points per sprint 2. In total 55 story points in backlog before completing sprint2.

Timeline:

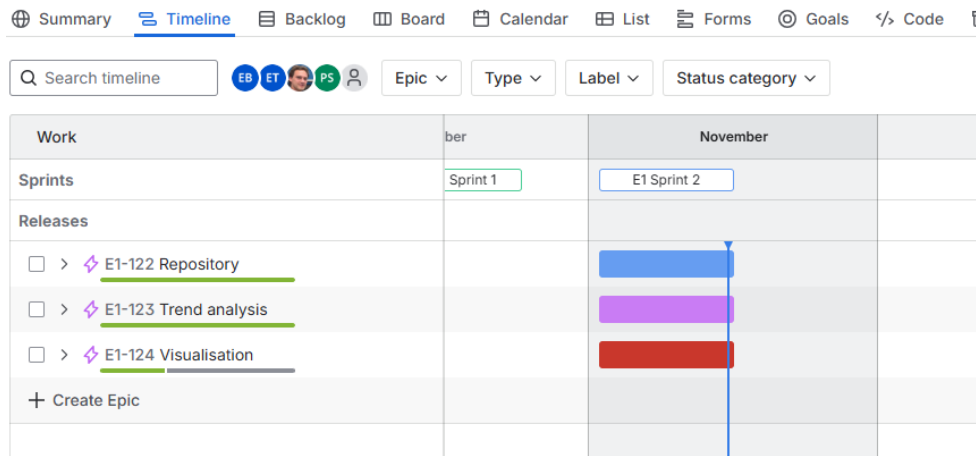

Scrum board screenshot:

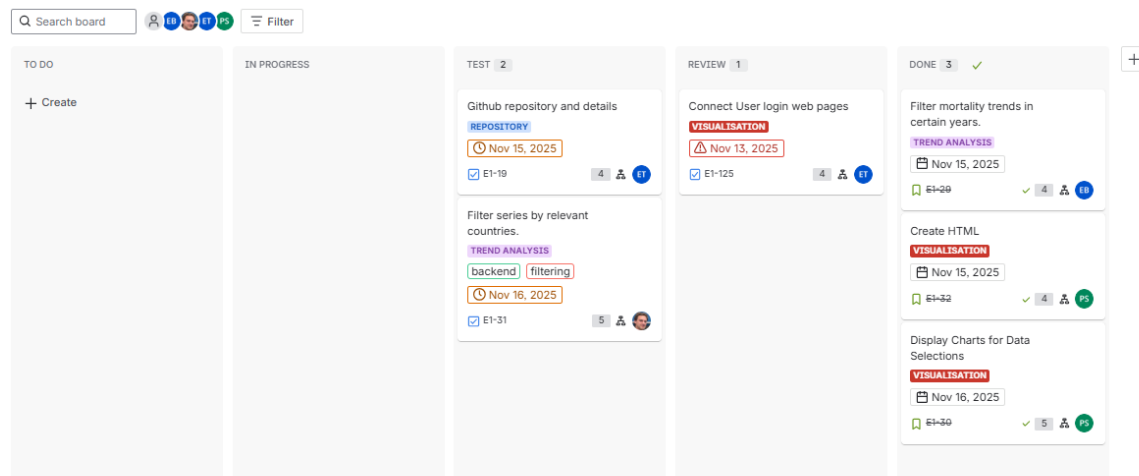

Sprint 2 planning report

- [✔ Sprint planning checklist](#)
- [👤 Sprint team members](#)
- [📋 Sprint planning meeting items](#)
 - [Agenda](#)
 - [Previous sprint summary](#)

- [Details](#)
- [Velocity tracking](#)
- [Adjusted velocity tracking](#)
- [Capacity planning](#)
- [Potential risks](#)
- [?? Sprint planning resources](#)
 - [Sprint boards and retrospectives](#)
 - [Team resources and definitions](#)

✓ Sprint planning checklist

Preparation	Meeting	Follow up
• Set up GitHub • Add Members • review backlog and make sure it reflect the project • Write script to do some comparisons • Git commands • Start working on HTML	• Communication via WhatsApp • Zoom call	• Git is set • Code is working • weekly updates on Jira • Mockup of HTML

👥 Sprint team members

Name	Role
Dariusz Olczak	Scrum master
Edita Buneviciene	PO
Ed Tracey	Developer
Patrick Strand	Developer

Sprint planning meeting items

Agenda

1. Sprint 2 closed
2. User stories in Sprint 2 completed
3. User stories in Sprint 2 completed
4. Create visualisation
5. HTML foundation

Previous sprint summary

Sprint theme	Visualization, HTML foundation
Story points	in Sprint 2 story points for user stories was 26. It was no user stories left for next sprint.
Summary	During this sprint, the team completed key setup activities and initiated core development tasks to establish the foundation of the project. The GitHub repository was created, team members were added, and the backlog was reviewed and refined to ensure it accurately represented the project scope and priorities. On the development side, the team implemented an initial comparison script and reviewed essential Git commands to standardize collaboration workflows. Work began on the HTML foundation for the user interface, providing the structural base for upcoming features. Additionally, initial data visualizations were created to support future analytical and prediction capabilities.

Details

Start date	03 Nov 2025
End date	16 Nov 2025
Sprint theme	Visualization, HTML foundation.

Capacity planning

	Current sprint	Previous sprint
Total days	14	28


Team capacity	100%	100%
Projected capacity	26	35
Individual capacity	Edita Buneviciene 5	8 points
	Dariusz Olczak 5	9 points
	Ed Tracey 7	10 points
	Patrick Strand 9	8 points

Potential risks

Risk	Mitigation
If the GitHub repository setup or team access is delayed, it could postpone development and collaboration	Assign a dedicated person to verify that everyone has the required access

Git workflow

This project uses the **GIT Feature Branch** workflow as shown below.

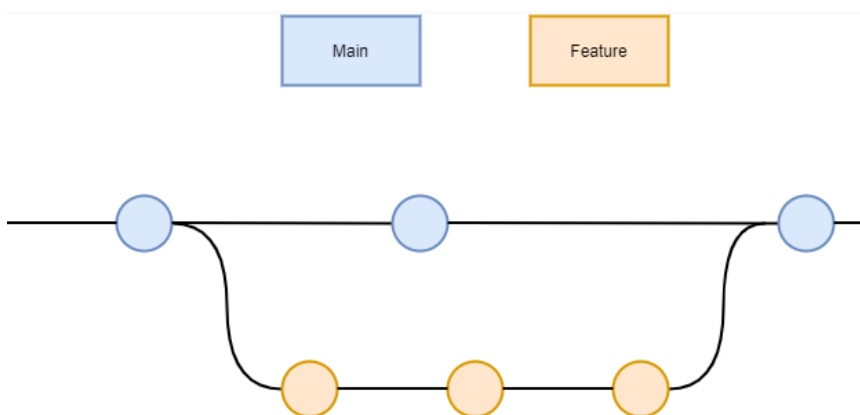

When a new feature is to be added, the developer first creates a new branch from the main branch.

When the feature branch has been tested, a pull request is made to merge the feature into the main branch. The pull request is reviewed by the development team, and any requested changes or questions are addressed before merging into the main branch.

Git commands

What are the differences between git blame, git log and git status?

Status - checks the current status of the branch you are currently on, the *git status* command is used. It will show files that have been modified and files that are not yet tracked. Below shows an untracked file that was added to the source code.

```
PS C:\Users\edwar\source\AgileProject\web> git status
On branch feature-connect_user_login_pages
Your branch is up to date with 'origin/feature-connect_user_login_pages'.

Untracked files:
  (use "git add <file>..." to include in what will be committed)
    local_server_setup_instructions.txt
```

Git log- allows developers to view the entire commit history of a repository - helping them track changes, review project progress, and identify when and by whom changes were made.

```
PS C:\Users\ebune\Desktop\AgileProject> git status
On branch edita
Your branch is up to date with 'origin/edita'.

Changes not staged for commit:
  (use "git add <file>..." to update what will be committed)
  (use "git restore <file>..." to discard changes in working directory)
    modified:   cleanCSVand_corr/cleanCSV.py

Untracked files:
  (use "git add <file>..." to include in what will be committed)
    cleanCSVand_corr/Data.csv
    cleanCSVand_corr/cleaned_file.csv

no changes added to commit (use "git add" and/or "git commit -a")
PS C:\Users\ebune\Desktop\AgileProject> git log
commit 9f4c4a525e77cda215d126499da7ac806a359f8a (HEAD -> edita, origin/edita)
Author: EditaBuneviciene <114923692+EditaBuneviciene@users.noreply.github.com>
Date: Mon Nov 10 12:30:13 2025 +0000

    added mortality from cancer code

commit 7e1d3af696e127c980d60b9663574b269f3ba937
Merge: f12a06c b60a66d
Author: EditaBuneviciene <114923692+EditaBuneviciene@users.noreply.github.com>
Date: Sun Nov 9 17:26:22 2025 +0000

    Merge branch 'main' of https://github.com/EditaBuneviciene/AgileProject into edita

commit f12a06c94872aaf4961a29c5cfaee9ef840ad37d
Author: EditaBuneviciene <114923692+EditaBuneviciene@users.noreply.github.com>
Date: Sun Nov 9 17:19:52 2025 +0000

    mortality rate code

commit b60a66dfb6853170e8ee398c7398af6e5932645f
Author: EditaBuneviciene <114923692+EditaBuneviciene@users.noreply.github.com>
Date: Sun Nov 9 17:05:40 2025 +0000

    updated code for series name.csv

commit 9f4c4a525e77cda215d126499da7ac806a359f8a (HEAD -> edita, origin/edita)
Author: EditaBuneviciene <114923692+EditaBuneviciene@users.noreply.github.com>
Date: Mon Nov 10 12:30:13 2025 +0000
```

Git blame, it gives the information of each line about who edited it, giving the last commit that modified the line, the author, the timestamp of the change, the line number and code content (optionally).

```
PS C:\Users\ebune\Desktop\AgileProject> git blame README.md
88ffc97f (edwardtracey 2025-10-27 19:00:50 +0000) 1) # AgileProject
150dee64 (EditaBuneviciene 2025-11-13 21:59:55 +0000) 2)
1a270cb5 (EditaBuneviciene 2025-11-13 22:04:15 +0000) 3) - Edita Buneviciene R00257694 email edita.buneviciene@mymtu.ie
88ffc97f (edwardtracey 2025-10-27 19:00:50 +0000) 4)
1a270cb5 (EditaBuneviciene 2025-11-13 22:04:15 +0000) 5) - Edward Tracey R00257771 edward.tracey@mymtu.ie
88ffc97f (edwardtracey 2025-10-27 19:00:50 +0000) 6)
1a270cb5 (EditaBuneviciene 2025-11-13 22:04:15 +0000) 7) - Dariusz Olczack Zwolinski R00242508
88ffc97f (edwardtracey 2025-10-27 19:00:50 +0000) 8)
1a270cb5 (EditaBuneviciene 2025-11-13 22:04:15 +0000) 9) - Patrick Strand R00064201 Email: p.strand@mymtu.ie
88ffc97f (edwardtracey 2025-10-27 19:00:50 +0000) 10)
88ffc97f (edwardtracey 2025-10-27 19:00:50 +0000) 11)
88ffc97f (edwardtracey 2025-10-27 19:00:50 +0000) 12) # Instructions
88ffc97f (edwardtracey 2025-10-27 19:00:50 +0000) 13)
88ffc97f (edwardtracey 2025-10-27 19:00:50 +0000) 14) Make sure you have **git** installed on your machine. Also install **gitk**.
88ffc97f (edwardtracey 2025-10-27 19:00:50 +0000) 15)
88ffc97f (edwardtracey 2025-10-27 19:00:50 +0000) 16) To clone this repository to your local machine use the command
```

Clone

To clone a remote repository, use the `git clone <url>` command.

```
PS C:\> git clone https://github.com/EditaBuneviciene/AgileProject
Cloning into 'AgileProject'...
remote: Enumerating objects: 236, done.
remote: Counting objects: 100% (138/138), done.
remote: Compressing objects: 100% (108/108), done.
remote: Total 236 (delta 62), reused 78 (delta 28), pack-reused 98 (from 4)
Receiving objects: 100% (236/236), 39.38 MiB | 3.86 MiB/s, done.
Resolving deltas: 100% (93/93), done.
```

Branch

To create a branch, use the following command, with the name of the new branch

git branch <name of new branch>

Checkout

To jump onto the new branch, use the `checkout` command.

git checkout <name of branch to switch to>

Adding Files

To add the untracked files, the command **git add *** can be used to add all untracked files or the command **git add <filename>** can be used to add a specific file.

```
PS C:\Users\edwar\source\AgileProject\web> git add *
```

Committing Changes

To commit the newly added files we can use the `commit` command.

```
PS C:\Users\edwar\source\AgileProject\web> git commit -a -m "Added instructions to start a local server."
[feature-connect_user_login_pages 7872530] Added instructions to start a local server.
1 file changed, 16 insertions(+)
create mode 100644 web/local_server_setup_instructions.txt
```

Push

Because the newly added files and changes only exist locally, we need to push the changes to the remote repository using the *git push* command.

If the branch was created locally and does not yet exist on the remote repository, we can use the following command.

Git push -u origin <branch_name>

```
PS C:\Users\edwar\source\AgileProject\web> git push -u origin feature-connect_user_login_pages
Enumerating objects: 8, done.
Counting objects: 100% (8/8), done.
Delta compression using up to 6 threads
Compressing objects: 100% (7/7), done.
Writing objects: 100% (7/7), 3.12 KiB | 1.56 MiB/s, done.
Total 7 (delta 3), reused 0 (delta 0), pack-reused 0 (from 0)
remote: Resolving deltas: 100% (3/3), completed with 1 local object.
remote:
remote: Create a pull request for 'feature-connect_user_login_pages' on GitHub by visiting:
remote:   https://github.com/EditaBuneviciene/AgileProject/pull/new/feature-connect_user_login_pages
remote:
```

When further changes are made to the source code, they are committed and then pushed to the remote repository.

Diff

We can use *git diff* to view any changes that have been made to tracked files. We can then commit these changes and push to the remote.

Lines highlighted in red are the old text and lines highlighted in green are the new additions.

```
PS C:\Users\edwar\source\AgileProject\web> git diff
diff --git a/web/local_server_setup_instructions.txt b/web/local_server_setup_instructions.txt
index d9c98c9..c1079d4 100644
--- a/web/local_server_setup_instructions.txt
+++ b/web/local_server_setup_instructions.txt
@@ -13,4 +13,11 @@ How to run a local server.

- Open a browser and copy this link into the navigation bar:

- http://localhost:8000/login.html
\ No newline at end of file
+ http://localhost:8000/login.html
+
+
+Login details:
+
+ User email:      edwardtracey@gmail.com
+
+ User password:   password
\ No newline at end of file
PS C:\Users\edwar\source\AgileProject\web> git commit -a -m "Added user email and password details server setup instructions."
[feature-connect_user_login_pages 4a84c50] Added user email and password details to the server
tructions.
1 file changed, 8 insertions(+), 1 deletion(-)
PS C:\Users\edwar\source\AgileProject\web> git push
Enumerating objects: 7, done.
Counting objects: 100% (7/7), done.
Delta compression using up to 6 threads
Compressing objects: 100% (4/4), done.
Writing objects: 100% (4/4), 450 bytes | 450.00 KiB/s, done.
Total 4 (delta 3), reused 0 (delta 0), pack-reused 0 (from 0)
remote: Resolving deltas: 100% (3/3), completed with 3 local objects.
To https://github.com/EditaBuneviciene/AgileProject
7872530..4a84c50 feature-connect_user_login_pages -> feature-connect_user_login_pages
```

Git stashing

```

PS C:\Users\ebune\Desktop\AgileProject> git status
On branch edita
Untracked files:
  (use "git add <file>..." to include in what will be committed)
    sprint2/

nothing added to commit but untracked files present (use "git add" to track)
PS C:\Users\ebune\Desktop\AgileProject> git add .
PS C:\Users\ebune\Desktop\AgileProject> git stash
Saved working directory and index state WIP on edita: d87d370 updated code for series name.csv
PS C:\Users\ebune\Desktop\AgileProject> git status
On branch edita
nothing to commit, working tree clean
PS C:\Users\ebune\Desktop\AgileProject> git stash pop
On branch edita
Changes to be committed:
  (use "git restore --staged <file>..." to unstage)
    new file:   sprint2/cleaned_file.csv
    new file:   sprint2/mortality_rate.py

Dropped refs/stash@{0} (58cf28c0702b2e057efcb0a1d388ea84368985b1)
PS C:\Users\ebune\Desktop\AgileProject>

```

.gitignore used to ignore Data_Cleaned.csv file because everytime main.py runs, it creates this file.

```

PS C:\Users\ebune\Desktop\AgileProject> git status
On branch main
Your branch is up to date with 'origin/main'.

Untracked files:
  (use "git add <file>..." to include in what will be committed)
    Data_Cleaned.csv

nothing added to commit but untracked files present (use "git add" to track)
PS C:\Users\ebune\Desktop\AgileProject> git status
On branch main
Your branch is up to date with 'origin/main'.

Changes not staged for commit:
  (use "git add <file>..." to update what will be committed)
  (use "git restore <file>..." to discard changes in working directory)
    modified:   .gitignore

  (use "git restore <file>..." to discard changes in working directory)
    modified:   .gitignore

Dropped refs/stash@{0} (ff5a34eac10e87a86bd5fdbba9d23f443f711524)
PS C:\Users\ebune\Desktop\AgileProject> git commit -m "code for mortality from cancer"
[main d2cd66d] code for mortality from cancer
 1 file changed, 52 insertions(+)
 create mode 100644 sprint2/editascode/mortality_from_cancer.py
PS C:\Users\ebune\Desktop\AgileProject> git push
Enumerating objects: 7, done.
Counting objects: 100% (7/7), done.
Delta compression using up to 16 threads
Compressing objects: 100% (5/5), done.
Writing objects: 100% (5/5), 1.19 KiB | 1.19 MiB/s, done.
Total 5 (delta 1), reused 0 (delta 0), pack-reused 0
remote: Resolving deltas: 100% (1/1), completed with 1 local object.
To https://github.com/EditaBuneviciene/AgileProject.git
 818b853..d2cd66d main -> main
PS C:\Users\ebune\Desktop\AgileProject> git add .gitignore
PS C:\Users\ebune\Desktop\AgileProject> git commit -m "Update .gitignore"
[main 89a3804] Update .gitignore
 1 file changed, 2 insertions(+)
PS C:\Users\ebune\Desktop\AgileProject> git push
Enumerating objects: 5, done.
Counting objects: 100% (5/5), done.
Delta compression using up to 16 threads
Compressing objects: 100% (3/3), done.
Writing objects: 100% (3/3), 343 bytes | 343.00 KiB/s, done.
Total 3 (delta 2), reused 0 (delta 0), pack-reused 0
remote: Resolving deltas: 100% (2/2), completed with 2 local objects.
To https://github.com/EditaBuneviciene/AgileProject.git
 d2cd66d..89a3804 main -> main
PS C:\Users\ebune\Desktop\AgileProject>

```

Git merge used to merge into main from edita branch.

```
PS C:\Users\ebune\Desktop\AgileProject> git checkout main
Your branch is up to date with 'origin/main'.
PS C:\Users\ebune\Desktop\AgileProject> git merge edita
Merge made by the 'ort' strategy.
 Data_Cleaned.csv | 19513 ++++++++
 sprint2/edita_code/Data.csv | 23871 ++++++++
 sprint2/edita_code/cleaned_file.csv | 19369 ++++++++
 sprint2/edita_code/mortality_from_cancer.py | 51 +
 sprint2/edita_code/plots/mortality_cancer.png | Bin 0 -> 68947 bytes
 .../edita_code/plots/mortality_rate_comparison.png | Bin 0 -> 37368 bytes
 sprint2/edita_code/plots/not_implemented.png | Bin 0 -> 5223 bytes
 sprint2/mortality_from_cancer.py | 51 +
 8 files changed, 62855 insertions(+)
 create mode 100644 Data_Cleaned.csv
 create mode 100644 sprint2/edita_code/Data.csv
 create mode 100644 sprint2/edita_code/cleaned_file.csv
 create mode 100644 sprint2/edita_code/mortality_from_cancer.py
 create mode 100644 sprint2/edita_code/plots/mortality_cancer.png
 create mode 100644 sprint2/edita_code/plots/mortality_rate_comparison.png
 create mode 100644 sprint2/edita_code/plots/not_implemented.png
 create mode 100644 sprint2/mortality_from_cancer.py
PS C:\Users\ebune\Desktop\AgileProject> git status
On branch main
Your branch is ahead of 'origin/main' by 4 commits.
(use "git push" to publish your local commits)

Changes not staged for commit:
  (use "git add/rm <file>..." to update what will be committed)
  (use "git restore <file>..." to discard changes in working directory)
        deleted:    sprint2/plots/mortality_cancer.png
        deleted:    sprint2/plots/mortality_rate_comparison.png
        deleted:    sprint2/plots/not_implemented.png

no changes added to commit (use "git add" and/or "git commit -a")
PS C:\Users\ebune\Desktop\AgileProject> git commit -m "add code"
On branch main
Your branch is ahead of 'origin/main' by 4 commits.
(use "git push" to publish your local commits)
```

Checking for tags

```
nothing to commit, working tree clean
PS C:\Users\ebune\Desktop\AgileProject> git tag
v1.0.0
v2.0.0
```

Untracked file on the branch. Newly created.

```
PS C:\Users\ebune\Desktop\AgileProject> git status
On branch feature/mortality_rate
Untracked files:
  (use "git add <file>..." to include in what will be committed)
        sprint2/edita_code/e_main.py

nothing added to commit but untracked files present (use "git add" to track)
PS C:\Users\ebune\Desktop\AgileProject> █
```

Git relog to track orphaned files.

```

PS C:\Users\ebune\Desktop\AgileProject> git reflog
2710dba (HEAD -> feature/mortality_rate, origin/main, origin/HEAD, main) HEAD@{0}: checkout: moving from main to feature/mortality_rate
2710dba (HEAD -> feature/mortality_rate, origin/main, origin/HEAD, main) HEAD@{1}: checkout: moving from edita to main
24ce933 (origin/edita, edita) HEAD@{2}: checkout: moving from main to edita
2710dba (HEAD -> feature/mortality_rate, origin/main, origin/HEAD, main) HEAD@{3}: commit: nothing to be seen
8cb7b0f HEAD@{4}: commit: add code
b38af32 HEAD@{5}: merge edita: Merge made by the 'ort' strategy.
94e356f HEAD@{6}: checkout: moving from edita to main
24ce933 (origin/edita, edita) HEAD@{7}: commit: adding mortality from cancer code
3f495b7 HEAD@{8}: reset: moving to HEAD
3f495b7 HEAD@{9}: reset: moving to HEAD
3f495b7 HEAD@{10}: pull: Merge made by the 'ort' strategy.
9f4c4a5 HEAD@{11}: checkout: moving from main to edita
94e356f HEAD@{12}: commit: no changes to be seen
89a3804 HEAD@{13}: commit: Update .gitignore
d2cd66d HEAD@{14}: commit: code for mortality from cancer
818b853 (tag: v2.0.0, origin/feature/filter-trends-across-years) HEAD@{15}: reset: moving to HEAD
818b853 (tag: v2.0.0, origin/feature/filter-trends-across-years) HEAD@{16}: pull: Fast-forward
9426eec HEAD@{17}: checkout: moving from paddystand-ops-patch-1 to main
2c210d6 (origin/paddystand-ops-patch-1, paddystand-ops-patch-1) HEAD@{18}: checkout: moving from editaTest to paddystand-ops-patch-1
1a270cb (origin/editaTest, editaTest) HEAD@{19}: commit: updated README.md
150dee6 HEAD@{20}: commit: updated README.md
9426eec HEAD@{21}: checkout: moving from main to editaTest
9426eec HEAD@{22}: checkout: moving from edita to main
9f4c4a5 HEAD@{23}: checkout: moving from main to edita
9426eec HEAD@{24}: clone: from https://github.com/EditaBuneviciene/AgileProject.git

```

Git:

-feature branch

-stash

-conflict/conflict resolving

-merging

```

PS C:\Users\olcza\PycharmProjects\AgileProject> ls

Directory: C:\Users\olcza\PycharmProjects\AgileProject

Mode                LastWriteTime         Length Name
----                -
d-----          13/11/2025   13:16         .idea
d-----          12/11/2025   19:45        sprint1
d-----          12/11/2025   19:45        sprint2
d-----          12/11/2025   19:45        template
-a-----          12/11/2025   19:45          42 .gitignore
-a-----          12/11/2025   19:45    4492459 cleaned_file.csv
-a-----          12/11/2025   19:45    5137647 Data.csv
-a-----          12/11/2025   19:45       1964 README.md
-a-----          12/11/2025   19:45       6728 unique_series_names.csv

PS C:\Users\olcza\PycharmProjects\AgileProject> git status
On branch main
Your branch is up to date with 'origin/main'.

nothing to commit, working tree clean

PS C:\Users\olcza\PycharmProjects\AgileProject> git log
commit 295df1f87719985ca3210ba03be024f75b07 (HEAD -> main, origin/main, origin/HEAD)
Author: Dariusz Olczak <olczakdariusz213@gmail.com>
Date:   Wed Nov 12 18:27:03 2025 +0000

    Added .gitignore file to exclude unwanted file tracking

commit 034d914a1d9c9235a982311ebe012148e40e6978
Author: paddystand <paddystand@gmail.com>
Date:   Wed Nov 13 00:11:11 2025 +0000

```

Creating branch feature/filter-columns

```

commit 034d9141d9c9235a982311e012148e46e6978
Author: paddystand-ops <paddystand@gmail.com>
Date: Wed Nov 12 00:21:33 2025 +0000
PS C:\Users\olca\PycharmProjects\AgileProject> git branch -a
* main
  remotes/origin/HEAD -> origin/main
  remotes/origin/dariusz
  remotes/origin/edit_user_details
  remotes/origin/edita
  remotes/origin/main
  remotes/origin/paddystand-ops-patch-1
PS C:\Users\olca\PycharmProjects\AgileProject> git status
On branch main
Your branch is up to date with 'origin/main'.

nothing to commit, working tree clean
PS C:\Users\olca\PycharmProjects\AgileProject> git remote
origin
PS C:\Users\olca\PycharmProjects\AgileProject> git remote -v
origin https://github.com/EditaBuneviciene/AgileProject.git (fetch)
origin https://github.com/EditaBuneviciene/AgileProject.git (push)
PS C:\Users\olca\PycharmProjects\AgileProject>

eProject > README.md 1:1 CRLF UTF-8 4 spaces Python 3.14

PS C:\Users\olca\PycharmProjects\AgileProject> git push -u origin feature/filter-columns
info: please complete authentication in your browser...
Total 0 (delta 0), reused 0 (delta 0), pack-reused 0 (from 0)
remote:
remote: Create a pull request for 'feature/filter-columns' on GitHub by visiting:
remote: https://github.com/EditaBuneviciene/AgileProject/pull/new/feature/filter-columns
remote:
To https://github.com/EditaBuneviciene/AgileProject.git
 * [new branch] feature/filter-columns -> feature/filter-columns
branch 'feature/filter-columns' set up to track 'origin/feature/filter-columns'.
PS C:\Users\olca\PycharmProjects\AgileProject>

```


Creating branch dariusz off the branch feature

```

PS C:\Users\olca\PycharmProjects\AgileProject> git branch -a
* feature/filter-columns
  main
  remotes/origin/feature/filter-columns
  remotes/origin/main
PS C:\Users\olca\PycharmProjects\AgileProject> git checkout -b dariusz
Switched to a new branch 'dariusz'
PS C:\Users\olca\PycharmProjects\AgileProject>

eProject > sprint1 > cleanCSVand_corr > cleanCSV.py 1:1 CRLF UTF-8 4 spaces Python 3.14

```

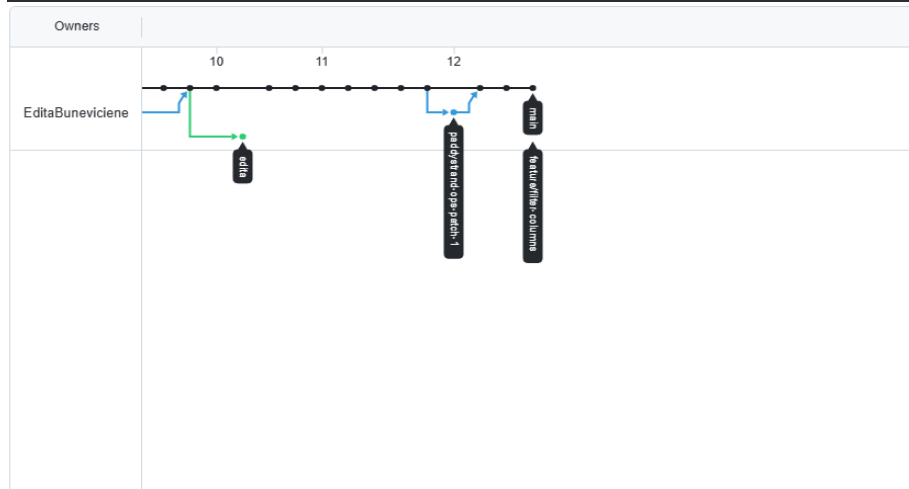

Stashing:

```

PS C:\Users\olca\PycharmProjects\AgileProject> git status
On branch dariusz
nothing to commit, working tree clean
PS C:\Users\olca\PycharmProjects\AgileProject> git stash push -u -m "Feature. FilterSerie, Coutries and Years Columns"
No local changes to save
PS C:\Users\olca\PycharmProjects\AgileProject> git status
On branch dariusz
nothing to commit, working tree clean
PS C:\Users\olca\PycharmProjects\AgileProject> git stash list
stash@{0}: On dariusz: Feature. Filter Series Counties and years columns
PS C:\Users\olca\PycharmProjects\AgileProject>

```

```

PS C:\Users\olcza\PycharmProjects\AgileProject> git stash pop
On branch dariusz
Changes to be committed:
  (use "git restore --staged <file>..." to unstage)
    new file:   sprint2/Data.csv
    new file:   sprint2/filter_columns.py

Untracked files:
  (use "git add <file>..." to include in what will be committed)
    sprint2/Data_Cleaned.csv

Dropped refs/stash@{0} (4847671b3c2287fdbc1cfc3ccee2b0e85012607)
PS C:\Users\olcza\PycharmProjects\AgileProject> git status
On branch dariusz
Changes to be committed:
  (use "git restore --staged <file>..." to unstage)
    new file:   sprint2/Data.csv
    new file:   sprint2/filter_columns.py

Untracked files:
  (use "git add <file>..." to include in what will be committed)
    sprint2/Data_Cleaned.csv

PS C:\Users\olcza\PycharmProjects\AgileProject> git add sprint2/filter_columns.py sprint2/Data_Cleaned.csv
PS C:\Users\olcza\PycharmProjects\AgileProject> git commit -m "feature, update filter columns and add cleaned dataset"
[dariusz f83d093] feature, update filter columns and add cleaned dataset
 3 files changed, 43670 insertions(+)
 create mode 100644 sprint2/Data.csv
 create mode 100644 sprint2/Data_Cleaned.csv
 create mode 100644 sprint2/filter_columns.py

```

A conflict in .gitignore file on branch dariusz happened and had to be resolved by removing three lines to resolve conflict

```

PS C:\Users\olcza\PycharmProjects\AgileProject> git push origin dariusz
To https://github.com/EditaBuneviciene/AgileProject.git
 ! [rejected]        dariusz -> dariusz (non-fast-forward)
error: failed to push some refs to 'https://github.com/EditaBuneviciene/AgileProject.git'
hint: Updates were rejected because the tip of your current branch is behind
hint: its remote counterpart. If you want to integrate the remote changes,
hint: use 'git pull' before pushing again.
hint: See the 'Note about fast-forwards' in 'git push --help' for details.
PS C:\Users\olcza\PycharmProjects\AgileProject> git pull origin dariusz
From https://github.com/EditaBuneviciene/AgileProject
 * branch      dariusz      -> FETCH_HEAD
 * [new branch] dariusz      -> origin/dariusz
Auto-merging .gitignore
CONFLICT (add/add): Merge conflict in .gitignore
CONFLICT (file location): cleanCSVand_corr/Data.csv added in f86b95e9a0fd1044b59a28b3bf94f967af395ecf inside a directory that was renamed in HEAD.
solving it should perhaps be moved to sprint1/cleanCSVand_corr/Data.csv.
CONFLICT (file location): cleanCSVand_corr/Data_Cleaned.csv added in f86b95e9a0fd1044b59a28b3bf94f967af395ecf inside a directory that was renamed in HEAD.
solving it should perhaps be moved to sprint1/cleanCSVand_corr/Data_Cleaned.csv.
CONFLICT (file location): cleanCSVand_corr/cleaned_file.csv added in f86b95e9a0fd1044b59a28b3bf94f967af395ecf inside a directory that was renamed in HEAD.
solving it should perhaps be moved to sprint1/cleanCSVand_corr/cleaned_file.csv.
CONFLICT (file location): cleanCSVand_corr/dariusz.py added in f86b95e9a0fd1044b59a28b3bf94f967af395ecf inside a directory that was renamed in HEAD.
solving it should perhaps be moved to sprint1/cleanCSVand_corr/dariusz.py.
Automatic merge failed; fix conflicts and then commit the result.
PS C:\Users\olcza\PycharmProjects\AgileProject> git status
On branch dariusz
You have unmerged paths.
  (fix conflicts and run "git commit")
  (use "git merge --abort" to abort the merge)

Changes to be committed:
  new file:   requirements.txt

Unmerged paths:
  (use "git add <file>..." to mark resolution)
    both added:      .gitignore
    added by them:   sprint1/cleanCSVand_corr/Data.csv
    added by them:   sprint1/cleanCSVand_corr/Data_Cleaned.csv
    added by them:   sprint1/cleanCSVand_corr/cleaned_file.csv
    added by them:   sprint1/cleanCSVand_corr/dariusz.py

```

```

File has unresolved merge conflicts
1 <<<<<< HEAD
2
3 .idea/
4 ..pycache__/
5 *.pyc
6 venv/
7 .env
8 =====
9 .venv/
10 venv/
11 .idea/
12 ..pycache__/
13 *.pyc
14 .env
15
16 # Enhanced Python ignores
17 *.py[co]d
18 +$.py.class
19 *.so
20 .Python
21 build/
22 dist/
23 *.egg-info/
24 .egg
25
26 >>>>>> f86b95e9af8d1844b59a28b3bf4f967af395ecf

```

```

File has unresolved merge conflicts
1
2 .idea/
3 ..pycache__/
4 *.pyc
5 venv/
6 .env
7
8 .venv/
9 venv/
10 .idea/
11 ..pycache__/
12 *.pyc
13 .env
14
15 # Enhanced Python ignores
16 *.py[co]d
17 +$.py.class
18 *.so
19 .Python
20 build/
21 dist/
22 *.egg-info/
23 .egg
24
25
26

```

Pushing to changes to branch dariusz

```

PS C:\Users\olcza\PycharmProjects\AgileProject> git commit -m ".gitignore conflict. Resolved by removing three lines"
[dariusz 9426eec] .gitignore conflict. Resolved by removing three lines
PS C:\Users\olcza\PycharmProjects\AgileProject> git push origin dariusz
Enumerating objects: 21, done.
Counting objects: 100% (21/21), done.
Delta compression using up to 12 threads
Compressing objects: 100% (14/14), done.
Writing objects: 100% (14/14), 3.27 MiB | 847.00 KiB/s, done.
Total 14 (delta 5), reused 3 (delta 0), pack-reused 0 (from 0)
remote: Resolving deltas: 100% (5/5), completed with 3 local objects.
To https://github.com/EditaBuneviciene/AgileProject.git
   f86b95e..9426eec  dariusz -> dariusz
PS C:\Users\olcza\PycharmProjects\AgileProject>

```

Pulling current version from branch feature/filter-columns

```

PS C:\Users\olcza\PycharmProjects\AgileProject> git pull origin feature/filter-columns
From https://github.com/EditaBuneviciene/AgileProject
 * branch          feature/filter-columns -> FETCH_HEAD
Already up to date.
PS C:\Users\olcza\PycharmProjects\AgileProject> git merge dariusz
Updating 295df1f..9426eec
Fast-forward
 .gitignore                | 20 +
 requirements.txt           | 7 +
 sprint1/cleanCSVand_corr/Data.csv | 23871 ++++++
 sprint1/cleanCSVand_corr/Data_Cleaned.csv | 19328 ++++++
 sprint1/cleanCSVand_corr/cleaned_file.csv | 19369 ++++++
 sprint1/cleanCSVand_corr/dariusz.py | 96 +
 sprint2/Data.csv           | 23871 ++++++
 sprint2/Data_Cleaned.csv   | 19513 ++++++
 sprint2/filter_columns.py  | 292 +
 9 files changed, 106367 insertions(+)
 create mode 100644 requirements.txt
 create mode 100644 sprint1/cleanCSVand_corr/Data.csv
 create mode 100644 sprint1/cleanCSVand_corr/Data_Cleaned.csv
 create mode 100644 sprint1/cleanCSVand_corr/cleaned_file.csv
 create mode 100644 sprint1/cleanCSVand_corr/dariusz.py
 create mode 100644 sprint2/Data.csv
 create mode 100644 sprint2/Data_Cleaned.csv
 create mode 100644 sprint2/filter_columns.py
PS C:\Users\olcza\PycharmProjects\AgileProject>


```

Merging feature branch with main branch

```

PS C:\Users\olcza\PycharmProjects\AgileProject> git push origin feature/filter-columns
Total 0 (delta 0), reused 0 (delta 0), pack-reused 0 (from 0)
To https://github.com/EditaBuneviciene/AgileProject.git
 295df1f..9426eec feature/filter-columns -> feature/filter-columns
PS C:\Users\olcza\PycharmProjects\AgileProject> git checkout main
Switched to branch 'main'
PS C:\Users\olcza\PycharmProjects\AgileProject> git pull origin main
From https://github.com/EditaBuneviciene/AgileProject
 * branch      main      -> FETCH_HEAD
Already up to date.
PS C:\Users\olcza\PycharmProjects\AgileProject> git merge feature/filter-columns
Updating 295df1f..9426eec
Fast-forward
 .gitignore                  | 20 +
 requirements.txt            | 7 +
 sprint1/cleanCSVand_corr/Data.csv | 23871 ++++++
 sprint1/cleanCSVand_corr/Data_Cleaned.csv | 19328 ++++++
 sprint1/cleanCSVand_corr/cleaned_file.csv | 19369 ++++++
 sprint1/cleanCSVand_corr/dariusz.py | 96 +
 sprint2/Data.csv            | 23871 ++++++
 sprint2/Data_Cleaned.csv    | 19513 ++++++
 sprint2/filter_columns.py    | 292 +
 9 files changed, 106367 insertions(+)
 create mode 100644 requirements.txt
 create mode 100644 sprint1/cleanCSVand_corr/Data.csv
 create mode 100644 sprint1/cleanCSVand_corr/Data_Cleaned.csv
 create mode 100644 sprint1/cleanCSVand_corr/cleaned_file.csv
 create mode 100644 sprint1/cleanCSVand_corr/dariusz.py
 create mode 100644 sprint2/Data.csv
 create mode 100644 sprint2/Data_Cleaned.csv
 create mode 100644 sprint2/filter_columns.py
PS C:\Users\olcza\PycharmProjects\AgileProject> git push origin main
Total 0 (delta 0), reused 0 (delta 0), pack-reused 0 (from 0)
To https://github.com/EditaBuneviciene/AgileProject.git
 295df1f..9426eec main -> main
PS C:\Users\olcza\PycharmProjects\AgileProject>

```

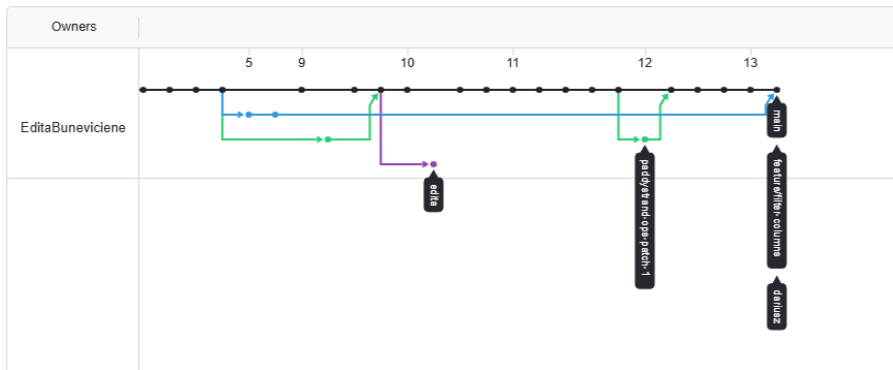


Removing dariusz branch and feature branch as no longer need:

```

PS C:\Users\olcza\PycharmProjects\AgileProject> git branch -a
dariusz
feature/filter-columns
* main
remotes/origin/dariusz
remotes/origin/feature/filter-columns
remotes/origin/main
PS C:\Users\olcza\PycharmProjects\AgileProject> git branch -d dariusz
Deleted branch dariusz (was 9426eec).
PS C:\Users\olcza\PycharmProjects\AgileProject> git branch -d feature/filter-columns
Deleted branch feature/filter-columns (was 9426eec).
PS C:\Users\olcza\PycharmProjects\AgileProject> git push origin --delete dariusz
To https://github.com/EditaBuneviciene/AgileProject.git
- [deleted] dariusz
PS C:\Users\olcza\PycharmProjects\AgileProject> git push origin --delete feature/filter-columns
To https://github.com/EditaBuneviciene/AgileProject.git
- [deleted] feature/filter-columns
PS C:\Users\olcza\PycharmProjects\AgileProject>

```

Git checking branch and log:

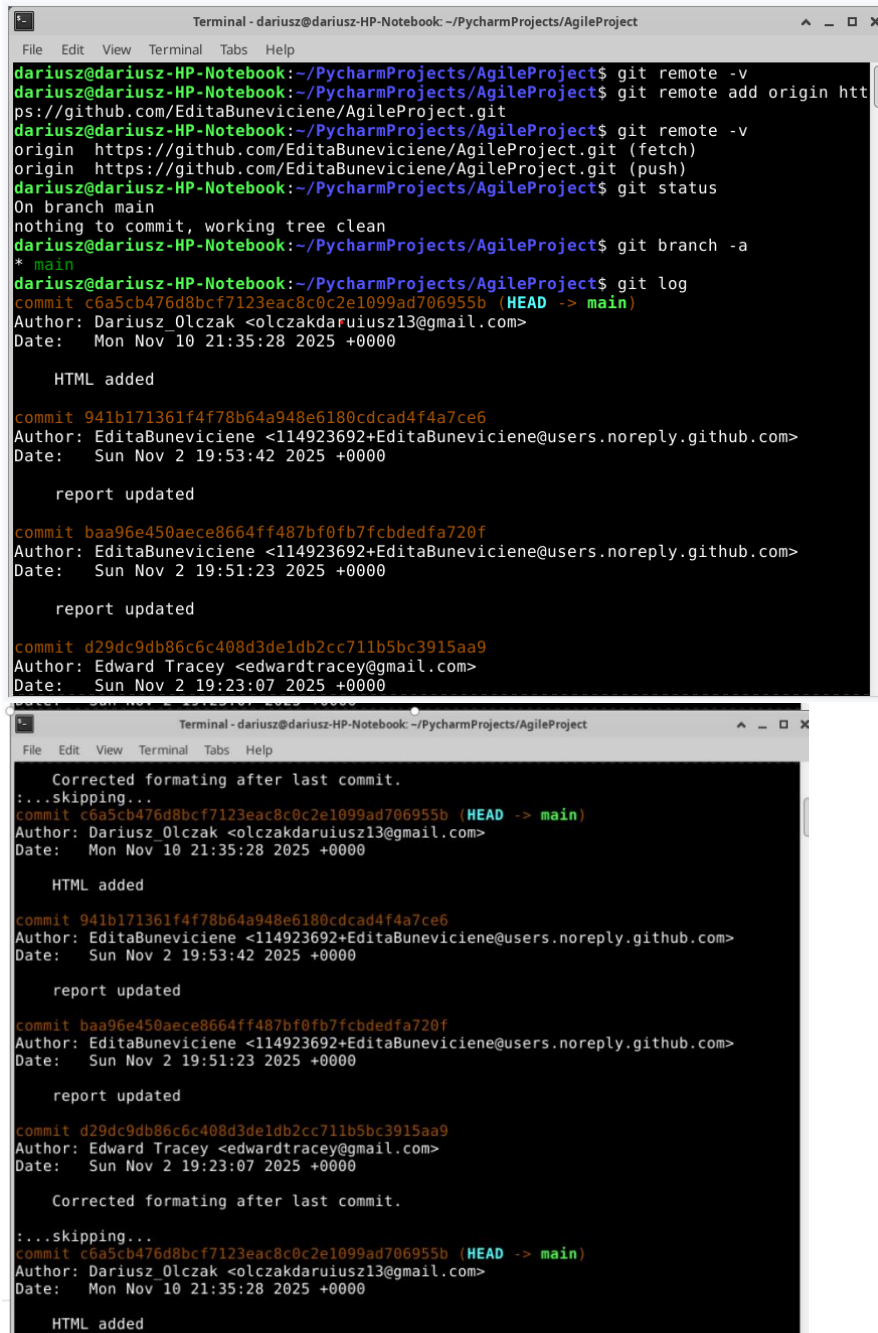

```

Terminal - dariusz@dariusz-HP-Notebook: ~/PycharmProjects/AgileProject
File Edit View Terminal Tabs Help

dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git remote -v
dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git remote add origin https://github.com/EditaBuneviciene/AgileProject.git
dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git remote -v
origin https://github.com/EditaBuneviciene/AgileProject.git (fetch)
origin https://github.com/EditaBuneviciene/AgileProject.git (push)
dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git status
On branch main
nothing to commit, working tree clean
dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git branch -a
* main
dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git log
commit c6a5cb476d8bcf7123eac8c0c2e1099ad706955b (HEAD -> main)
Author: Dariusz Olczak <olczakdariusz13@gmail.com>
Date: Mon Nov 10 21:35:28 2025 +0000

    HTML added

commit 941b171361f4f78b64a948e6180cdcad4f4a7ce6
Author: EditaBuneviciene <114923692+EditaBuneviciene@users.noreply.github.com>
Date: Sun Nov 2 19:53:42 2025 +0000

    report updated

commit baa96e450aece8664ff487bf0fb7fcbddedfa720f
Author: EditaBuneviciene <114923692+EditaBuneviciene@users.noreply.github.com>
Date: Sun Nov 2 19:51:23 2025 +0000

    report updated

commit d29dc9db86c6c408d3de1db2cc711b5bc3915aa9
Author: Edward Tracey <edwardtracey@gmail.com>
Date: Sun Nov 2 19:23:07 2025 +0000

    report updated

Corrected formatting after last commit.
...skipping...
commit c6a5cb476d8bcf7123eac8c0c2e1099ad706955b (HEAD -> main)
Author: Dariusz Olczak <olczakdariusz13@gmail.com>
Date: Mon Nov 10 21:35:28 2025 +0000

    HTML added

commit 941b171361f4f78b64a948e6180cdcad4f4a7ce6
Author: EditaBuneviciene <114923692+EditaBuneviciene@users.noreply.github.com>
Date: Sun Nov 2 19:53:42 2025 +0000

    report updated

commit baa96e450aece8664ff487bf0fb7fcbddedfa720f
Author: EditaBuneviciene <114923692+EditaBuneviciene@users.noreply.github.com>
Date: Sun Nov 2 19:51:23 2025 +0000

    report updated

commit d29dc9db86c6c408d3de1db2cc711b5bc3915aa9
Author: Edward Tracey <edwardtracey@gmail.com>
Date: Sun Nov 2 19:23:07 2025 +0000


    report updated

Corrected formatting after last commit.
...skipping...
commit c6a5cb476d8bcf7123eac8c0c2e1099ad706955b (HEAD -> main)
Author: Dariusz Olczak <olczakdariusz13@gmail.com>
Date: Mon Nov 10 21:35:28 2025 +0000

    HTML added

```

Merging:

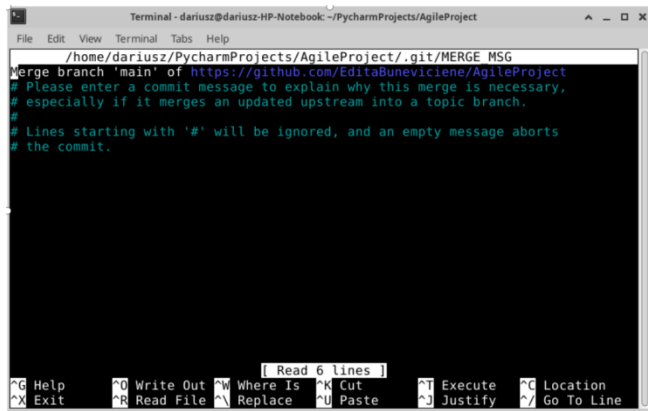

Pulling latest changes:

```
(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git pull health_i main
remote: Enumerating objects: 38, done.
remote: Counting objects: 100% (38/38), done.
remote: Compressing objects: 100% (21/21), done.
remote: Total 30 (delta 17), reused 21 (delta 9), pack-reused 0 (from 0)
Unpacking objects: 100% (30/30), 2.19 MiB | 1.49 MiB/s, done.
From https://github.com/EditaBuneviciene/AgileProject
* branch          main      -> FETCH_HEAD
  295df1f..01e6fac  main      -> health_i/main
Updating 295df1f..01e6fac
Fast-forward
 .gitignore          | 20 +
 README.md           | 9 +-
 requirements.txt     | 7 +
```

```
  295df1f..01e6fac  main      -> health_i/main
Updating 295df1f..01e6fac
Fast-forward
 .gitignore          | 20 +
 README.md           | 9 +-
 requirements.txt     | 7 +
 sprint1/cleanSVand_corr/Data.csv | 23871 +
 sprint1/cleanSVand_corr/Data_Cleaned.csv | 19328 +
 sprint1/cleanSVand_corr/Cleaned_file.csv | 19369 +
 sprint1/cleanSVand_corr/dariusz.py | 96 +
 sprint2/Data.csv     | 23871 +
 sprint2/Data_Cleaned.csv | 19513 +
 sprint2/filter_columns.py | 292 +
 18 files changed, 186372 insertions(+), 4 deletions(-)
 create mode 100644 requirements.txt
 create mode 100644 sprint1/cleanSVand_corr/Data.csv
 create mode 100644 sprint1/cleanSVand_corr/Data_Cleaned.csv
 create mode 100644 sprint1/cleanSVand_corr/Cleaned_file.csv
 create mode 100644 sprint1/cleanSVand_corr/dariusz.py
 create mode 100644 sprint2/Data.csv
 create mode 100644 sprint2/Data_Cleaned.csv
 create mode 100644 sprint2/filter_columns.py

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git status
On branch main
Your branch is up to date with 'health_i/main'.

nothing to commit, working tree clean

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git checkout main
Already on 'main'
Your branch is up to date with 'health_i/main'.

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git checkout -b feature/filter-trends-across-years
```

Creating feature branch and developer branch out of feature branch:

```
(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git checkout main
Already on 'main'
Your branch is up to date with 'health_i/main'.

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git checkout -b feature/filter-trends-across-years
Switched to a new branch 'feature/filter-trends-across-years'

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git checkout -b edita
Switched to a new branch 'edita'
```

Pushing latest commit from main to feature branch:

```
(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git push -u health_i feature/filter-trends-across-years
Username for 'https://github.com': Dariusz0lczak
Password for 'https://Dariusz0lczak@github.com':
Total 0 (delta 0), reused 0 (delta 0), pack-reused 0
remote:
remote: Create a pull request for 'feature/filter-trends-across-years' on GitHub by visiting:
remote:   https://github.com/EditaBuneviciene/AgileProject/pull/new/feature/filter-trends-across-years
remote:
To https://github.com/EditaBuneviciene/AgileProject.git
 * [new branch]   feature/filter-trends-across-years -> feature/filter-trends-across-years
branch 'feature/filter-trends-across-years' set up to track 'health_i/feature/filter-trends-across-years'.
```

Creating feature branch and developer branch out of feature branch:

```
(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git checkout main
Already on 'main'
Your branch is up to date with 'health_i/main'.

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git checkout -b feature/filter-trends-across-years
Switched to a new branch 'feature/filter-trends-across-years'

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git checkout -b edita
Switched to a new branch 'edita'
```

Pushing latest commit from main to feature branch:

```
(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git push -u health_i feature/filter-trends-across-years
Username for 'https://github.com': Dariusz0lczak
Password for 'https://Dariusz0lczak@github.com':
Total 0 (delta 0), reused 0 (delta 0), pack-reused 0
remote:
remote: Create a pull request for 'feature/filter-trends-across-years' on GitHub by visiting:
remote:   https://github.com/EditaBuneviciene/AgileProject/pull/new/feature/filter-trends-across-years
remote:
To https://github.com/EditaBuneviciene/AgileProject.git
 * [new branch]   feature/filter-trends-across-years -> feature/filter-trends-across-years
branch 'feature/filter-trends-across-years' set up to track 'health_i/feature/filter-trends-across-years'.
```

Switching to feature branch and developer branch to commit changes:

```
(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git checkout feature/filter-trends-across-years
Switched to branch 'feature/filter-trends-across-years'
Your branch is up to date with 'health_i/feature/filter-trends-across-years'.

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git checkout -b edita
Switched to a new branch 'edita'

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git push -u health_i edita
Username for 'https://github.com': Dariusz0lczak
Password for 'https://Dariusz0lczak@github.com':
Total 0 (delta 0), reused 0 (delta 0), pack-reused 0
remote:
remote: Create a pull request for 'edita' on GitHub by visiting:
remote:   https://github.com/EditaBuneviciene/AgileProject/pull/new/edita
remote:
To https://github.com/EditaBuneviciene/AgileProject.git
 * [new branch]   edita -> edita

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git status
On branch edita
Your branch is up to date with 'health_i/edita'.

Changes to be committed:
  (use "git restore --staged <file>..." to unstage)
    new file:   sprint2/Mortality rate.py
    new file:   sprint2/main.py
    new file:   sprint2/mortality from cancer.py
    new file:   sprint2/plots/mortality_cancer.png
    new file:   sprint2/plots/mortality_rate_comparison.png
    new file:   sprint2/plots/not_implemented.png

Changes not staged for commit:
  (use "git add <file>..." to update what will be committed)
  (use "git restore <file>..." to discard changes in working directory)
    modified:   requirements.txt
    modified:   sprint1/cleanCSVand_corr/correlation.py
    modified:   sprint2/Mortality rate.py
    modified:   sprint2/main.py
    modified:   sprint2/mortality from cancer.py
```

Committing changes:

```
(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git push health_i feature/filter-trends-across-years
Username for 'https://github.com': Dariusz0lczak
Password for 'https://Dariusz0lczak@github.com':
remote: Invalid username or token. Password authentication is not supported for Git operations.
fatal: Authentication failed for 'https://github.com/EditaBuneviciene/AgileProject.git/'

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git push health_i feature/filter-trends-across-years
Username for 'https://github.com': Dariusz0lczak
Password for 'https://Dariusz0lczak@github.com':
Total 0 (delta 0), reused 0 (delta 0), pack-reused 0
To https://github.com/EditaBuneviciene/AgileProject.git
  01e6fac..670442d  feature/filter-trends-across-years -> feature/filter-trends-across-years

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$
```

```
(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git add .

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git push health_i edita
Username for 'https://github.com': Dariusz0lczak
Password for 'https://Dariusz0lczak@github.com':
Enumerating objects: 20, done.
Counting objects: 100% (20/20), done.
Delta compression using up to 4 threads
Compressing objects: 100% (14/14), done.
Writing objects: 100% (14/14), 103.17 KiB | 2.79 MiB/s, done.
Total 14 (delta 6), reused 0 (delta 0), pack-reused 0
remote: Resolving deltas: 100% (6/6), completed with 6 local objects.
To https://github.com/EditaBuneviciene/AgileProject.git
  01e6fac..670442d  edita -> edita

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git checkout feature/filter-trends-across-years
Switched to branch 'feature/filter-trends-across-years'
Your branch is up to date with 'health_i/feature/filter-trends-across-years'.

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git pull health_i feature/filter-trends-across-years
From https://github.com/EditaBuneviciene/AgileProject
 * branch                feature/filter-trends-across-years -> FETCH_HEAD
Already up to date.

create mode 100644 sprint2/Mortality rate.py
create mode 100644 sprint2/main.py
create mode 100644 sprint2/mortality from cancer.py
create mode 100644 sprint2/plots/mortality_cancer.png
create mode 100644 sprint2/plots/mortality_rate_comparison.png
create mode 100644 sprint2/plots/not_implemented.png
```

```
(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git push health_i edita
Username for 'https://github.com': Dariusz0lczak
Password for 'https://Dariusz0lczak@github.com':
Enumerating objects: 20, done.
Counting objects: 100% (20/20), done.
Delta compression using up to 4 threads
Compressing objects: 100% (14/14), done.
Writing objects: 100% (14/14), 103.17 KiB | 2.79 MiB/s, done.
Total 14 (delta 6), reused 0 (delta 0), pack-reused 0
remote: Resolving deltas: 100% (6/6), completed with 6 local objects.
To https://github.com/EditaBuneviciene/AgileProject.git
  01e6fac..670442d  edita -> edita
```

Merging Feature Branch

```
(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git checkout feature/filter-trends-across-years
Switched to branch 'feature/filter-trends-across-years'
Your branch is up to date with 'health_i/feature/filter-trends-across-years'.

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git pull health_i feature/filter-trends-across-years
From https://github.com/EditaBuneviciene/AgileProject
 * branch                feature/filter-trends-across-years -> FETCH_HEAD
Already up to date.

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git merge edita
Updating 01e6fac..670442d
Fast-forward
 requirements.txt          | 2 ++
 sprint1/cleanCSVand_corr/correlation.py | 2 ++
 sprint2/Mortality rate.py | 69 +++++
 sprint2/main.py           | 49 +++++
 sprint2/mortality from cancer.py | 53 +++++
 sprint2/plots/mortality_cancer.png | Bin 0 -> 68947 bytes
 sprint2/plots/mortality_rate_comparison.png | Bin 0 -> 37368 bytes
 sprint2/plots/not_implemented.png | Bin 0 -> 5223 bytes
 8 files changed, 174 insertions(+), 1 deletion(-)
 create mode 100644 sprint2/Mortality rate.py
 create mode 100644 sprint2/main.py
 create mode 100644 sprint2/mortality from cancer.py
 create mode 100644 sprint2/plots/mortality_cancer.png
 create mode 100644 sprint2/plots/mortality_rate_comparison.png
 create mode 100644 sprint2/plots/not_implemented.png
```

Pushing next improved changes

```
(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git branch
dariusz
* edita
  edita-backup
  feature/filter-trends-across-years
  main
  vv

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git add .

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git commit -m "edita: improved filter trends across years"
[edita 4837f28] edita: improved filter trends across years
5 files changed, 280 insertions(+), 516 deletions(-)
delete mode 100644 sprint2/Mortality rate.py
delete mode 100644 sprint2/filter_columns.py
delete mode 100644 sprint2/mortality from cancer.py
delete mode 100644 sprint2/mortality_rate.py

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git push health_1 edita
Username for 'https://github.com': Dariusz0lczak
Password for 'https://Dariusz0lczak@github.com':
Enumerating objects: 7, done.
Counting objects: 100% (7/7), done.
Delta compression using up to 4 threads
Compressing objects: 100% (4/4), done.
Writing objects: 100% (4/4), 3.35 MiB | 1.67 MiB/s, done.
Total 4 (delta 2), reused 0 (delta 0), pack-reused 0
remote: Resolving deltas: 100% (2/2), completed with 2 local objects.
To https://github.com/EditaBuneviciene/AgileProject.git
 670442d..4837f28  edita -> edita
```

Creating second dev branch off feature branch

```
(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git status
On branch feature/filter-trends-across-years
Your branch is up to date with 'health_1/feature/filter-trends-across-years'.

nothing to commit, working tree clean

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git checkout -b dariusz
Switched to a new branch 'dariusz'

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git push -u health_1 dariusz
Username for 'https://github.com': Dariusz0lczak
Password for 'https://Dariusz0lczak@github.com':
Total 0 (delta 0), reused 0 (delta 0), pack-reused 0
remote:
remote: Create a pull request for 'dariusz' on GitHub by visiting:
remote:   https://github.com/EditaBuneviciene/AgileProject/pull/new/dariusz
remote:
To https://github.com/EditaBuneviciene/AgileProject.git
 * [new branch]   dariusz -> dariusz
branch 'dariusz' set up to track 'health_1/dariusz'.

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$
```

Merging changes with feature branch

```
(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git checkout feature/filter-trends-across-years
Switched to branch 'feature/filter-trends-across-years'
Your branch is up to date with 'health_1/feature/filter-trends-across-years'.

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git pull health_1 feature/filter-trends-across-years
From https://github.com/EditaBuneviciene/AgileProject
 * branch      feature/filter-trends-across-years -> FETCH_HEAD
Already up to date.

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git merge edita
Updating 670442d..4837f28
Fast-forward
 sprint2/Mortality rate.py      | 69 -----
 sprint2/filter_columns.py     | 292 -----
 sprint2/main.py               | 316 -----
 sprint2/mortality from cancer.py | 53 -----
 sprint2/mortality_rate.py     | 66 -----
 5 files changed, 280 insertions(+), 516 deletions(-)
 delete mode 100644 sprint2/Mortality rate.py
 delete mode 100644 sprint2/filter_columns.py
 delete mode 100644 sprint2/mortality from cancer.py
 delete mode 100644 sprint2/mortality_rate.py

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git push health_1 feature/filter-trends-across-years
Username for 'https://github.com': Dariusz0lczak
Password for 'https://Dariusz0lczak@github.com':
Total 0 (delta 0), reused 0 (delta 0), pack-reused 0
To https://github.com/EditaBuneviciene/AgileProject.git
 670442d..4837f28  feature/filter-trends-across-years -> feature/filter-trends-across-years
```

Making changes to wrong branch and stashing work to move to correct branch

```
(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git push health_1 feature/filter-trends-across-years
Username for 'https://github.com': Dariusz0lczak
Password for 'https://Dariusz0lczak@github.com':
Total 0 (delta 0), reused 0 (delta 0), pack-reused 0
To https://github.com/Edita8unovicicna/AgileProject.git
 670442d..4837428 feature/filter-trends-across-years -> feature/filter-trends-across-years

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git status
On branch feature/filter-trends-across-years
Your branch is up to date with 'health_1/feature/filter-trends-across-years'.

nothing to commit, working tree clean

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git branch
dariusz
edita
edita-backup
* feature/filter-trends-across-years
main
vv

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git checkout dariusz
error: Your local changes to the following files would be overwritten by checkout:
  sprint2/main.py
Please commit your changes or stash them before you switch branches.
Aborting
```

```
(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git stash push -u -m "my uncommitted feature work"
Saved working directory and index state On feature/filter-trends-across-years: my uncommitted feature work

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git status
On branch feature/filter-trends-across-years
Your branch is up to date with 'health_1/feature/filter-trends-across-years'.

nothing to commit, working tree clean

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git reset --hard
HEAD is now at 4837428 edita: improved filter trends across years

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git status
On branch feature/filter-trends-across-years
Your branch is up to date with 'health_1/feature/filter-trends-across-years'.

nothing to commit, working tree clean

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git checkout dariusz
Switched to branch 'dariusz'
Your branch is up to date with 'health_1/dariusz'.
```

Retrieving stash

```
(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git stash pop
Auto-merging sprint2/main.py
CONFLICT (content): Merge conflict in sprint2/main.py
sprint2/Data.csv already exists, no checkout
sprint2/Data_Cleaned.csv already exists, no checkout
error: could not restore untracked files from stash
On branch dariusz
Your branch is up to date with 'health_1/dariusz'.

Changes to be committed:
  (use "git restore --staged <file>..." to unstage)
    deleted:   sprint2/cleaned_file.csv

Unmerged paths:
  (use "git restore --staged <file>..." to unstage)
  (use "git add <file>..." to mark resolution)
    both modified: sprint2/main.py

The stash entry is kept in case you need it again.
```

```
(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git merge dariusz
Auto-merging sprint2/main.py
CONFLICT (content): Merge conflict in sprint2/main.py
Automatic merge failed; fix conflicts and then commit the result.

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git branch
dariusz
edita
edita-backup
* feature/filter-trends-across-years
main
vv

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git checkout feature/filter-trends-across-years
D      sprint2/Data.csv
D      sprint2/Data_Cleaned.csv
D      sprint2/cleaned_file.csv
M      sprint2/main.py
Already on 'feature/filter-trends-across-years'
Your branch is up to date with 'health_1/feature/filter-trends-across-years'.

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git checkout dariusz -- sprint2/main.py

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git add sprint2/main.py

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git commit -m "feature: restore improved main.py"
(feature/filter-trends-across-years 818b853) feature: restore improved main.py
4 files changed, 128 insertions(+), 62821 deletions(-)
delete mode 180644 sprint2/Data.csv
delete mode 180644 sprint2/Data_Cleaned.csv
delete mode 180644 sprint2/cleaned_file.csv
```

Committing changes on second dev branch:

Conflicts occurred and had to be solved


```

c:\venv> carlusz@carlusz-WP-Notebook:~/PycharmProjects/AgileProject$ git merge Feature/filter-trends-across-years
Updating 0106fac..810b853
Fast-forward
 requirements.txt | 2 +
 sprint1/cleanCSvand_corr/correlation.py | 2 +-
 sprint2/Data.csv | 23871 -----
 sprint2/Data_Cleaned.csv | 19513 -----
 sprint2/cleaned_file.csv | 19369 -----
 sprint2/filter_columns.py => main.py | 193 -
 sprint2/mortality_rate.py | 66 -
 sprint2/plots/mortality_cancer.png | Bin 0 -> 68947 bytes
 sprint2/plots/mortality_rate_comparison.png | Bin 0 -> 37368 bytes
 sprint2/plots/not_implemented.png | Bin 0 -> 5223 bytes
 10 files changed, 130 insertions(+), 62886 deletions(-)
delete mode 108644 sprint2/Data.csv
delete mode 108644 sprint2/Data_Cleaned.csv
delete mode 108644 sprint2/cleaned_file.csv
rename sprint2/filter_columns.py => main.py (64%)
delete mode 108644 sprint2/mortality_rate.py
create mode 108644 sprint2/plots/mortality_cancer.png
create mode 108644 sprint2/plots/mortality_rate_comparison.png
create mode 108644 sprint2/plots/not_implemented.png

```

After solving conflicts

```
(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git push health_i main
Username for 'https://github.com': Dariusz20lczak
Password for 'https://Dariusz20lczak@github.com':
Total 0 (delta 0), reused 0 (delta 0), pack-reused 0
To https://github.com/EditaBuneviciene/AgileProject.git
01e0fac..818b853 main -> main
```

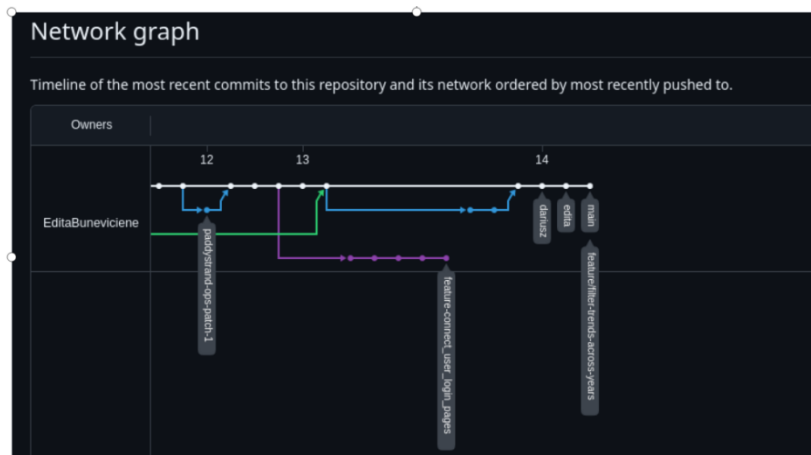

Git Tagging

Tagging Sprint versions

Checking for already existing tags and checking commit history:
Creating tag for Sprint1

```
Terminal Local x + v
(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git tag
(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git tag -l -n
(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git log --oneline --graph --all
* 818b853 (HEAD -> main, health_i/main, health_i/feature/filter-trends-across-years, feature/filter-trends-across-years) feature: restore improved main.py
* 654d1a7 (dariusz) Improved main
* e3e7116 (refs/stash) On Feature/filter-trends-across-years: my uncommitted feature work
//\
//\
* d768500 untracked files on feature/filter-trends-across-years: 4837f28 edita: improved filter trends across years
...skipping...
* 818b853 (HEAD -> main, health_i/main, health_i/feature/filter-trends-across-years, feature/filter-trends-across-years) feature: restore improved main.py
* 654d1a7 (dariusz) Improved main
* e3e7116 (refs/stash) On Feature/filter-trends-across-years: my uncommitted feature work
//\
//\
* d768500 untracked files on feature/filter-trends-across-years: 4837f28 edita: improved filter trends across years
* 50da610 index on feature/filter-trends-across-years: 4837f28 edita: improved filter trends across years
//\
//\
* 4837f28 (health_i/edita, edita) edita: improved filter trends across years
//\
* 470669d (health_i/dariusz) Feature: Filter Trends
(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git tag
(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git tag -a v1.0.0 81ecba4 -m "Sprint 1: Dataset cleaning and project setup"
(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git tag
v1.0.0
(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$
```

Creating tag for Sprint 2:

```
(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git tag -a v2.0.0 -m "Sprint 2: Data filtering and visualization"
(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git tag
v1.0.0
v2.0.0
(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$
```

Checking content of Tag v1.0.0

```
(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git show v1.0.0
tag v1.0.0
Tagger: Dariusz_Olczak <olczakdariusz13@gmail.com>
Date: Sat Nov 15 10:39:48 2025 +0000

Sprint 1: Dataset cleaning and project setup

commit 81ecba4f3fa292b4e5908389f3f306cfa983a17f (tag: v1.0.0)
Author: Dariusz_Olczak <olczakdariusz13@gmail.com>
Date: Wed Nov 5 16:57:38 2025 +0000

    Added .gitignore and requirements.txt. Copied Data.csv to cleanCSV file

diff --git a/.gitignore b/.gitignore
new file mode 100644
index 0000000..1e9fd54
--- /dev/null
+++ b/.gitignore
@@ -0,0 +1,17 @@
+.venv/
+.venv/
+.idea/
+__pycache__/
+*.pyc
+.env
+
+# Enhanced Python ignores
+*.py[cod]
+*$py.class
+*.so
+.Python
```

Checking for content of Tag v2.0.0

```
(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git show v2.0.0
tag v2.0.0
Tagger: Dariusz_Olczak <olczakdariusz13@gmail.com>
Date: Sat Nov 15 10:42:50 2025 +0000

Sprint 2: Data filtering and visualization

commit 818b853b1f53fbc8af2318b97bf9adc45287ba54 (HEAD -> main, tag: v2.0.0, health_i/main, health_i/feature/filter-trends-across-years, feature/filter-trends-across-years)
Author: Dariusz_Olczak <olczakdariusz13@gmail.com>
Date: Fri Nov 14 18:44:17 2025 +0000

    feature: restore improved main.py

diff --git a/sprint2/Data.csv b/sprint2/Data.csv
deleted file mode 100644
index 734d86a..0000000
--- a/sprint2/Data.csv
+++ /dev/null
@@ -1,23871 +0,0 @@
```

Pushing changes (added Tags) to remote:

```
(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git status
On branch main
Your branch is up to date with 'health_i/main'.

nothing to commit, working tree clean

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git log --oneline -1
818b853 (HEAD -> main, tag: v2.0.0, health_i/main, health_i/feature/filter-trends-across-years, feature/filter-trends-across-years) feature: restore improved main.py

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git tag
v1.0.0
v2.0.0

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git remote -v
health_i https://github.com/EditaBuneviciene/AgileProject.git (fetch)
health_i https://github.com/EditaBuneviciene/AgileProject.git (push)

(.venv) dariusz@dariusz-HP-Notebook:~/PycharmProjects/AgileProject$ git push health_i --tags
Username for 'https://github.com': DariuszOlczak
Password for 'https://DariuszOlczak@github.com':
Enumerating objects: 2, done.
Counting objects: 100% (2/2), done.
Delta compression using up to 4 threads
Compressing objects: 100% (2/2), done.
Writing objects: 100% (2/2), 355 bytes | 355.00 KiB/s, done.
Total 2 (delta 0), reused 0 (delta 0), pack-reused 0
To https://github.com/EditaBuneviciene/AgileProject.git
 * [new tag] v1.0.0 -> v1.0.0
 * [new tag] v2.0.0 -> v2.0.0
```

Sprint review

Sprint 2 daily /weekly scrum meeting

All team members should provide their priorities, progress, and problems each day in this report.

Team name	evSD
Direct supervisor	Scrum master Dariusz
Table of contents	\uD83D\uDD3 Week1 <03/11/2025> \uD83D\uDD3 Week 2 <10/11/2025> \uD83D\uDD3 Wednesday <12/11/25>

Week1 <03/11/2025>

	Name	Priorities 🤔	Progress 😊	Problems 😞
1	evSD_Group1 (Edita Buneviciene Dariusz Olczak Ed Tracey Patrick Strand)	Decide what information implement in user stories	Details in user story description	
2	evSD_Group1 (Edita Buneviciene Dariusz Olczak Ed Tracey Patrick Strand)	Pick a scrum master and PO	Scrum master and PO selected	
3	Ed Tracey Patrick Strand)	Research on HTML visualization	Working on it.	

Week 2 <10/11/2025>

	Name	Priorities 🤔	Progress 😊	Problems 😞
1	Dariusz Olczak	- Connect Jira and git. - Connect with Patrick to work on displaying data. - Create short report on tasks.		

2	Ed Tracey	• Git report and checklist. • Sprint2 user stories, subtasks acceptance criteria. • Create short report on tasks. • Update meeting minutes.		
3	Patrick Strand	• Update sprint user stories and subtasks. • Setup git on local machine and clone repo. • Create short report on tasks.		
4	Edita Buneviciene	• Write the script for a subtask. • Create short report on tasks.	Write main.py to display graphs/charts	



Wednesday <12/11/25>

	Name	Priorities 🧐	Progress 😊	Problems 😐
1	evSD_Group1 (Edita Buneviciene Dariusz Olczak Ed Tracey Patrick Strand)	• take screenshot continuously of work • Add more details user stories and subtask descriptions		

Sprint

E1 Sprint 2

Estimation field

Story points




Date - November 2nd, 2025 - November 15th, 2025



Date	Event	Work Item	Completed	Scope
Sun, Nov 02 2025, 8:32pm	Sprint started	E1-19 Github repository and details E1-29 Filter mortality trends in certain years. E1-31 Filter series by relevant countries. E1-32 Create HTML E1-30 Display Charts for Data Selections	0	23
Wed, Nov 12 2025, 9:53pm	Added to sprint	E1-125 Connect User login web pages	0	23
Wed, Nov 12 2025, 9:53pm	Estimate updated	E1-125 Connect User login web pages	0	23 → 26
Thu, Nov 13 2025, 8:58pm	Work item completed	E1-125 Connect User login web pages	0 → 3	26
Sat, Nov 15 2025, 11:36am	Work item completed	E1-31 Filter series by relevant countries.	3 → 8	26
Sat, Nov 15 2025, 3:51pm	Estimate updated	E1-29 Filter mortality trends in certain years.	8	26 → 25
Sat, Nov 15 2025, 5:47pm	Work item re-opened	E1-31 Filter series by relevant countries.	8 → 3	25
Sat, Nov 15 2025, 5:47pm	Work item completed	E1-31 Filter series by relevant countries.	3 → 8	25
Sat, Nov 15 2025, 5:58pm	Work item completed	E1-29 Filter mortality trends in certain years.	8 → 12	25
Sat, Nov 15 2025, 6:24pm	Work item completed	E1-19 Github repository and details	12 → 16	25
Sat, Nov 15 2025, 6:33pm	Estimate updated	E1-125 Connect User login web pages	16 → 19	25 → 28
Sat, Nov 15 2025, 6:34pm	Estimate updated	E1-125 Connect User login web pages	19 → 17	28 → 26
Sat, Nov 15 2025, 10:25pm	Estimate updated	E1-32 Create HTML	17	26 → 27
Sat, Nov 15 2025, 10:31pm	Estimate updated	E1-32 Create HTML	17	27 → 26
Sat, Nov 15 2025, 10:43pm	Estimate updated	E1-30 Display Charts for Data Selections	17	26 → 28
Sat, Nov 15 2025, 10:44pm	Estimate updated	E1-32 Create HTML	17	28 → 27
Sat, Nov 15 2025, 10:45pm	Estimate updated	E1-30 Display Charts for Data Selections	17	27 → 26
Sun, Nov 16 2025, 10:23am	Work item completed	E1-32 Create HTML	17 → 21	26
Sun, Nov 16 2025, 10:23am	Work item completed	E1-30 Display Charts for Data Selections	21 → 26	26
Sun, Nov 16 2025, 10:36am	Work item re-opened	E1-29 Filter mortality trends in certain years.	26 → 22	26
Sun, Nov 16 2025, 10:36am	Work item completed	E1-29 Filter mortality trends in certain years.	22 → 26	26
Sun, Nov 16 2025, 10:36am	Work item re-opened	E1-31 Filter series by relevant countries.	26 → 21	26
Sun, Nov 16 2025, 10:36am	Work item re-opened	E1-19 Github repository and details	21 → 17	26
Sun, Nov 16 2025, 10:36am	Work item re-opened	E1-125 Connect User login web pages	17 → 13	26

Sprint 2 Burndown chart

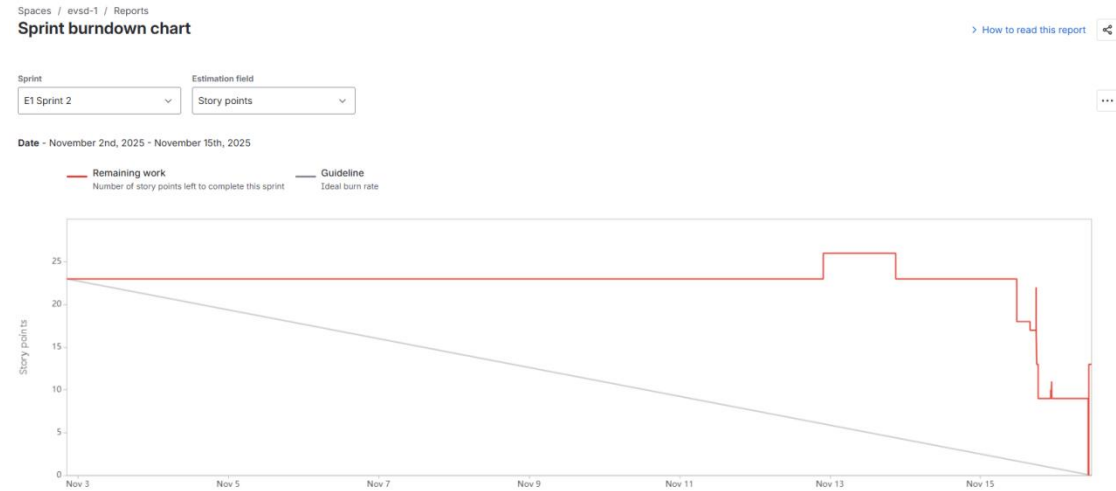

Report: E1 Sprint 2

• Work item added after sprir

Scope changes log

[View in All work na](#)

Date ↑	Key	Summary	Work type	Epic	Details of scope change	Change in estim
2025-11-12	E1-125+	Connect User login web pages	Task	VISUALISATION	Work item added to sprint	-
2025-11-12	E1-125	Connect User login web pages	Task	VISUALISATION	Estimate of 3 has been added	- → 3
2025-11-15	E1-29	Filter mortality trends in certain years.	Story	TREND ANALYSIS	Estimate changed from 5 to 4	5 → 4
2025-11-15	E1-125	Connect User login web pages	Task	VISUALISATION	Estimate changed from 3 to 6	3 → 6
2025-11-15	E1-125	Connect User login web pages	Task	VISUALISATION	Estimate changed from 6 to 4	6 → 4
2025-11-15	E1-32	Create HTML	Story	VISUALISATION	Estimate changed from 5 to 6	5 → 6
2025-11-15	E1-32	Create HTML	Story	VISUALISATION	Estimate changed from 6 to 5	6 → 5
2025-11-15	E1-30	Display Charts for Data Selections	Story	VISUALISATION	Estimate changed from 4 to 6	4 → 6
2025-11-15	E1-32	Create HTML	Story	VISUALISATION	Estimate changed from 5 to 4	5 → 4
2025-11-15	E1-30	Display Charts for Data Selections	Story	VISUALISATION	Estimate changed from 6 to 5	6 → 5

Completed work items

[View in All work navigator](#)

Key	Summary	Work type	Epic	Status	Assignee	Story points
E1-18	Github repository and details	Task	REPOSITORY	DONE	ET	4
E1-29	Filter mortality trends in certain years.	Story	TREND ANALYSIS	DONE	EB	4
E1-31	Filter series by relevant countries.	Task	TREND ANALYSIS	DONE	ET	5
E1-32	Create HTML	Story	VISUALISATION	DONE	PS	4
E1-30	Display Charts for Data Selections	Story	VISUALISATION	DONE	PS	5
E1-125	Connect User login web pages	Task	VISUALISATION	DONE	ET	4



Sprint 2

Sprint Summary

Sprint Dates: 02 Nov 2025 to 15 Nov 2025

This sprint focuses on the following goals.

- Finish the web login interface and test it's functionality.
- Document the git workflow and record any additions to the repository with screenshots and descriptions.
- Ensure the data set is clean and accessible via the home page.
- Create the home page interface to visualize selections of the data set on a graph.

Sprint2 Detail

Completed

Key	Summary	Story Points	Planned	Comment	Feedback
E1-29	Filter mortality trends in certain years.	4	YES		
E1-19	Github repository and details	4	YES		
E1-32	Create HTML	4	YES		
E1-30	Display Charts for Data Selections	5	YES		
E1-31	Filter series by relevant countries.	5	YES		
E1-125	Connect User login web pages	4	NO		

Added

Key	Summary	Story Points	Planned	Comment	Feedback
E1-125	Connect User login web pages	4	NO		

Removed

No issues removed

Impediments & Risks

Impediments

Title / Description	Impact	Status	Action taken
The final home page is still in development and the data set needs more processing.	Small	Resolved	A temporary home page was created to allow column selection from a dummy data set for displaying a graph.
Training for git commands and deciding on a compatible git workflow.	Small	Resolved	A document outlining the procedure for branch, committing, pull requests, etc., was created so the team could familiarize itself with procedure.
Data visualization development needed to be prioritized to meet the sprint due date.	Medium	Resolved	Members of the development Team, (Patrick & Dariusz), paired together to complete the task.

Risks

Title / Description	Impact	Likelihood	Action taken
Towards the end of the Sprint there was a risk of not meeting the due date due to the number of tasks in the sprint.	Medium		Each task was revisited and any details that were unclear were updated. A number of tasks were then able to be removed due to overlapping work or repeated tasks. This reduced the overall workload and focused the work more clearly on the objectives of the sprint.
Risk of incomplete tasks becoming blockers for other tasks.	Medium		The frequency of planning meetings and short communication calls between the development team members was increased to ensure that the team was always aware of the status and progress of related tasks in the Sprint.

Reflect on past work and identify opportunities for improvement by following the instructions for the [Retrospective Play](#).

Overview

Date	10 Nov 2025
Team	evsd-1
Participants	Edita Buneviciene, Dariusz Olczak, Patrick Strand, Edward Tracey

Retrospective

 Start doing	 Stop doing	 Keep doing
Document each task with a basic cheat sheet.	Ensure any tasks that may overlap do not end up as duplicate tasks.	Updating the subtasks and DoD details.
Ensure a clear definition of the acceptance criteria has been outlined before a task has started.	Don't let tasks sit for long periods without updating.	Keep updating the backlog to reflect the changes in priority and eliminate any redundant tasks.
Meeting topics should be limited to 10 minutes. If longer is needed then a separate meeting involving the relevant developers should be scheduled.	Unless a task is blocked, complete existing tasks in the sprint before starting a new one, especially when it comes close to the end of a sprint.	Revisiting the story point descriptions and done definitions to help focus the objectives.
For complex tasks the work should be paired between developers to ensure the knowledge is spread and help the task complete faster.	Creating test branches on the remote repo can make the tree look confusing and hard to follow. Any test branches should be local and all merges back into main should be done via pull requests/reviews.	Keep the collaboration and communication regular.
Update dates for task completion once the task has started to help view the project progress.	A definitive and understandable path for the project should be outlined as early as possible. (Module description)	Periodic meetings and discussions on the relevant tasks.

Action items

- Create a checklist for description, dod, subtasks with details, story point values, that should be completed before the task is added to the sprint.
- To keep the git tree looking tidy, ensure all merges into main are done via a pull request and update the git readme details if anything is unclear.
- Ensure meeting topics don't run overtime by setting 10 mins max per topic.
- Document all tasks with a quick cheat sheet with info on the task and screenshots/diagrams to help ensure the final report can be assembled quicker.

What's next

- Sprint 3

Sprint 3

Product backlog

Epics for Sprint3: Test cases, GitHub pipeline, CI/CD, Communication with LLM, Website integration.

Product backlog

By Edita Buneviciene See views Add a reaction

Type	Key	Summary	Assignee	Priority	Status	Updated
🔗	E1-135	Test cases1	 Dariusz Olczak	Medium	TO DO	Dec 2, 2025, 21:28
🔗	E1-134	Website integration	 Ed Tracey	Medium	TO DO	Dec 2, 2025, 21:00
🔗	E1-133	Communication with LLM	 Ed Tracey	Medium	TO DO	Dec 1, 2025, 20:54
🔗	E1-132	GitHub pipeline, CI/CD	 Dariusz Olczak	Medium	TO DO	Nov 18, 2025, 13:43
🔗	E1-130	DevOps toolchain	 Edita Buneviciene	Medium	TO DO	Nov 18, 2025, 13:38
🔗	E1-129	Create test home page for data visualization.	 Ed Tracey	Medium	DONE	Nov 15, 2025, 18:34
🔗	E1-128	Create instructions in the read.me file for user to start local server.	 Ed Tracey	Medium	DONE	Nov 15, 2025, 17:30
🔗	E1-127	Add on-click functionality to buttons for navigation.	 Ed Tracey	Medium	DONE	Nov 15, 2025, 17:26
🔗	E1-126	Ensure each html page layout is complete.	 Ed Tracey	Medium	DONE	Nov 15, 2025, 18:34
🔗	E1-125	Connect User login web pages	 Ed Tracey	Medium	DONE	Nov 16, 2025, 11:29
🔗	E1-124	Visualisation		Medium	TO DO	Nov 18, 2025, 13:44
🔗	E1-123	Trend analysis	 Edita Buneviciene	Medium	TO DO	Nov 10, 2025, 12:45

User stories: Test cases, Log in and front user HTML integration, Create HTML for front end user, Design tool chain, Pipeline.

User story:

E1-130

/

E1-35

1

Share

More

Design toolchain

Done

Done

Lightning bolt

Eye

+

Description

As a developer I want to design a toolchain so that DevOps team could decide what tools should be use to automate the process of each stage.

Acceptance criteria:

1. A diagram should display what tools are used for each stage.

Dependencies:

1. Different tools depends on needs of team members.

Risk:

1. The developers may not be aware of some tools.

Subtasks

100% Done

Work

E1-101

Design toolchain

E1-102

Toolchain research

Details

Assignee

EB

Edita Buneviciene

Labels

Add labels

Parent

E1-130

DevOps toolchain

Due date

Dec 05, 2025

Team

Add team

Start date

Nov 24, 2025

Sprint

E1 Sprint 3

Story point estimate

4

Fix version

Subtasks:

E1-35

/

E1-101

1

Share

More

Design toolchain

Done

Done

Lightning bolt

Eye

+

Description

As a developer I need to design a toolchain so the others developer could follow it.

DoD criterion:

1. Use a graphical tool for design diagram.

Estimated time: 1 hour

Linked work items

Add linked work item

Details

Assignee

EB

Edita Buneviciene

Labels

Add labels

Parent

E1-35

Design toolchain

Due date

Dec 01, 2025

Start date

Nov 17, 2025

Fix versions

None

Sprint

E1 Sprint 3

Story point estimate

1

E1-35

E1-102

1

Toolchain research

Done

✓ Done

▼ Description

Do the research on available tools for DevOps toolchain.

DoD:

1. The available tools are displayed in toolchain diagram.

Estimated time: 1 hour

Linked work items

▼ Details

Edita Buneviciene

Labels

Add labels

Parent

E1-35 Design toolchain

Due date

Dec 05, 2025

Start date

Nov 17, 2025

Fix versions

None

Sprint

E1 Sprint 3

Story point estimate

1

User story:

E1-135

E1-3

1

Test cases

Done

✓ Done

▼ Description

As a developer, I need to test critical part of project.

Acceptance criteria:

1. It should check about 80 % of code.

Dependencies:

1. The code should be critical for the project.

Risk:

1. The test results do not meet requirement.

▼ Subtasks

...

+

0% Done

Work

E1-110 Unit test

Linked work items

▼ Details

Assignee

Dariusz Olczak

Assign to me

Labels

None

Parent

E1-135 Test cases1

Due date

Dec 05, 2025

Team

None

Start date

Nov 17, 2025

Sprint

E1 Sprint 3

Story point estimate

2

Subtask:

Subtask:

☒ E1-42 /  E1-119

👁 1





Data, time range option selection.

Done ▾

✓ Done







▼ Description

As a developer I want to be able to select countries and year for predictions so create drop down menu in HTML.

DoD: drop down menu is available for the selection.

Estimated time: 6 hours

Linked work items

Add linked work item

☒ E1-42 /  E1-120

👁 1





Analysis option field

TEST ▾







▼ Description

As a developer I need to display a chart of results and predictions so I will update code in Python.

DoD:

Graph is displayed after Generate Analysis button is pressed.

Estimated time: 3 hours.

Linked work items

Add linked work item

▼ Details



Assignee

 Patrick Strand

[Assign to me](#)

Labels

Add labels

Parent

☒ [E1-42 Create HTML for front end user](#)

Due date

Dec 05, 2025

Team

 evSD_Group1

Start date

Nov 17, 2025

Fix versions

None

Sprint

[E1 Sprint 3](#)

Story point estimate

2

▼ Details



Assignee

 Dariusz Olczak

[Assign to me](#)

Labels

Add labels

Parent

☒ [E1-42 Create HTML for front end user](#)

Due date

📅 Dec 5, 2025

Team

 evSD_Group1

Start date

Nov 17, 2025

Fix versions

None

Sprint

[E1 Sprint 3](#)

Story point estimate

2

☒ E1-42 /  E1-121

 1





Manual upload of file.

Done ▾

✓ Done







▼ **Description**

AS a user I want to have a manual upload option for exploring different dataset.

DoD:

manual upload is implemented at a bottom of HTML.

Estimated time: 3 hours.

Linked work items

Add linked work item

▼ Details 

Assignee
 Patrick Strand
[Assign to me](#)

Labels
Add labels

Parent
☒ E1-42 Create HTML for front end user

Due date
Dec 05, 2025

Team
 evSD_Group1

Start date
Nov 17, 2025

Fix versions
None

Sprint
[E1 Sprint 3](#)

Story point estimate

1

☒ E1-42 /  E1-136

 1





AI analysis and insights

TEST ▾







▼ **Description**

Update code in Python main for predictions display.

DoD: panel on left had side gives the info regarding predictions.

Estimated time: 3 hours

Linked work items

Add linked work item

▼ Details 

Assignee
 Dariusz Olczak
[Assign to me](#)

Labels
Add labels

Parent
☒ E1-42 Create HTML for front end user

Due date

 Dec 5, 2025

Team
 evSD_Group1

Start date
Nov 17, 2025

Fix versions
None

Sprint
[E1 Sprint 3](#)

Story point estimate

4

E1-42 / E1-137

1

API connections

TEST

Description

Connect main.py to HTML

DoD: HTML is connected to local server and main.py

Estimated time:6 hours

Linked work items

Add linked work item

Details

Assignee

Dariusz Olczak

Assign to me

Labels

Add labels

Parent

E1-42 Create HTML for front end user

Due date

Dec 5, 2025

Team

evSD_Group1

Start date

Nov 17, 2025

Fix versions

None

Sprint

E1 Sprint 3

Story point estimate

5

Development

User story:

E1-132 / E1-36

1

Pipeline

Done

Done

Description

As a developer I need to automate some action in Github for ensure consistency across environments.

Acceptance criteria:

1. A file created in .github/workflows should be yaml or yml format.

Dependencies: should be able to login Github.

Risk: typo mistakes in file.

Subtasks

100% Done

Work	P...	A...	Status
E1-107 Create pipelin...	=		DONE
E1-108 CI process	=		DONE
E1-109 CD process	=		DONE

Linked work items

Details

Assignee

Dariusz Olczak

Assign to me

Labels

Add labels

Parent

E1-132 GitHub pipeline, CI/CD

Due date

Dec 05, 2025

Team

Add team

Start date

Nov 17, 2025

Sprint

E1 Sprint 3

Story point estimate

3

Fix versions

Subtasks:

Create pipeline .yaml file

Done ▾ ✓ Done ⚡ ⌚ +

▼ Description

As a developer I need have a pipeline in GitHub to tell GitHub what to run, when to run how to run.

DoD:

1. Created a yaml document in .gitworkflows folder in Github.

Estimated time: 1 hour.

Linked work items

Add linked work item

▼ Details

Assignee

 Dariusz Olczak

[Assign to me](#)

Labels

Add labels

Parent

 [E1-36 Pipeline](#)

Due date

Dec 05, 2025

Start date

Nov 17, 2025

Fix versions

None

Sprint

[E1 Sprint 3](#)

Story point estimate

1

 E1-36 /  E1-108

 1  ...

CI process

Done ▾ ✓ Done ⚡ ⌚ +

▼ Description

As a developer I need to follow and screenshot CI process of build, test, package.

DoD: Screenshots are capture.

Estimated time: 2 hours.

Linked work items

Add linked work item

▼ Details

Assignee

 Dariusz Olczak

[Assign to me](#)

Labels

Add labels

Parent

 [E1-36 Pipeline](#)

Due date

Dec 05, 2025

Start date

Nov 17, 2025

Fix versions

None

Sprint

[E1 Sprint 3](#)

Story point estimate

1

E1-36 / E1-109  1  

CD process

Done ▾ ✓ Done   

✓ **Description**

As a developer I need to track the process of CD and take screenshots.

DoD: screenshots are captured of process.

Estimated time: 2 hours.

Linked work items

Add linked work item

Details 

Assignee

 Dariusz Olczak

[Assign to me](#)

Labels

Add labels

Parent

 [E1-36 Pipeline](#)

Due date

Dec 05, 2025

Start date

Nov 17, 2025

Fix versions

None

Sprint

[E1 Sprint 3](#)

Story point estimate

1

User story:

E1-134 / E1-41  1  

Log in and front end user HTML integration

In Progress ▾   

✓ **Description**

As a developer, I want that user would be able to login and after selecting preferable indicators, get predictions.

Acceptance criteria:

1. After the server is started. The first page should be the login page. After a successful login the user should land on the main page for data display.

Dependencies:

1. All login related pages should be complete.
2. Ensure all module/libs dependencies are installed.

Risk:

1. Ensure the server has started correctly.
2. If the paths to pages should change, ensure that the related code is updated.

Details 

Assignee

 Ed Tracey

[Assign to me](#)

Labels

Add labels

Parent

 [E1-134 Website integration](#)

Due date

 Dec 5, 2025

Team

Add team

Start date

Nov 17, 2025

Sprint

[E1 Sprint 3](#)

Story point estimate

5

Fix versions

Subtasks:

E1-41 / E1-116

1

Successful login should open the data visualization page.

Done

Done

Description

As a developer I want to change the way we start the web interface so that it starts on the login page. After the user has logged in, the data visualization page should be displayed. The user login details should be stored as a text file for now to allow for easy testing.

DoD:

1. Before the user opens the login page, our local server needs to be started from a script. Once the user logs in, the data display page should be visible.

Estimated time:

3 hours

E1-41 / E1-117

1

Create PDF page reports for export

Done

Done

Description

Description:

As a developer I want to allow exporting reports in a standard format (PDF) that can be shared externally. Keep branding consistent and remove sensitive identifiers.

Dod:


Test task is complete by generating a PDF report.

Estimated Time:

2hrs

Attachments

1



Details

Assignee

ET

Ed Tracey

Assign to me

Labels

Add labels

Parent

E1-41 Log in and front end user HTML

Due date

Dec 05, 2025

Start date

Nov 17, 2025

Fix versions

None

Sprint

E1 Sprint 3

Story point estimate

1

Details

Assignee

ET

Ed Tracey

Assign to me

Labels

Add labels

Parent

E1-41 Log in and front end user HTML

Due date

Dec 05, 2025

Start date

Nov 17, 2025

Fix versions

None

Sprint

E1 Sprint 3

Story point estimate


2

Planning Poker Process:


During this sprint, we carried out Planning Poker estimation through a Zoom meeting, similar to our previous sprint. Patrick acted as the Product Owner, while Ed was nominated as the Scrum Master. We used the Planning Poker technique to estimate the story points of several tasks, with each team member voting anonymously to ensure unbiased input. Although the process worked well, we found it to be quite time-consuming when applied to every item in the backlog. Therefore, after estimating the first set of tasks using the formal game, we agreed to assign story points verbally for the remaining items. These story points were based on the average of the team's suggested estimates, allowing us to complete the session efficiently while maintaining a fair assessment of task complexity.

▼ Planning Poker

VOTED: 0



Pick your estimate



When scores were tied, the scrum master had the final decision.

Sprint 3 planning

Backlog

☐ ▼ E1 Sprint 3 17 Nov – 5 Dec (5 work items)				0	5	16	Complete sprint	...
☒ E1-3	Test cases	TEST CASES1	DONE ▼	Dec 5	3			
☐ E1-41	Log in and front end user HTML integration	WEBSITE IN...	IN PROGRESS ▼	Dec 5	5			ET
☒ E1-42	Create HTML for front end user	COMMUNIC...	DONE ▼	Dec 5	6			PS
☒ E1-35	Design toolchain	DEVOPS TO...	DONE ▼	Dec 5	4			EB
☐ E1-36	Pipeline	GITHUB PIP...	DONE ▼	Dec 5	3			
+ Create								

In this sprint we choose velocity and story point approach. Total 21 story points for Sprint3 .

In this project, we used the velocity approach to measure the team's progress and plan our sprints more effectively. Velocity represents the amount of work the team can complete in a single sprint, typically measured in story points. By tracking completed story points at the end of each sprint, we gained a clearer understanding of our actual delivery capacity.

User story "Test cases" assigned to Dariusz, subtask is assigned to Dariusz.


User story "Log in and front end user HTML integration" is assigned to Ed, subtasks are assigned to Ed also.

User story "Create HTML for front end user" assigned to Patrick. Subtasks "Data, time range option selection", "Manual upload of file" are assigned to Patrick. The rest of subtasks "Analysis option field", "AI analysis and insights", "API connections" are assigned to Dariusz.


User story "Design toolchain" and corresponding subtasks assigned to Edita.

User story "Pipeline" and corresponding subtasks are assigned to Dariusz.

Scrum board

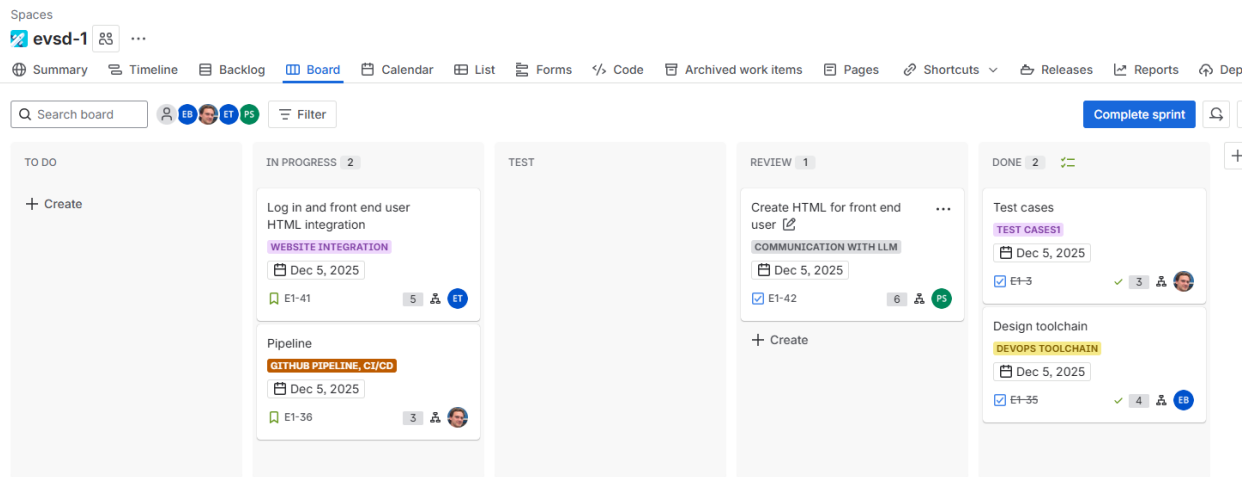

Timeline

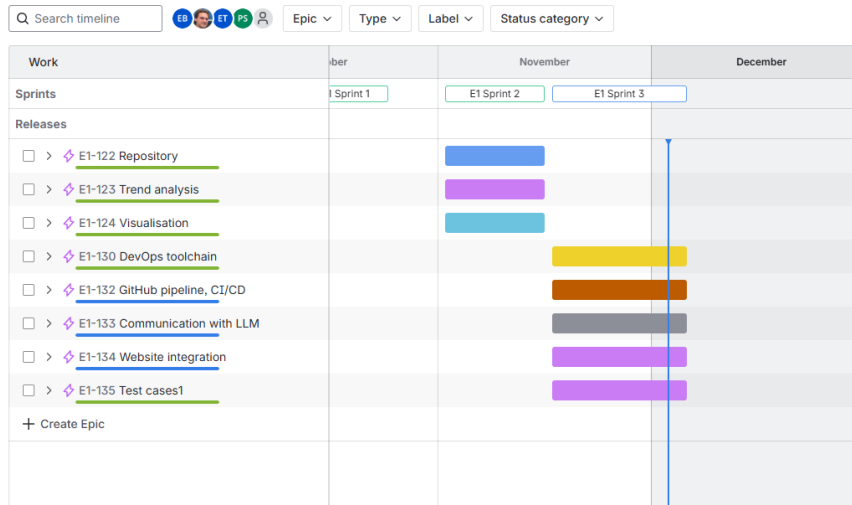

Sprint 3 Planning report

-  [Sprint planning checklist](#)
-  [Sprint team members](#)
-  [Sprint planning meeting items](#)
 - [Agenda](#)
 - [Previous sprint summary](#)
 - [Details](#)
 - [Velocity tracking](#)
 - [Adjusted velocity tracking](#)
 - [Capacity planning](#)
 - [Potential risks](#)
- [?? Sprint planning resources](#)
 - [Team resources and definitions](#)

Sprint planning checklist

Preparation	Meeting	Follow up
• prioritize on epics, user stories, subtask, give proper description • improve the script for intelligent part of project • improve HTML layout to accommodate extra feature • do research for toolchain • research on testing • script for testing. • integration of • pipeline .yaml	• Confirm proper story description, acceptance criteria • Add subtasks for implementation, testing, documentation. • Improve HTML layout to support new features • Automation scripts for testing	• Finalize sprint backlog in Jira • Verify stories have subtasks and clear owners •

Sprint team members

	Name	Role
1	Ed Tracey	Scrum master
2	Patrick Strand	PO
3	Edita Buneviciene	Developer
4	Dariusz Olczak	Developer

Sprint planning meeting items

Use this template to structure your meeting, set expectations and goals, and define the backlog for the upcoming sprint. For detailed instructions and best practices, see our [sprint planning guide](#) and review how to [estimate story points](#).

Agenda

1. Close Sprint 3
2. Expected team capacity 100%, delivered 100%
3. Average capacity in previous sprints 30 story points, predicted story points for Sprint3 21 points.

Previous sprint summary

Sprint theme	HTML for predictions
Story points	Previous Sprint3 carried 21 story points. All planned subtask were implemented. No backlog for next Sprint.
Summary	The team developed the HTML interface that enables end users to navigate the application and generate predictions based on selected data. We also integrated the previous sprint's main.py logic with the new frontend, establishing full API connectivity between the UI and backend services.

Details

Start date	17/11/2025
End date	05/12/2025

Sprint theme	HTML for predictions
---------------------	-----------------------------

Capacity planning

	Current sprint	Previous sprint
Total days	19	14
Team capacity	100%	100%
Projected capacity	21	26
Individual capacity	Dariusz Olczak 6	5
	Edita Buneviciene 4	5
	Ed Tracey 5	7
	Patrick Strand 6	9

Potential risks

Risk	Mitigation
API endpoints may not respond as expected; UI may fail to render results.	Detect problems before integration.
Incorrect comparisons; wrong prediction outputs; inconsistencies in logic.	Create automated tests for logic validation.

Sprint planning resources

Team resources and definitions:

HTML, UI (user interface), API, backend, GitHub, predictions.

Sprint 3 review

Sprint 3 Daily/weekly report

All team members should provide their priorities, progress, and problems each day in this report.

Team name	evsd
Direct supervisor	
Table of contents	• \uD83D\uDD33 Monday <17/11/2025> • \uD83D\uDD33 Sunday <23/11/2025> • \uD83D\uDD33 Wednesday <03/12/2025>

Monday <17/11/2025>

	Name	Priorities 🧐	Progress 😊	Problems 😞
1	evSD Group1 (Edita Buneviciene Dariusz Olczak Ed Tracey Patrick Strand)	Go other lecture notes Look in Unit testing tools Do research on LLM Prepare epics for Sprint 3 Look in git hub pipeline, CI/CD	Start working on creating front and back end.	Uncertain where to run HTML, but will do on local server.

Sunday <23/11/2025>

	Name	Priorities 🤔	Progress 😊	Problems 😞
1	Edita Buneviciene	Design tool chain Keep up Jira up to date.		
2	Dariusz Olczak	test script .yaml file for pipeline API connection		
3	Patrick Strand	final updates for HTML		
4	Ed Tracey	API connections with Dariusz Dashboard Summary PDF		

📅 Wednesday <03/12/2025>

	Name	Priorities 🤔	Progress 😊	Problems 😞
1	evSD Group1 (Edita Buneviciene Dariusz Olczak Ed Tracey Patrick Strand)	Updates for User stories before Sprint3 completion		
2	evSD Group1 (Edita Buneviciene Dariusz Olczak Ed Tracey Patrick Strand)	collect feedback from stakeholders	Waiting on stakeholders feedback	

Sprint 3

Sprint Summary

Sprint Dates: 17 Nov 2025 to 05 Dec 2025

- This sprint focuses on the following goals:

- API connection
- Running HTML
- .pipeline in Github
- Tool chain
- Remove “ No LLM model found” line from HTML.
- The stakeholder was satisfied with the project outcomes and the progress made throughout the development process. Their positive feedback indicated that the delivered features aligned well with expectations and addressed the intended objectives.

Sprint3 Detail

Completed

Key	Summary	Story Points	Planned	Comment	Feedback
E1-3	Test cases	3	NO		
E1-35	Design toolchain	4	NO		
E1-42	Create HTML for front end user	6	NO		
E1-36	Pipeline	3	NO		
E1-41	Log in and front end user HTML integration	5	NO		

Added

Key	Summary	Story Points	Planned	Comment	Feedback
E1-3	Test cases	3	NO		
E1-35	Design toolchain	4	NO		
E1-42	Create HTML for front end user	6	NO		
E1-36	Pipeline	3	NO		
E1-41	Log in and front end user HTML integration	5	NO		

Impediments & Risks

Impediments

Title / Description	Impact	Status	Action taken
The integration between the main application code and the HTML interface presented several challenges. The API connection was a source of unexpected bugs, and resolving them required technical expertise that the team had not yet fully developed.	High	Resolved	Being focused effort and collaboration, we successfully overcame these issues and achieved a working connection between the back end and the user-facing front end.
Understanding the pipeline structure and configuring CI/CD actions in GitHub , especially .	Medium	Resolved	Despite the learning curve, the team gradually built confidence with these tools and

			improved our ability to automate and manage the development process effectively
--	--	--	---

Risks


Title / Description	Impact	Likelihood	Action taken
Risk of incomplete workload becomes unfinished project.	High		Dedicate time and putting all team effort got us to the finish of project.
LLM connections and predictions wouldn't work .	High		Reviewed the API setup, corrected configuration errors, validated request formats, and checked environment variables. After consulting documentation, established LLM connectivity and predictions.

Sprint Report

[How to read this chart](#)

How to read this chart

Understand the work completed or pushed back to the backlog in each sprint. This helps you determine if your team is overcommitting or if there is excessive scope creep.



Status Report

Completed Issues

[View in Issue Navigator](#)


Key	Summary	Issue Type	Priority	Status	Story Points (-)
E1-35 *	Design toolchain	Task	Medium	DONE	-
E1-36 *	Pipeline	Story	Medium	DONE	-
E1-41 *	Log in and front end user HTML integration	Story	Medium	DONE	-
E1-42 *	Create HTML for front end user	Task	Medium	DONE	-

Only displaying 4 user stories, could not figure out why.

Burndown chart

Spaces / evsd-1 / Reports

Sprint burndown chart

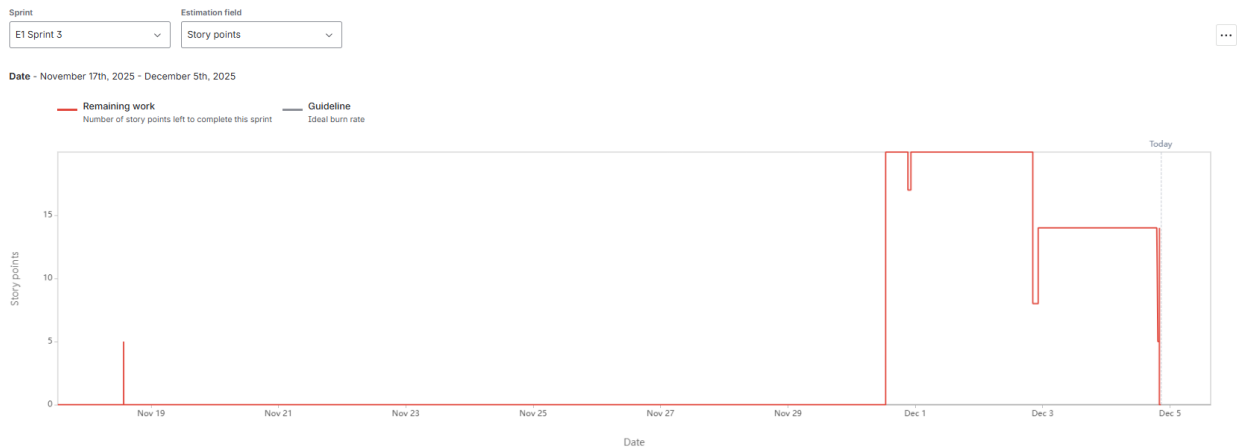[How to read this report](#)

Report: E1 Sprint 3

*Work item added after sprint start

Scope changes log

[View in All work navigator](#)

Date ↑	Key	Summary	Work type	Epic	Details of scope change	Change in estimation
2025-11-18	E1-35+	Design toolchain	Task	DEVOPS TOOLCHAIN	Work item added to sprint	5
2025-11-18	E1-35	Design toolchain	Task	DEVOPS TOOLCHAIN	Work item removed from sprint	-5
2025-11-20	E1-35	Design toolchain	Task	DEVOPS TOOLCHAIN	Estimate changed from 5 to 4	5 → 4
2025-11-30	E1-36+	Pipeline	Story	GITHUB PIPELINE, CI/CD	Work item added to sprint	3
2025-11-30	E1-35+	Design toolchain	Task	DEVOPS TOOLCHAIN	Work item added to sprint	4
2025-11-30	E1-3+	Test cases	Task	TEST CASES1	Work item added to sprint	4
2025-11-30	E1-41+	Log in and front end user HTML integration	Story	WEBSITE INTEGRATION	Work item added to sprint	4
2025-11-30	E1-42+	Create HTML for front end user	Task	COMMUNICATION WITH ...	Work item added to sprint	5
2025-11-30	E1-3	Test cases	Task	TEST CASES1	Estimate changed from 4 to 1	4 → 1
2025-11-30	E1-3	Test cases	Task	TEST CASES1	Estimate changed from 1 to 2	1 → 2
2025-11-30	E1-42	Create HTML for front end user	Task	COMMUNICATION WITH ...	Estimate changed from 5 to 6	5 → 6
2025-11-30	E1-41	Log in and front end user HTML integration	Story	WEBSITE INTEGRATION	Estimate changed from 4 to 5	4 → 5
2025-12-04	E1-3	Test cases	Task	TEST CASES1	Estimate changed from 2 to 4	2 → 4
2025-12-04	E1-3	Test cases	Task	TEST CASES1	Estimate changed from 4 to 3	4 → 3

Your sprint commitment has increased by 21 story points


Due to scope changes: You have 21 story points to complete this sprint

Completed work items


[View in All work navigator](#)

Key	Summary	Work type	Epic	Status	Assignee	Story points
E1-35	Design toolchain	Task	DEVOPS TOOLCHAIN	DONE	EB	4
E1-36	Pipeline	Story	GITHUB PIPELINE, CI/CD	DONE		3
E1-3	Test cases	Task	TEST CASES1	DONE		3
E1-41	Log in and front end user HTML integration	Story	WEBSITE INTEGRATION	DONE	ET	5
E1-42	Create HTML for front end user	Task	COMMUNICATION WITH LLM	DONE	IP	6

Burn up chart

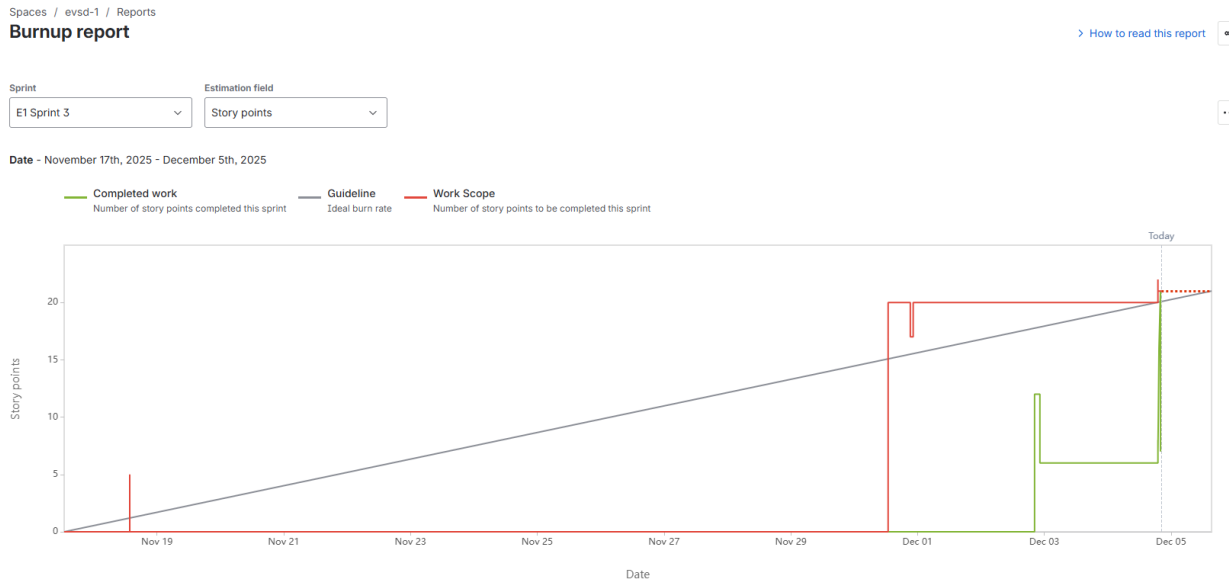

Mon, Nov 17 2025, 12:52pm	Sprint started		0	0
Tue, Nov 18 2025, 1:41pm	Added to sprint	E1-35 Design toolchain	0	0 → 5
Tue, Nov 18 2025, 1:42pm	Removed from sprint	E1-35 Design toolchain	0	5 → 0
Thu, Nov 20 2025, 8:27pm	Estimate updated	E1-35 Design toolchain	0	0
Sun, Nov 30 2025, 12:51pm	Added to sprint	E1-36 Pipeline	0	0 → 3
Sun, Nov 30 2025, 12:51pm	Added to sprint	E1-35 Design toolchain	0	3 → 7
Sun, Nov 30 2025, 12:51pm	Added to sprint	E1-3 Test cases	0	7 → 11
Sun, Nov 30 2025, 12:51pm	Added to sprint	E1-41 Log in and front end user HTML integration	0	11 → 15
Sun, Nov 30 2025, 12:52pm	Added to sprint	E1-42 Create HTML for front end user	0	15 → 20
Sun, Nov 30 2025, 9:16pm	Estimate updated	E1-3 Test cases	0	20 → 17
Sun, Nov 30 2025, 10:21pm	Estimate updated	E1-3 Test cases	0	17 → 18
Sun, Nov 30 2025, 10:21pm	Estimate updated	E1-42 Create HTML for front end user	0	18 → 19
Sun, Nov 30 2025, 10:21pm	Estimate updated	E1-41 Log in and front end user HTML integration	0	19 → 20
Tue, Dec 02 2025, 8:18pm	Work item completed	E1-42 Create HTML for front end user	0 → 6	20
Tue, Dec 02 2025, 8:19pm	Work item completed	E1-35 Design toolchain	6 → 10	20
Tue, Dec 02 2025, 8:19pm	Work item completed	E1-3 Test cases	10 → 12	20
Tue, Dec 02 2025, 10:20pm	Work item re-opened	E1-42 Create HTML for front end user	12 → 6	20
Thu, Dec 04 2025, 7:01pm	Estimate updated	E1-3 Test cases	6 → 8	20 → 22
Thu, Dec 04 2025, 7:01pm	Estimate updated	E1-3 Test cases	8 → 7	22 → 21
Thu, Dec 04 2025, 7:10pm	Work item completed	E1-36 Pipeline	7 → 10	21
Thu, Dec 04 2025, 7:25pm	Work item completed	E1-42 Create HTML for front end user	10 → 16	21
Thu, Dec 04 2025, 7:59pm	Work item completed	E1-41 Log in and front end user HTML integration	16 → 21	21
Thu, Dec 04 2025, 8:00pm	Work item re-opened	E1-41 Log in and front end user HTML integration	21 → 16	21
Thu, Dec 04 2025, 8:00pm	Work item re-opened	E1-36 Pipeline	16 → 13	21
Thu, Dec 04 2025, 8:00pm	Work item re-opened	E1-42 Create HTML for front end user	13 → 7	21
Thu, Dec 04 2025, 8:00pm	Work item completed	E1-42 Create HTML for front end user	7 → 13	21
Thu, Dec 04 2025, 8:00pm	Work item completed	E1-36 Pipeline	13 → 16	21
Thu, Dec 04 2025, 8:00pm	Work item completed	E1-41 Log in and front end user HTML integration	16 → 21	21

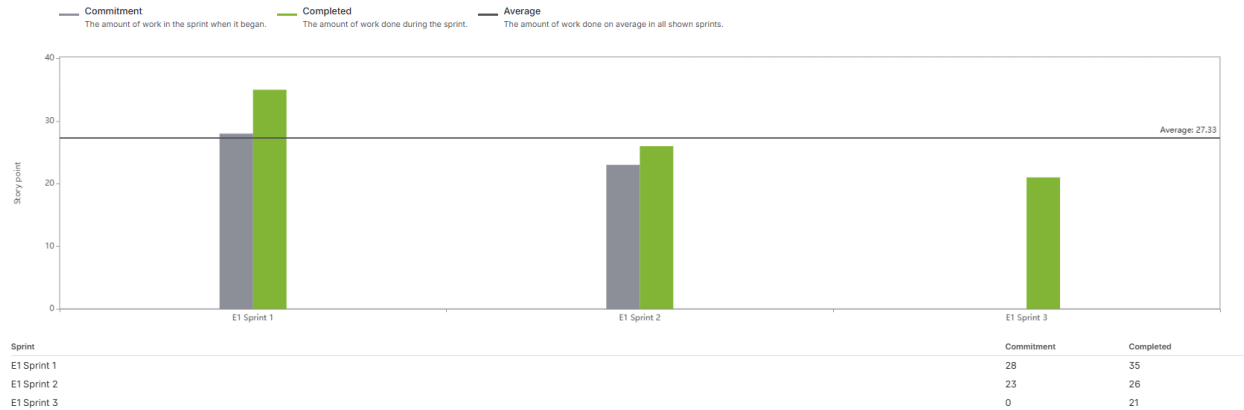

Sprint 3 retrospective review

Reflect on past work and identify opportunities for improvement by following the instructions for the [Retrospective Play](#).



Overview

Date	04 Dec 2025
Team	evsd-1
Participants	Edita Buneviciene, Dariusz Olczak, Patrick Strand, Edward Tracey



Retrospective

Start doing	Stop doing	Keep doing
Update the Team if any delayed tasks to prevent blockers	Completing a task without documenting details	Regular communication to clarify objectives.
Document each task with a simple cheat sheet so other Team members can understand changes that may relate to other tasks	Modifying the task description or changing direction of the task.	Keep meetings short and concise. Keep technical or fine detailed discussions for separate meeting.

Clear out unused files or redundant code from the code base.	Sub tasks should only be related to the work item. It's OK to have a work item with just one sub task.	Testing the application regularly to highlight issues/bugs
When smaller tasks turn out to be more work, split into new sub task or assign multiple Team members.	Task that sit for long periods should be revised to confirm if they are actually needed/viable.	Keep Promoting a good team spirit and working together to accomplish hard/large tasks.


Pro tip: You can also run a retro on a Confluence whiteboard by typing /retro

✓ Action items


- Revise your task details and screen shots in the final report to ensure they are correctly documented.
- Remove any unused code or files before we cut the release for the final application.
- Check the final report for any errors.
- Update the Team if any task objectives change.

DevOps

Customizable Tool chain

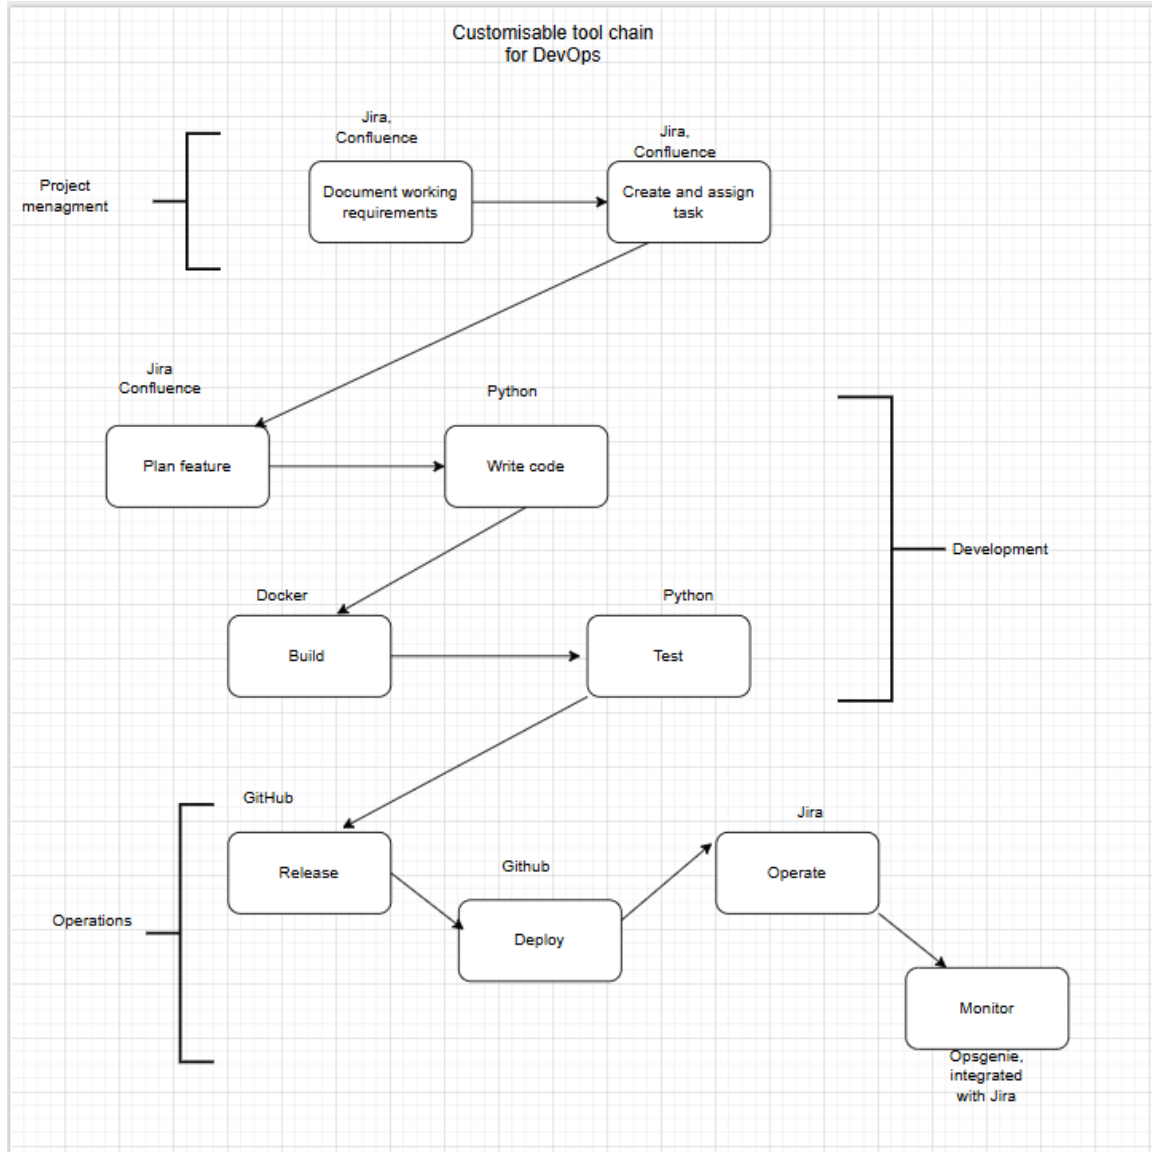

Test case for checking if dataset exists and loading, and HTML exists and loads.



Pipeline yml :

```

name: CI/CD Pipeline

on:
  push:
    branches:
      - main
  pull_request:
    branches:
      - main

jobs:
  # Build & Test
  build_and_test:
    runs-on: ubuntu-latest

    steps:
      - name: Checkout Repository
        uses: actions/checkout@v4

      - name: Set up Python
        uses: actions/setup-python@v5
        with:
          python-version: "3.10"

      - name: Add project root to PYTHONPATH
        run: echo "PYTHONPATH=$PYTHONPATH:$(pwd)" >> $GITHUB_ENV

      - name: Install Dependencies
        run: |
          pip install -r requirements.txt
          pip install pytest pytest-cov beautifulsoup4 lxml

      - name: Run Tests
        run: |
          python -m pip install --upgrade pip
          pip install -r requirements.txt
          pip install pytest

      - name: Run Tests
        run: |
          pytest --maxfail=1 --disable-warnings -q

      - name: Upload test results
        uses: actions/upload-artifact@v4
        with:
          name: test-results
          path: ./tests

```

Screenshots of CI/CD

7 workflow runs			Event ▾	Status ▾	Branch ▾	Actor ▾
✓	Production version CI/CD Pipeline #13: Commit 1c535c3 pushed by DariuszOlczak	main	Dec 1, 3:36 AM GMT 🕒 1m 41s	...		
✓	Fixed typo in .yml CI/CD Pipeline #12: Commit d58ac51 pushed by DariuszOlczak	main	Dec 1, 3:30 AM GMT 🕒 1m 42s	...		
✓	Added triggering pipeline on pull CI/CD Pipeline #10: Commit f25b571 pushed by DariuszOlczak	main	Nov 30, 4:13 AM GMT 🕒 49s	...		
✓	Feature/front back integration CI/CD Pipeline #9: Pull request #6 synchronize by DariuszOlczak	feature/front-back-integrat...	Nov 30, 3:54 AM GMT 🕒 48s	...		
✓	Added filepath to pipeline so main will be found by test_main CI/CD Pipeline #8: Commit 1ee7066 pushed by DariuszOlczak	feature/front-back-integrat...	Nov 30, 3:54 AM GMT 🕒 49s	...		
✓	Merge pull request #5 from EditaBuneviciene/feature/LLM-integration Project CI/CD Pipeline with Artifacts #7: Commit c13b3e2 pushed by DariuszOlczak	main	Nov 25, 5:40 PM GMT 🕒 2m 32s	...		
✓	Feature/llm integration Project CI/CD Pipeline with Artifacts #6: Pull request #5 synchronize by DariuszOlczak	feature/LLM-integration	Nov 25, 5:31 PM GMT 🕒 2m 34s	...		

Artifact generated by DEvOps

Triggered via push 2 days ago

DariuszOlczak pushed 1c535c3 main

Status

Success

Total duration

1m 41s

Artifacts

3

github_pipeline.yml

on: push

✓ build

40s

→

✓ test

39s

→

✓ production

10s

Artifacts

Produced during runtime

Name	Size	Digest		
build-artifact	2.89 MB	sha256:53cd36a3450410b4fa3aa852204ff80ff70481ad03b2770aaeb98091eee999...		
production-artifact	2.95 MB	sha256:4a1e6440f123a5f68b7ee833b410b15c7604a21f7ff8044d66f5945e0284aa...		
test-artifact	2.77 KB	sha256:f71978e14d2e334b830ef7159b5b75980f80c9821495f3a85cd1b701a15b48...		

GitHub Pipeline

Actions

New workflow

All workflows

Project CI/CD Pipeline with Artifacts

Management

Caches

Attestations

Runners

Usage metrics

Performance metrics

All workflows

Showing runs from all workflows

2 workflow runs

Event Status Branch Actor

Merge pull request #5 from Editabuneviciene/feature/LLM-integration
Project CI/CD Pipeline with Artifacts #7: Commit `c13b3e2` pushed by [DariuszOlczak](#)
main
1 hour ago
5m 7s

Feature/llm integration
Project CI/CD Pipeline with Artifacts #6: Pull request #5 synchronize by [DariuszOlczak](#)
feature/LLM-integration
Today at 5:31 PM
2m 34s

Project CI/CD Pipeline with Artifacts

Merge pull request #5 from Editabuneviciene/feature/LLM-integration #7

Cancel workflow Latest #2

Summary

Jobs

test

Run details

Usage

Workflow file

Re-run triggered now

DariuszOlczak `c13b3e2` main

Status Queued

Total duration

Artifacts

ci.yml
on: push

test build package

Project CI/CD Pipeline with Artifacts

Merge pull request #5 from Editabuneviciene/feature/LLM-integration #7

Cancel workflow Latest #2

Summary

Jobs

test

build

package

Run details

Usage

Workflow file

Re-run triggered 1 minute ago

DariuszOlczak `c13b3e2` main

Status In progress

Total duration

Artifacts 1

ci.yml
on: push

test 56s build 6s package 6s

Summary

Jobs

test

build

package

Run details

Usage

Workflow file

build
Started 34s ago

Search logs

Set up job 2s

Checkout code 4s

Set up Docker Buildx 5s

Build production Docker image 22s

Save Docker Image as Artifact

Upload Docker Image Artifact

Test production image

Post Set up Docker Buildx

Post Checkout code

← Project CI/CD Pipeline with Artifacts

✓ Merge pull request #5 from EditaBuneviciene/feature/LLM-integration #7

Re-run all jobs Latest #2 ...

Summary

Jobs

- test
- ✓ build
- package

Run details

Usage

Workflow file

build
succeeded now in 1m 24s

Search logs

- Set up job 2s
- Checkout code 4s
- Set up Docker Buildx 5s
- Build production Docker image 46s
- Save Docker Image as Artifact 5s
- Upload Docker Image Artifact 17s
- Test production image 2s
- Post Set up Docker Buildx 8s
- Post Checkout code 8s
- Complete job 8s

← Project CI/CD Pipeline with Artifacts

✓ Merge pull request #5 from EditaBuneviciene/feature/LLM-integration #7

Re-run all jobs Latest #2 ...

Summary

Jobs

- test
- ✓ build
- package

Run details

Usage

Workflow file

Re-run triggered 3 minutes ago Status: Success Total duration: 2m 32s Artifacts: 3

ci.yml
on: push

test 5s → build 1m 24s → package 7s

Artifacts
Produced during runtime

Name	Size	Digest
application-package	11.1 KB	sha256:3da19b3ff1e1795151c9b0eac362bef3bfb0b6842cc8830806da3fe70894...
production-docker-image	178 MB	sha256:b08ea0b6cc784a4a2e9ed549fc281a0e158ed52854428363e4f9772852...
test-results	2.47 KB	sha256:c9c385b7eb72f699ad30e1ae3c973fd284feee60b31f131da06291ec84...

```
PS C:\Users\olcza\PycharmProjects\AgileProject> git add .
PS C:\Users\olcza\PycharmProjects\AgileProject> git commit -m "Further changes in yml to improve creating artifacts"
[feature/LLM-integration 3f27ea5] Further changes in yml to improve creating artifacts
1 file changed, 2 insertions(+), 5 deletions(-)
PS C:\Users\olcza\PycharmProjects\AgileProject> git branch
* feature/LLM-integration
  feature/filter-columns
  main
PS C:\Users\olcza\PycharmProjects\AgileProject> git push origin feature/LLM-integration
Enumerating objects: 9, done.
Counting objects: 100% (9/9), done.
Delta compression using up to 12 threads
Compressing objects: 100% (3/3), done.
Writing objects: 100% (5/5), 446 bytes | 446.00 KiB/s, done.
Total 5 (delta 2), reused 0 (delta 0), pack-reused 0 (from 0)
remote: Resolving deltas: 100% (2/2), completed with 2 local objects.
To https://github.com/EditaBuneviciene/AgileProject.git
  7a5da7b..3f27ea5 feature/LLM-integration -> feature/LLM-integration
PS C:\Users\olcza\PycharmProjects\AgileProject> git fetch origin
remote: Enumerating objects: 8, done.
remote: Counting objects: 100% (8/8), done.
remote: Compressing objects: 100% (6/6), done.
remote: Total 8 (delta 1), reused 0 (delta 0), pack-reused 0 (from 0)
Unpacking objects: 100% (8/8), 4.06 KiB | 62.00 KiB/s, done.
From https://github.com/EditaBuneviciene/AgileProject
  0e63ad0..c13b3e2 main -> origin/main
PS C:\Users\olcza\PycharmProjects\AgileProject> git checkout feature/LLM-integration
Already on 'feature/LLM-integration'
Your branch is up to date with 'origin/feature/LLM-integration'.
PS C:\Users\olcza\PycharmProjects\AgileProject> git merge origin/main
Updating 3f27ea5..c13b3e2
Fast-forward
 sprint1/InterimReport/report.doc | 3784 ++++++-----
 sprint2/Report2.docx             | 81n 0 -> 8892500 bytes
```

```

PS C:\Users\olcza\PycharmProjects\AgileProject> git merge origin/main
Updating 3f27ea5..c13b3e2
Fast-forward
 sprint1/InterimReport/report.doc | 3784 ++++++-----
 sprint2/Report2.docx | Bin 0 -> 8892500 bytes
 sprint2/edita_code/e_main.py | 48 +
 sprint2/edita_code/mortality_rate.py | 67 +
 web/dummy_data.csv | 101 +
 web/edwardtracey@gmail.com.txt | 4 +
 web/forgot_password.html | 91 +
 web/home.html | 397 +
 web/local_server_setup_instructions.txt | 23 +
 web/login.html | 124 +
 web/reset_link_sent.html | 64 +
 web/signup.html | 113 +
12 files changed, 3614 insertions(+), 1202 deletions(-)
create mode 100644 sprint2/Report2.docx
create mode 100644 sprint2/edita_code/e_main.py
create mode 100644 sprint2/edita_code/mortality_rate.py
create mode 100644 web/dummy_data.csv
create mode 100644 web/edwardtracey@gmail.com.txt
create mode 100644 web/forgot_password.html
create mode 100644 web/home.html
create mode 100644 web/local_server_setup_instructions.txt
create mode 100644 web/login.html
create mode 100644 web/reset_link_sent.html
create mode 100644 web/signup.html

```

```

PS C:\Users\olcza\PycharmProjects\AgileProject> git checkout main
Switched to branch 'main'
PS C:\Users\olcza\PycharmProjects\AgileProject> git pull origin
You asked to pull from the remote 'origin', but did not specify
a branch. Because this is not the default configured remote
for your current branch, you must specify a branch on the command line.
PS C:\Users\olcza\PycharmProjects\AgileProject> git pull origin main
From https://github.com/EditaBuneviciene/AgileProject
 * branch      main      -> FETCH_HEAD

```

```


Updating 2710dba..c13b3e2
Fast-forward
 .github/workflows/ci.yml | 81 +
 Data_Cleaned.csv | 19516 +-----
 Dockerfile | 39 +
 main.py | 1122 ++
 requirements.txt | 4 +
 sprint1/InterimReport/report.doc | 3784 +---
 sprint2/Report2.docx | Bin 0 -> 8892500 bytes
 sprint2/edita_code/e_main.py | 48 +
 sprint2/edita_code/mortality_rate.py | 67 +
 sprint3/Data.csv | 23871 ++++++
 sprint3/README.md | 15 +
 sprint3/main.py | 1122 ++
 sprint3/requirements.txt | 13 +
 sprint3/test_main.py | 165 +
 sprint3/web_pages/creat_account.html | 113 +
 sprint3/web_pages/forgot_password.html | 84 +
 test_main.py | 165 +
 web/dummy_data.csv | 101 +
 web/edwardtracey@gmail.com.txt | 4 +
 web/forgot_password.html | 91 +
 web/home.html | 397 +
 web/local_server_setup_instructions.txt | 23 +
 web/login.html | 124 +
 web/reset_link_sent.html | 64 +
 web/signup.html | 113 +
25 files changed, 30411 insertions(+), 20715 deletions(-)
create mode 100644 .github/workflows/ci.yml
create mode 100644 Dockerfile
create mode 100644 main.py
create mode 100644 sprint2/Report2.docx

```

```


25 files changed, 30411 insertions(+), 20715 deletions(-)
create mode 100644 .github/workflows/ci.yml
create mode 100644 Dockerfile
create mode 100644 main.py
create mode 100644 sprint2/Report2.docx
create mode 100644 sprint2/edita_code/e_main.py
create mode 100644 sprint2/edita_code/mortality_rate.py
create mode 100644 sprint3/Data.csv
create mode 100644 sprint3/README.md
create mode 100644 sprint3/main.py
create mode 100644 sprint3/requirements.txt
create mode 100644 sprint3/test_main.py
create mode 100644 sprint3/web_pages/creat_account.html
create mode 100644 sprint3/web_pages/forgot_password.html
create mode 100644 test_main.py
create mode 100644 web/dummy_data.csv
create mode 100644 web/edwardtracey@gmail.com.txt
create mode 100644 web/forgot_password.html
create mode 100644 web/home.html
create mode 100644 web/local_server_setup_instructions.txt
create mode 100644 web/login.html
create mode 100644 web/reset_link_sent.html
create mode 100644 web/signup.html
PS C:\Users\olcza\PycharmProjects\AgileProject>

```

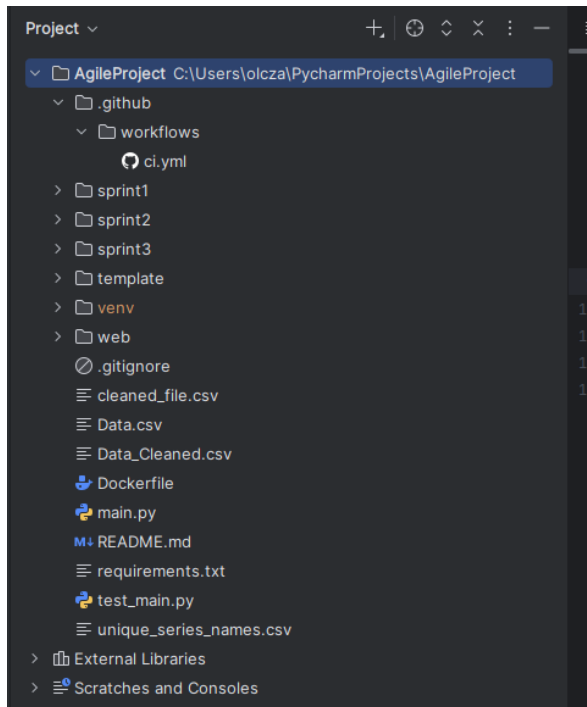

Network graph


Timeline of the most recent commits to this repository and its network ordered by most recently pushed to.

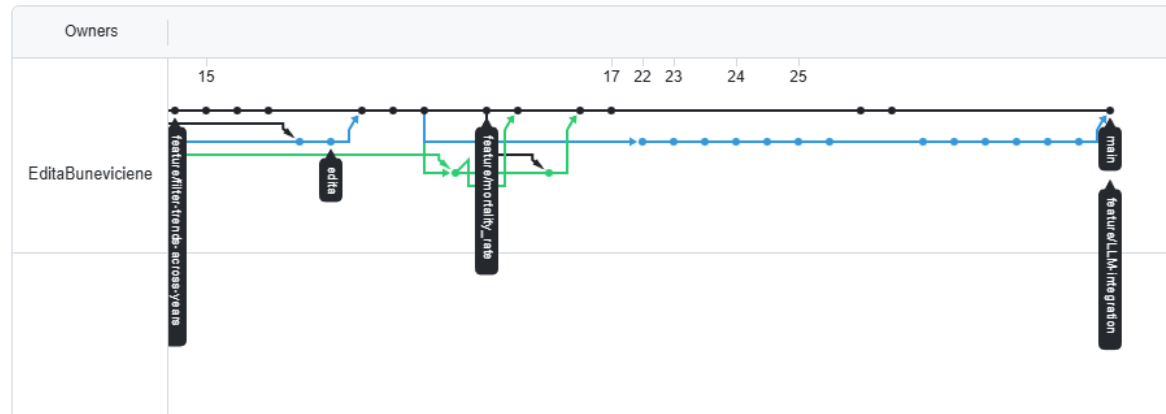

```
PS C:\Users\olcza\PycharmProjects\AgileProject> git status
On branch main
nothing to commit, working tree clean
PS C:\Users\olcza\PycharmProjects\AgileProject> git log --oneline -5
c13b3e2 (HEAD -> main, origin/main, origin/feature/LLM-integration, feature/LLM-integration) Merge pull request #5 from EditaBuneviciene/feature/LLM-integration
3f27ea5 Further changes in yml to improve creating artifacts
7a5da7b Added package job to create application package.Solving 1 out of 3 artifacts generated
f992c09 corrected docker to build image in pipeline
68a15e9 Moved main.py test_main.py and Dockerfile to main as Issues with Docker in GitHub pipeline persisted
PS C:\Users\olcza\PycharmProjects\AgileProject> git branch -a
feature/LLM-integration
feature/filter-columns
* main
remotes/origin/dariusz
remotes/origin/edit-user-details
remotes/origin/edita
remotes/origin/feature-connect-user_login-pages
remotes/origin/feature/LLM-integration
remotes/origin/feature/filter-trends-across-years
remotes/origin/feature/mortality_rate
remotes/origin/main
remotes/origin/paddystrand-ops-patch-1
```

Docker


Project directory with Dockerfile necessary to build image of application

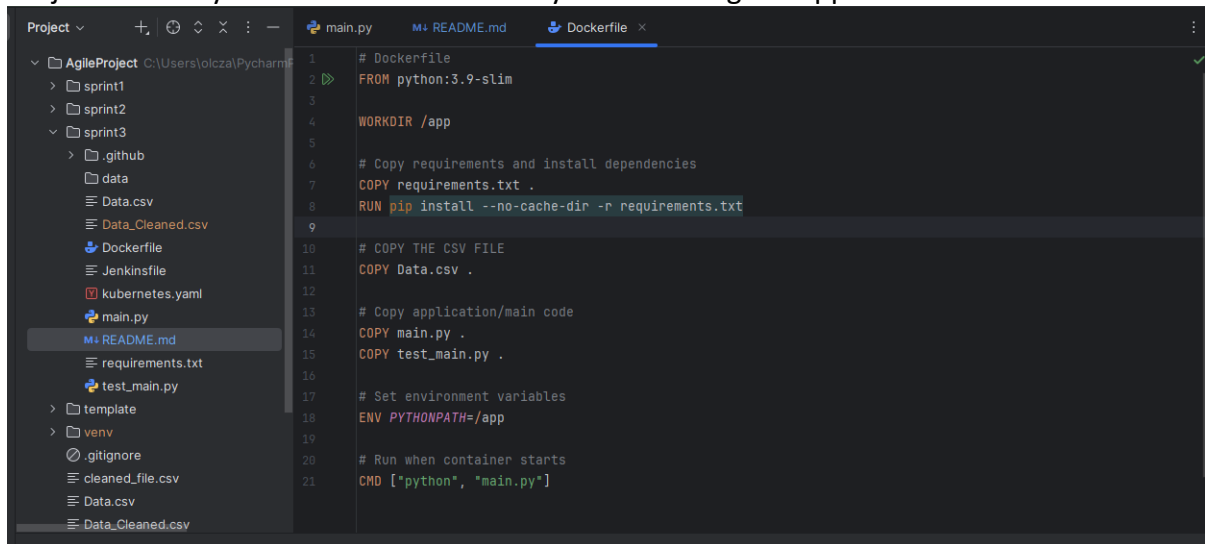

```

1 # Dockerfile
2 FROM python:3.9-slim
3
4 WORKDIR /app
5
6 # Copy requirements and install dependencies
7 COPY requirements.txt .
8 RUN pip install --no-cache-dir -r requirements.txt
9
10 # COPY THE CSV FILE
11 COPY Data.csv .
12
13 # Copy application/main code
14 COPY main.py .
15 COPY test_main.py .
16
17 # Set environment variables
18 ENV PYTHONPATH=/app
19
20 # Run when container starts
21 CMD ["python", "main.py"]
  
```

GIT CI Pipeline

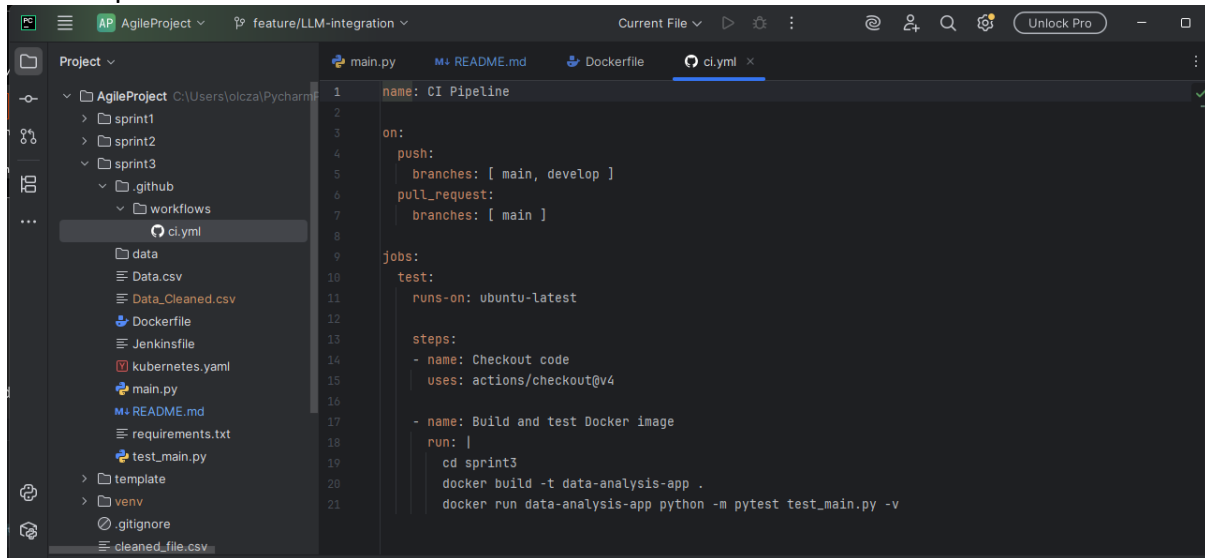

```

1 name: CI Pipeline
2
3 on:
4   push:
5     branches: [ main, develop ]
6   pull_request:
7     branches: [ main ]
8
9 jobs:
10  test:
11    runs-on: ubuntu-latest
12
13    steps:
14      - name: Checkout code
15        uses: actions/checkout@v4
16
17      - name: Build and test Docker image
18        run: |
19          cd sprint3
20          docker build -t data-analysis-app .
21          docker run data-analysis-app python -m pytest test_main.py -v
  
```

Checking if branch is up to date. Checking for docker and building image of the application.
docker build -t data-analysis-app .

```

PS C:\Users\olcza\PycharmProjects\AgileProject\sprint3> git status
On branch feature/LLM-integration
Your branch is up to date with 'origin/feature/LLM-integration'.

nothing to commit, working tree clean
PS C:\Users\olcza\PycharmProjects\AgileProject\sprint3> git log --oneline -5
a4cffe2 (HEAD -> feature/LLM-integration, origin/feature/LLM-integration) Added readme and updated dockerfile to save Data.csv
aa95e37 Added README.md for ease of testing
67b15ba Simple tests, github pipeline and Docker added. Need to work on Kubernetes
ce1ce8e Added LLM Engine
2710dba (main) nothing to be seen
PS C:\Users\olcza\PycharmProjects\AgileProject\sprint3> git remote
origin
PS C:\Users\olcza\PycharmProjects\AgileProject\sprint3> git remote -v
origin https://github.com/EditaBuneviciene/AgileProject.git (fetch)
origin https://github.com/EditaBuneviciene/AgileProject.git (push)
PS C:\Users\olcza\PycharmProjects\AgileProject\sprint3> docker --version
Docker version 29.0.1, build eedd969
PS C:\Users\olcza\PycharmProjects\AgileProject\sprint3> docker ps
CONTAINER ID   IMAGE      COMMAND                  CREATED        STATUS        PORTS        NAMES
PS C:\Users\olcza\PycharmProjects\AgileProject\sprint3> docker build -t data-analysis-app .
[+] Building 1.8s (13/13) FINISHED                                docker:desktop-linux
=> [internal] load build definition from Dockerfile                                0.0s
=> => transferring dockerfile: 433B                                              0.0s
=> [internal] load metadata for docker.io/library/python:3.9-slim                1.3s
=> [auth] library/python:pull token for registry-1.docker.io                    0.0s
=> [internal] load .dockerignore                                                  0.0s
=> => transferring context: 2B                                                    0.0s
=> [internal] load build context                                                  0.1s
=> => transferring context: 128B                                                  0.0s
=> [1/7] FROM docker.io/library/python:3.9-slim@sha256:2d97f6910b16bd338d3060f261f53f144965f755599aab1acd1e13cf1731b1b 0.1s
=> => resolve docker.io/library/python:3.9-slim@sha256:2d97f6910b16bd338d3060f261f53f144965f755599aab1acd1e13cf1731b1b 0.1s
=> CACHED [2/7] WORKDIR /app                                                      0.0s
=> CACHED [3/7] COPY requirements.txt .                                            0.0s
=> CACHED [4/7] RUN pip install --no-cache-dir -r requirements.txt                0.0s

```

Running the application with command

docker run -it data-analysis-app

```

=> CACHED [4/7] RUN pip install --no-cache-dir -r requirements.txt                0.0s
=> CACHED [5/7] COPY Data.csv .                                                    0.0s
=> CACHED [6/7] COPY main.py .                                                    0.0s
=> CACHED [7/7] COPY test_main.py .                                              0.0s
=> exporting to image                                                            0.2s
=> => exporting layers                                                            0.0s
=> => exporting manifest sha256:3bee65cd451b054370379d3f7e092e61fd452a18d59932949128c1b36b256889 0.0s
=> => exporting config sha256:5dcf4948dd4f6e8824b7a6e62adfe41199b827bbd9c683a05cd54fd244ad72ac 0.0s
=> => exporting attestation manifest sha256:20ccc9c477f51c3cd47f75dde4908051d6d4561d2b9728624a02e83daddc015b 0.0s
=> => exporting manifest list sha256:3dd0c858767d2b05a634e799a4692bd75d71fd543713d8b61409275a66933547 0.0s
=> => naming to docker.io/library/data-analysis-app:latest                       0.0s
=> => unpacking to docker.io/library/data-analysis-app:latest                   0.0s

View build details: docker-desktop://dashboard/build/desktop-linux/desktop-linux/3r3kb2xwdb11latn6ut6yo02p
PS C:\Users\olcza\PycharmProjects\AgileProject\sprint3> docker images


```

IMAGE	ID	DISK USAGE	CONTENT SIZE	EXTRA
data-analysis-app:latest	3dd0c858767d	562MB	126MB	
mcp/playwright@sha256:fd43bc74a3ad644c4dc935a45a3f311a3a93fb4d0ef9a752427601dee01bc217	fd43bc74a3ad	1.67GB	415MB	

```

PS C:\Users\olcza\PycharmProjects\AgileProject\sprint3> docker run data-analysis-app
Loading dataset...
No cleaned data found
Starting cleaning process...
Analyzing missing values...
Found 4358 rows with more than 70.0% missing data
Cleaning dataset...
Cleaned dataset saved as 'Data_Cleaned.csv'
Dataset found and cleaned
Dataset loaded successfully: 110 series, 217 countries, 24 years
Dataset: 110 series, 217 countries, 24 years

=====
MANUAL SELECTION INTERFACE
=====

```

Application:

```
=====
MANUAL SELECTION INTERFACE
=====
```

```
STEP 1: Select a Series
```

- ```

1. Adolescent fertility rate (births per 1,000 women ages 15-19)
2. Adults (ages 15+) and children (ages 0-14) newly infected with HIV
3. Adults (ages 15-49) newly infected with HIV
4. Age dependency ratio (% of working-age population)
5. Age dependency ratio, old (% of working-age population)
6. Age dependency ratio, young (% of working-age population)
7. Antiretroviral therapy coverage (% of people living with HIV)
8. Birth rate, crude (per 1,000 people)
9. Births attended by skilled health staff (% of total)
10. Children (0-14) living with HIV
11. Children (ages 0-14) newly infected with HIV
12. Current health expenditure (% of GDP)
13. Current health expenditure per capita (current US$)
14. Current health expenditure per capita, PPP (current international $)
15. Death rate, crude (per 1,000 people)
16. Domestic general government health expenditure (% of current health expenditure)
17. Domestic general government health expenditure (% of GDP)
18. Domestic general government health expenditure (% of general government expenditure)
19. Domestic general government health expenditure per capita (current US$)
20. Domestic general government health expenditure per capita, PPP (current international $)
... and more
```

```
Enter series number (1-110) or name: 1
```

```
Selected series: Adolescent fertility rate (births per 1,000 women ages 15-19)
```

```
Enter series number (1-110) or name: 1
Selected series: Adolescent fertility rate (births per 1,000 women ages 15-19)
```

```
STEP 2: Select Countries (found 217 countries)
```

- ```
-----
1. Afghanistan
2. Albania
3. Algeria
4. American Samoa
5. Andorra
6. Angola
7. Antigua and Barbuda
8. Argentina
9. Armenia
10. Aruba
11. Australia
12. Austria
13. Azerbaijan
14. Bahamas, The
15. Bahrain
... and 202 more
```

```
Enter country numbers (comma-separated) or names (comma-separated): 1
```

```
Selected countries: Afghanistan
```

```
STEP 3: Select Years (available: 24 years)
```

```
-----
Available years: 2000, 2001, 2002, 2003, 2004, 2005, 2006, 2007, 2008, 2009 ...
```

```
Enter years to compare (comma-separated, 'all', or range like '2000-2010'): all
```

```
Selected years: 24 years
```

```

STEP 3: Select Years (available: 24 years)
-----
Available years: 2000, 2001, 2002, 2003, 2004, 2005, 2006, 2007, 2008, 2009 ...

Enter years to compare (comma-separated, 'all', or range like '2000-2010'): all
Selected years: 24 years

STEP 4: Select Chart Type
-----
Available chart types:
1. Line Chart - Trend comparison over time
2. Bar Chart - Side-by-side country comparison
3. Heatmap - Value distribution across years

Enter chart type number (1-3): 1
Selected chart: Line Chart

=====
GENERATING VISUALIZATION...
Series: Adolescent fertility rate (births per 1,000 women ages 15-19)
Countries: Afghanistan
Years: 24 selected
Chart Type: line
=====

=====
AI ANALYSIS OPTIONS
=====
Series: Adolescent fertility rate (births per 1,000 women ages 15-19)
Countries: Afghanistan
Years: 24 selected
-----

Select analysis type:
1. Simple Insight Report (Fast, basic analysis)
2. Simple Trend Prediction (Fast, basic forecast)
3. View Chart Only (no additional analysis)

Enter choice (1-3): 1

=====
AI INSIGHT REPORT
=====

```

Running tests with command

`docker run data-analysis-app python -m pytest test_main.py -v`

```

=====
AI INSIGHT REPORT
=====

Analyzing Adolescent fertility rate (births per 1,000 women ages 15-19)...
Error getting models: Connection error.
No LLM models available.

=====
Report saved as: insight_report_20251124_160616.txt

Would you like to analyze another series? (y/n): n
Goodbye!
PS C:\Users\olcza\PycharmProjects\AgileProject\sprint3> docker run data-analysis-app python -m pytest test_main.py -v
===== test session starts =====
platform linux -- Python 3.9.25, pytest-8.4.2, pluggy-1.6.0 -- /usr/local/bin/python
cachedir: .pytest_cache
rootdir: /app
plugins: anyio-4.11.0
collecting ... collected 6 items

test_main.py::TestDataAnalysis::test_missing_values_detection PASSED [ 16%]
test_main.py::TestDataAnalysis::test_clean_dataset_removes_rows PASSED [ 33%]
test_main.py::TestDataAnalysis::test_mathematical_prediction_basic PASSED [ 50%]
test_main.py::TestDataAnalysis::test_manual_predictions_creation PASSED [ 66%]
test_main.py::TestDataAnalysis::test_parse_alternative_format PASSED [ 83%]
test_main.py::TestDataAnalysis::test_llm_insight_report PASSED [100%]

===== 6 passed in 1.53s =====
PS C:\Users\olcza\PycharmProjects\AgileProject\sprint3>

```

Conclusions and future work

Problem Statement Summary

Large global health datasets from 2000 to the present contain valuable information about mortality, disease trends, life expectancy, and access to healthcare, but the data is often raw, messy, and difficult for students or educators to interpret. Existing tools like spreadsheets make it hard to detect patterns, spot anomalies, or ask intelligent questions about the data. The challenge is to transform this complex, unprocessed information into an interactive system that automatically imports, cleans, visualizes, and analyzes global health data, so users can easily explore trends and gain meaningful insights.

Project Management Approach

In this project we followed Agile principles and Scrum approach. Agile process follows flexibility to adapt requirements and changes. In this project we learned a lot not only about agile and scrum, but it involved new technical skills to complete project. Instead of planning the project upfront, we build it bit by bit, dividing in 3 sprints. Agile helps team to respond quickly to changes. This approach was particularly beneficial given the team's developing technical skills and frequent need for adjustments.

Nearly everyone got a chance to do the different roles in this project as PO, scrum master and skills involving that role. We realized that Scrum stand-up meetings are inseparable part of Agile process and necessary for maintaining communication, addressing blockers, and ensuring steady progress toward our sprint goals.

Technical Approach

Overview of Objectives

To achieve the main objectives for the project, we broke the tasks into small simple objectives. This helped to identify tasks that would need more time or development resources, and gave the Team a good understanding of the workflow of the architecture of the application. The work load was roughly divided into the following sections.


- Database.
- Web Interface for users, accounts and sign-up.
- Data visualization for displaying graph plots.
- Data Prediction.
- Documentation.

The following is a more detailed description of the main sections of the workload.

DataBase

After choosing a suitable database, the next step was to clean it for processing. we set a threshold of 0.7 and if missing values in the row were higher then threshold, we removed it from dataset.

Once we had clean valid data and understood the information it contained we could then confidently test it manually by using Excel to plot a graph as shown below.

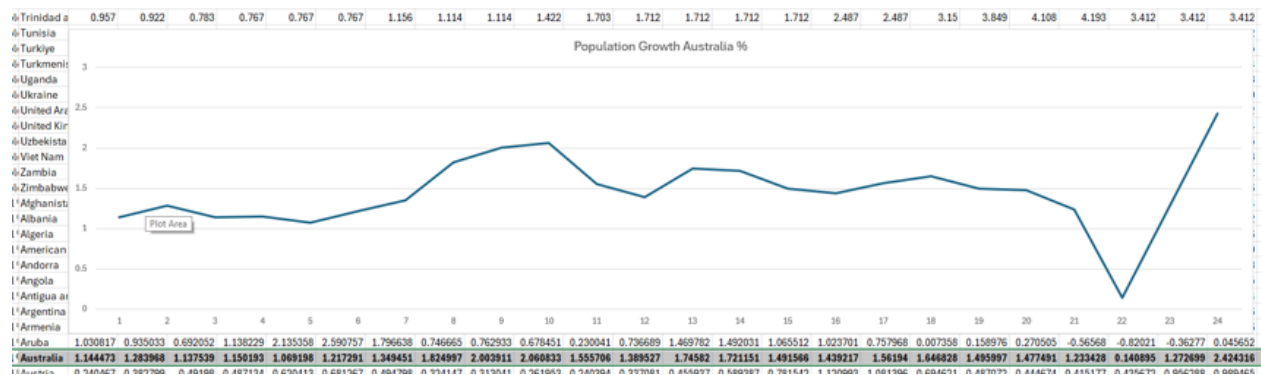

Web Interface

To access the application, a set of web pages were needed so a user could sign-up and log-in to the main page. Each page related to user login was created separately and then the on-click button functions were connected so the pages could be navigated. The pages were written in HTML and use CSS styling. JavaScript functions handle reading the login details and passwords.

evSD_Group1 Project

Login

Email Address

joe@email.com

Password


Enter your password

Login

[Forgot Password?](#)

Don't have an account? [Create Account](#)

During the development phase, the user would land on a test visualization page after a successful log-in. We used dummy data to create a set of curve values to display on a graph. A drop-down list gave the user a choice of the curve type. This prototype page gave us a indication of the tools we would need to import a file, select data, and plot a graph.

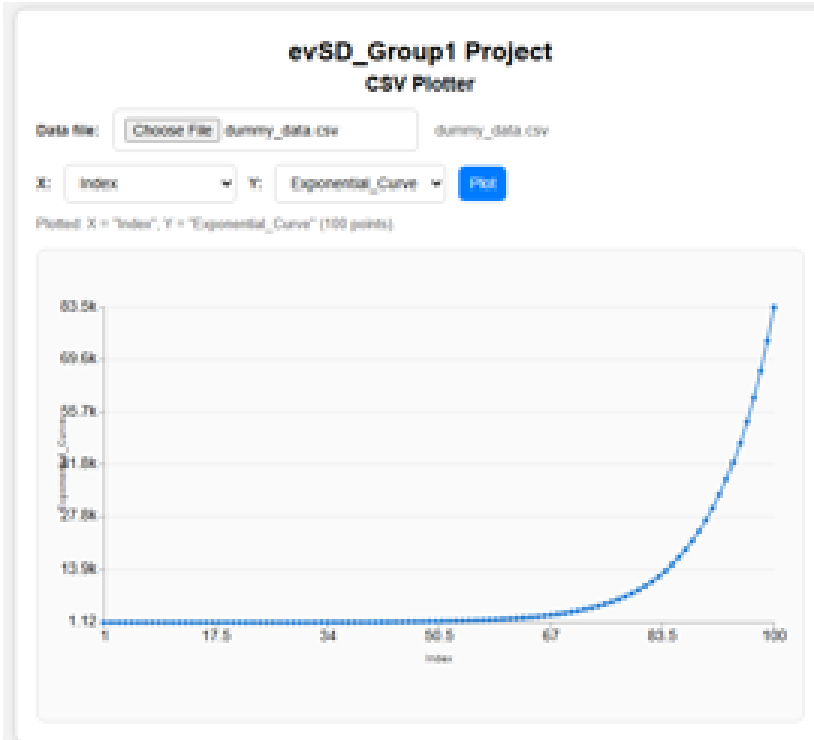

Data visualization

At a high level we used HTML, CSS and JS to create the main page. This page talks to our backend API (api_connection.py) to handle the following tasks.

- Upload and process CSV data
- Load dropdown options (series, countries, years)
- Settings for graph display options (line chart, bar graph, heatmap)

To accomplish this we used the **Flask** web framework.

Flask listens on localhost:5000, defines our /api routes and parses our JSON input/output requests. It also handles our file access for loading the .csv data.

Matplotlib was used to create the chart on our backend. The chart drawing is done by the backend. We used the `matplotlib.use('Agg')` feature to render the chart as a PNG image we can send back to the HTML page. The frontend then just shows the final image.

We use **CORS** to allow simple access to our frontend to interact with the API.



Data Prediction

Need to add details here on how the **Trend Prediction works.*


A feature to estimate/predict future values of the data set was added. This generates an analysis of the existing data to predict a 5, 10 or 15 year prediction.

Below is an output sample of the prediction feature.



The accuracy of the predictions can be studied by first displaying the full range of years 2000-2023.


We then display the 2000-2018 range and use the 5 year prediction to compare how close the prediction for the last 5 years matches the real data.

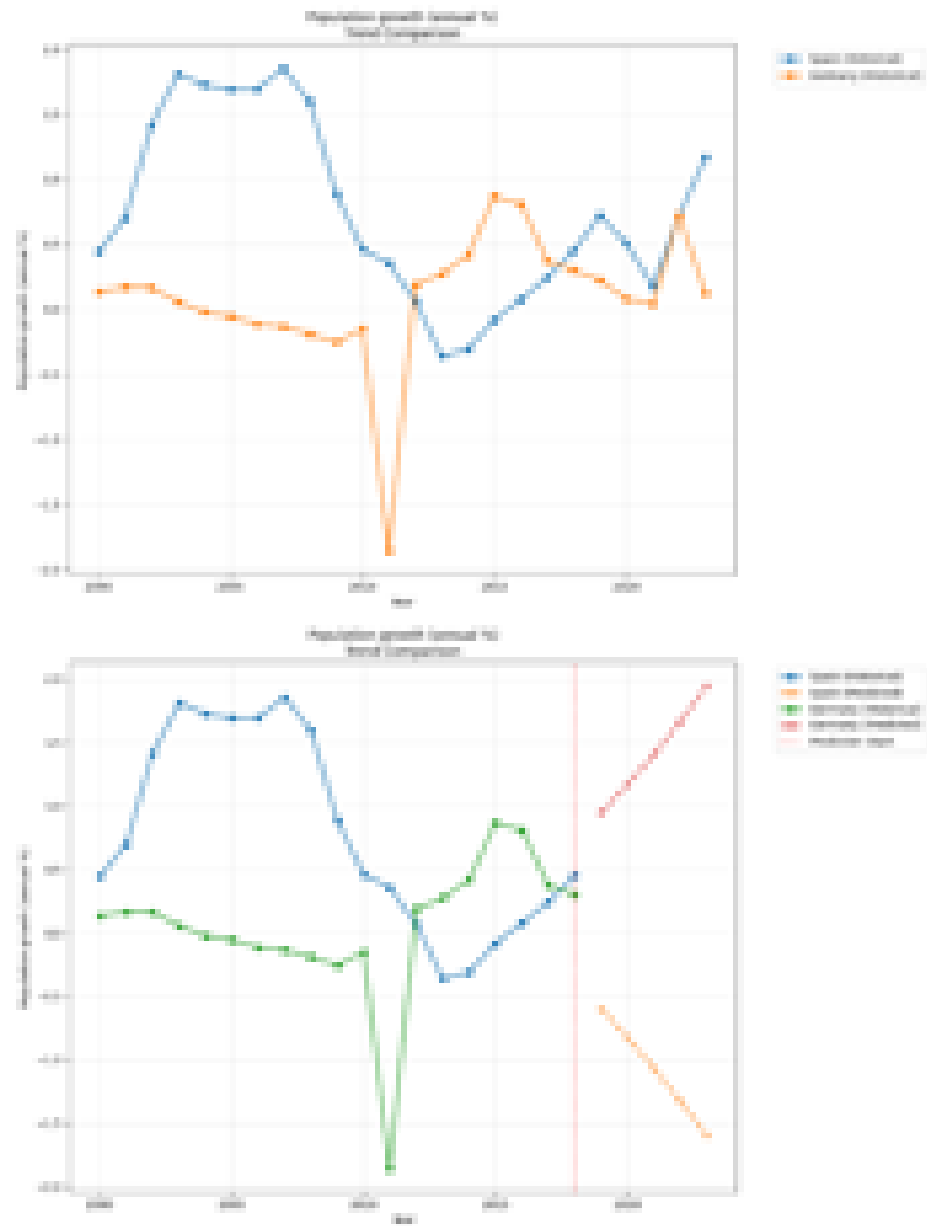

Population growth (annual %): 1980 - 2016: Spain, Germany

Documentation

A feature to generate a PDF version of the page was also added. This is similar to our chart generation method, but it renders the entire web page as an image which is then written to a PDF document and downloaded to the users local machine.

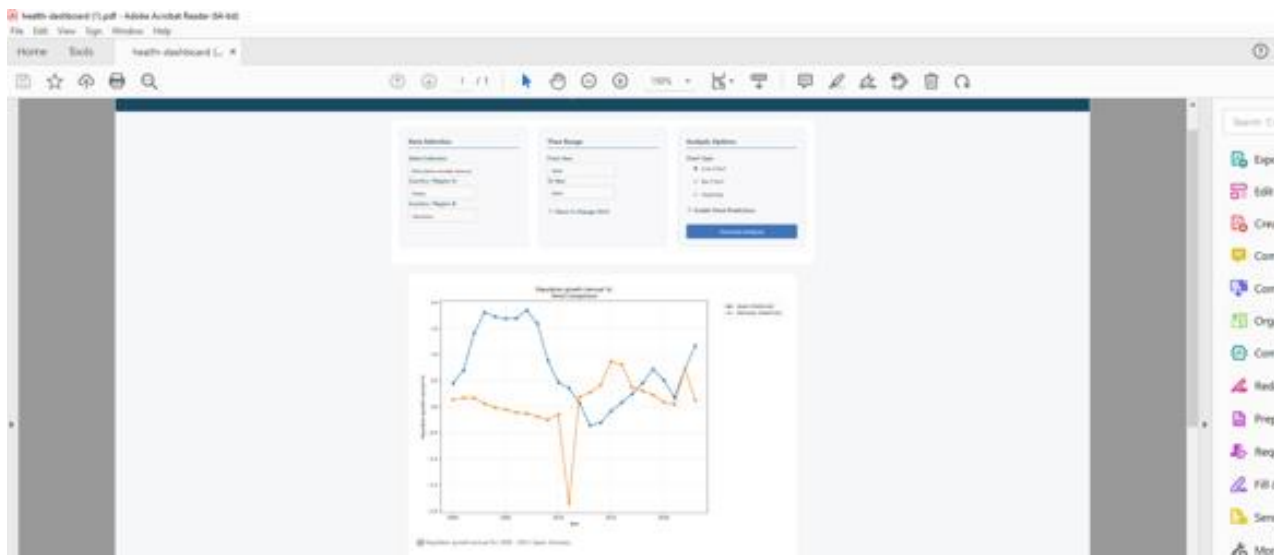

Findings of Approach

Analysis of results.

Using the population growth data as an example, we can see that the predictions generated by the model are inconsistent with the actual data. The model only uses the current trend to generate the future forecast. It would have no concept of predicting a large change in the values that could be caused by external factors such as high emigration or an economic crisis which could effect the population growth. A different model which could take into account these factors would greatly increase the complexity of the model.

For an analysis on a different set of data such as disease or infection rates, the model may produce a more accurate predication, but the effect of external factors may still be an issue. Although the current model may not be an accurate predictor, using the application to compare different models could help to chose a suitable model for a given dataset if we compare the predictions against the actual data. The downside to this is that we are using the last 5 years of data for validating the prediction, when the model may be more accurate if the data from the last 5 years was included in it's analysis.


Not sure how to get the over/under fitting values of the model. Dariusz?

Tool chain

We chose customizable tool chain for Devops. A DevOps toolchain is a collection of tools and technologies that support the entire software development and deployment lifecycle. It enables automation, continuous integration, continuous delivery, monitoring, and collaboration between development and operations teams. We tended to pick the tools we were familiar as GitHub for version control, for CI, pipeline, HTML for front-end development. Used Python and libraries for build and dependencies, Flask for enable smooth communication between the backend and the user interface.

Future Enhancements

When the plot is displayed on the chart it gives a good visualization of the data, but a description of the data would help greatly to explain some of the changes. For example, in the population growth from the graphs above, there was a massive dip in numbers for Germany in 2011. In 2012 the value increased sharply but still followed the trend from previous years. The data from 2011 almost looks like an outlier. When we research why this was the case, a simple google search provided the following...



If we were to get the user selection for the dropdown lists on the page, we could get the names of the headers in CSV file (*Germany, Spain*), get the data series title (*Annual Population Growth*), and also get the range of the years (*2002-2023*). We could take these strings and pass them into an LLM as a request: “Describe the **population growth** changes between **2002-2003** for **Spain** and **Germany**”. The generated feedback could provide a better insight into the data rather than relying on just a graph plot and it could explain perceived anomalies such as the population dip previously described. Naturally, the validity of the feedback would need to be verified but as a general description alongside the data plot, it may provide useful insights.
